

Flight Procedures Cover Page	Task Action: FLIGHT CHECK	Task Type: Textual DP	Estimated Chart Date: 02/23/2023	APWS Task ID: E20B5CE4D5CB42819BD17D93FF485E0B	APWS Project ID: D5FBCE881B694F228BE371EDFE2AF394
Procedure: POMPANO BEACH, FL A6		Enroute: NO	Specialist: Garrity, Michael		Agreement Number:
Airport ID: KPMP			Airport City: POMPANO BEACH		State: FL
Facility ID:	Facility Type:	Flight Inspection Remark Type: New FC Slot			
<p><b>Procedure Comments:</b>  ACTIVE DATA USED FOR KPMP AIRPORT AND RUNWAYS</p> <p>CANCELS !FDC 2/5749</p> <p>CONTACT: ALLAN WILL, TEAM 2 SUBTEAM-C MANAGER, 405.954.6103, OR MARLON ROBINSON, TEAM 2 MANAGER, 405.954.3636</p>					





## FL FLL FRSBE ONE (RNAV) DEPARTURE

5-5-2022 PRB Results: Returned for Rework

REQUESTED BY: AJV-A

PRB RESULTS: RETURN FOR REWORK

- IAW 8260.19, PARA 2-8-3F: THE SID CLIMB GRADIENT AND THE ODP CLIMB GRADIENT ARE NOT CONSISTENT. THE ICA IS THE SAME FOR THE SID AND THE ODP. THE SID NEWER EVALUATION HAS IDENTIFIED THE SAME CONTROLLING OBSTACLES RWY 10 BUT RWY 15 DIFFERENT BUT DIFFERENT MINS. 4/6/22 ODP PERIODIC REVIEW IDENTIFIED NEW CONTROLLING OBSTACLES FOR RWY 10 WHICH A NOTAM WAS ISSUED. WHICH ARE THE CORRECT MINS FOR RWY 10/15 AT KPMP?

Following NOTAM issued to reconcile PMP TO MINIMA with FLL FRSBE. We expect to reconcile PMP textual ODP on or about 11-03-2022

!FDC 2/4043 PMP ODP POMPARO BEACH AIRPARK, POMPARO BEACH, FL. TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES AMDT 5... TAKE-OFF MINIMUMS RWY 10: 300-1 1/4 OR STANDARD WITH A MINIMUM CLIMB OF 265 FT PER NM TO 280. TAKE-OFF MINIMUMS RWY 15: 400-1 3/8 OR STANDARD WITH A MINIMUM CLIMB OF 425 FT PER NM TO 470. ALL OTHER DATA REMAINS AS PUBLISHED



# TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



22251

## POMPANO BEACH, FL

### POMPANO BEACH AIRPARK (PMP)

#### TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 5 18SEP14 (14261) (FAA)

##### TAKEOFF MINIMUMS:

**Rwy 10**, 300-1¼ or std. w/ min. climb of 261' per NM to 300.

**Rwy 15**, 400-1¼ or std. w/ min. climb of 441' per NM to 500.

##### TAKEOFF OBSTACLE NOTES:

**Rwy 6**, trees beginning 101' from DER, 26' left and 232' right of centerline, up to 70' AGL/88' MSL.

**Rwy 10**, pole 154' from DER, 131' left of centerline, 9' AGL/18' MSL.

Trees, pole, and building beginning 427' from DER, 12' left and 343' right of centerline, up to 49' AGL/63' MSL.

Poles and buildings beginning 1264' from DER, 166' left and 286' right of centerline, up to 64' AGL/72' MSL.

Building 5670' from DER, 604' right of centerline, 186' AGL/190' MSL.

Buildings 1 NM from DER, 887' left of centerline, up to 201' AGL/210' MSL.

**Rwy 15**, building, trees, and poles beginning 502' from DER, 306' left and 434' right of centerline, 44' AGL/54' MSL.

Trees beginning 1229' from DER, 152' left and 190' right of centerline, up to 71' AGL/162' MSL.

Building 5994' from DER, 1491' left of centerline, 213' AGL/221' MSL.

Building 1.1 NM from DER, 1259' left of centerline, 300' AGL/310' MSL.

Building 1.7 NM from DER, 1385' right of centerline, 255' AGL/265' MSL.

**Rwy 24**, trees beginning 190' from DER, 304' right of centerline, up to 30' AGL/49' MSL.

Trees beginning 423' from DER, 3' left of centerline, up to 47' AGL/66' MSL.

Tanks, building, tree, and pole beginning 630' from DER, 23' right of centerline, 60' AGL/80' MSL.

Trees beginning 2179' from DER, 253' left of centerline, up to 91' AGL/110' MSL.

**Rwy 28**, trees beginning 358' from DER, 255' left of centerline, up to 25' AGL/44' MSL.

Poles, buildings, trees, and tank beginning 722' from DER, 33' left and 238' right of centerline, up to 45' AGL/64' MSL.

**Rwy 33**, buildings beginning 29' from DER, 398' left of centerline, 18' AGL/34' MSL.

Trees beginning 629' from DER, 518' left of centerline, up to 59' AGL/77' MSL.

Trees beginning 202' from DER, 548' right of centerline, up to 38' AGL/56' MSL.

OLD

## PONCE, PR

### MERCEDITA (PSE) (TJPS)

#### TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 6 15AUG19 (21280) (FAA)

##### TAKEOFF MINIMUMS:

**Rwy 12**, std. w/min. climb of 300' per NM to 5300 or 5100-3 for VCOA.

**Rwy 30**, 500-1¼ w/min. climb of 350' per NM to 1300 or std. w/min. climb of 808' per NM to 500 or 5100-3 for VCOA.

##### DEPARTURE PROCEDURE:

**Rwy 12**, climb heading 119° to 2500 then proceed on a heading between 304° CW to 248° from DER to avoid R-7105 and unmarked tethered balloon up to 15000 MSL.

**Rwy 30**, climbing left turn on a heading between 120° CW to 200° from DER. Do not proceed northbound (headings 316° CW 119°) until leaving 5000; do not proceed westbound (headings 200° CW 315°) until leaving 12000 to avoid R-7105 and unmarked tethered balloon up to 15000 MSL.

##### VCOA:

**All runways:** obtain ATC approval for VCOA when requesting IFR clearance. Climb in visual conditions to cross Mercedita airport at or above 5100 then climb heading 090° to SJU VORTAC R-239 to CLAYO INT/SJU 35 DME.

##### TAKEOFF OBSTACLE NOTES:

**Rwy 12**, trees beginning 126' from DER, 480' left of centerline, 5' AGL/31' MSL.

Poles beginning 126' from DER, 435' right of centerline, up to 68' AGL/87' MSL.

Trees beginning 306' from DER, 500' left of centerline, up to 33' AGL/64' MSL.

Poles and trees beginning 323' from DER, 219' right of centerline, up to 59' AGL/88' MSL.

Trees beginning 1003' from DER, 368' left of centerline, up to 33' AGL/71' MSL.

Stack 5536' from DER, 1749' right of centerline, 184' AGL/210' MSL.

**Rwy 30**, pole 143' from DER, 238' left of centerline, 43' AGL/76' MSL.

Pole 144' from DER, 281' right of centerline, 44' AGL/87' MSL.

Tree 3014' from DER, 1264' left of centerline, 133' MSL.

Poles and trees beginning 3217' from DER, 705' right of centerline, up to 46' AGL/353' MSL.

Trees, poles, and transmission line beginning 3282' from DER, 135' right of centerline, up to 41' AGL/355' MSL.

Tree 3492' from DER, 327' left of centerline, 164' MSL.

Tree 4406' from DER, 194' left of centerline, 55' AGL/172' MSL.

Tree 4765' from DER, 109' left of centerline, 34' AGL/176' MSL.

Pole 5243' from DER, 513' left of centerline, 106' AGL/197' MSL.

Poles beginning 5256' from DER, 188' left of centerline, up to 73' AGL/216' MSL.

Buildings beginning 1.2 NM from DER, 1986' left of centerline, up to 194' AGL/259' MSL.




# TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)




22251




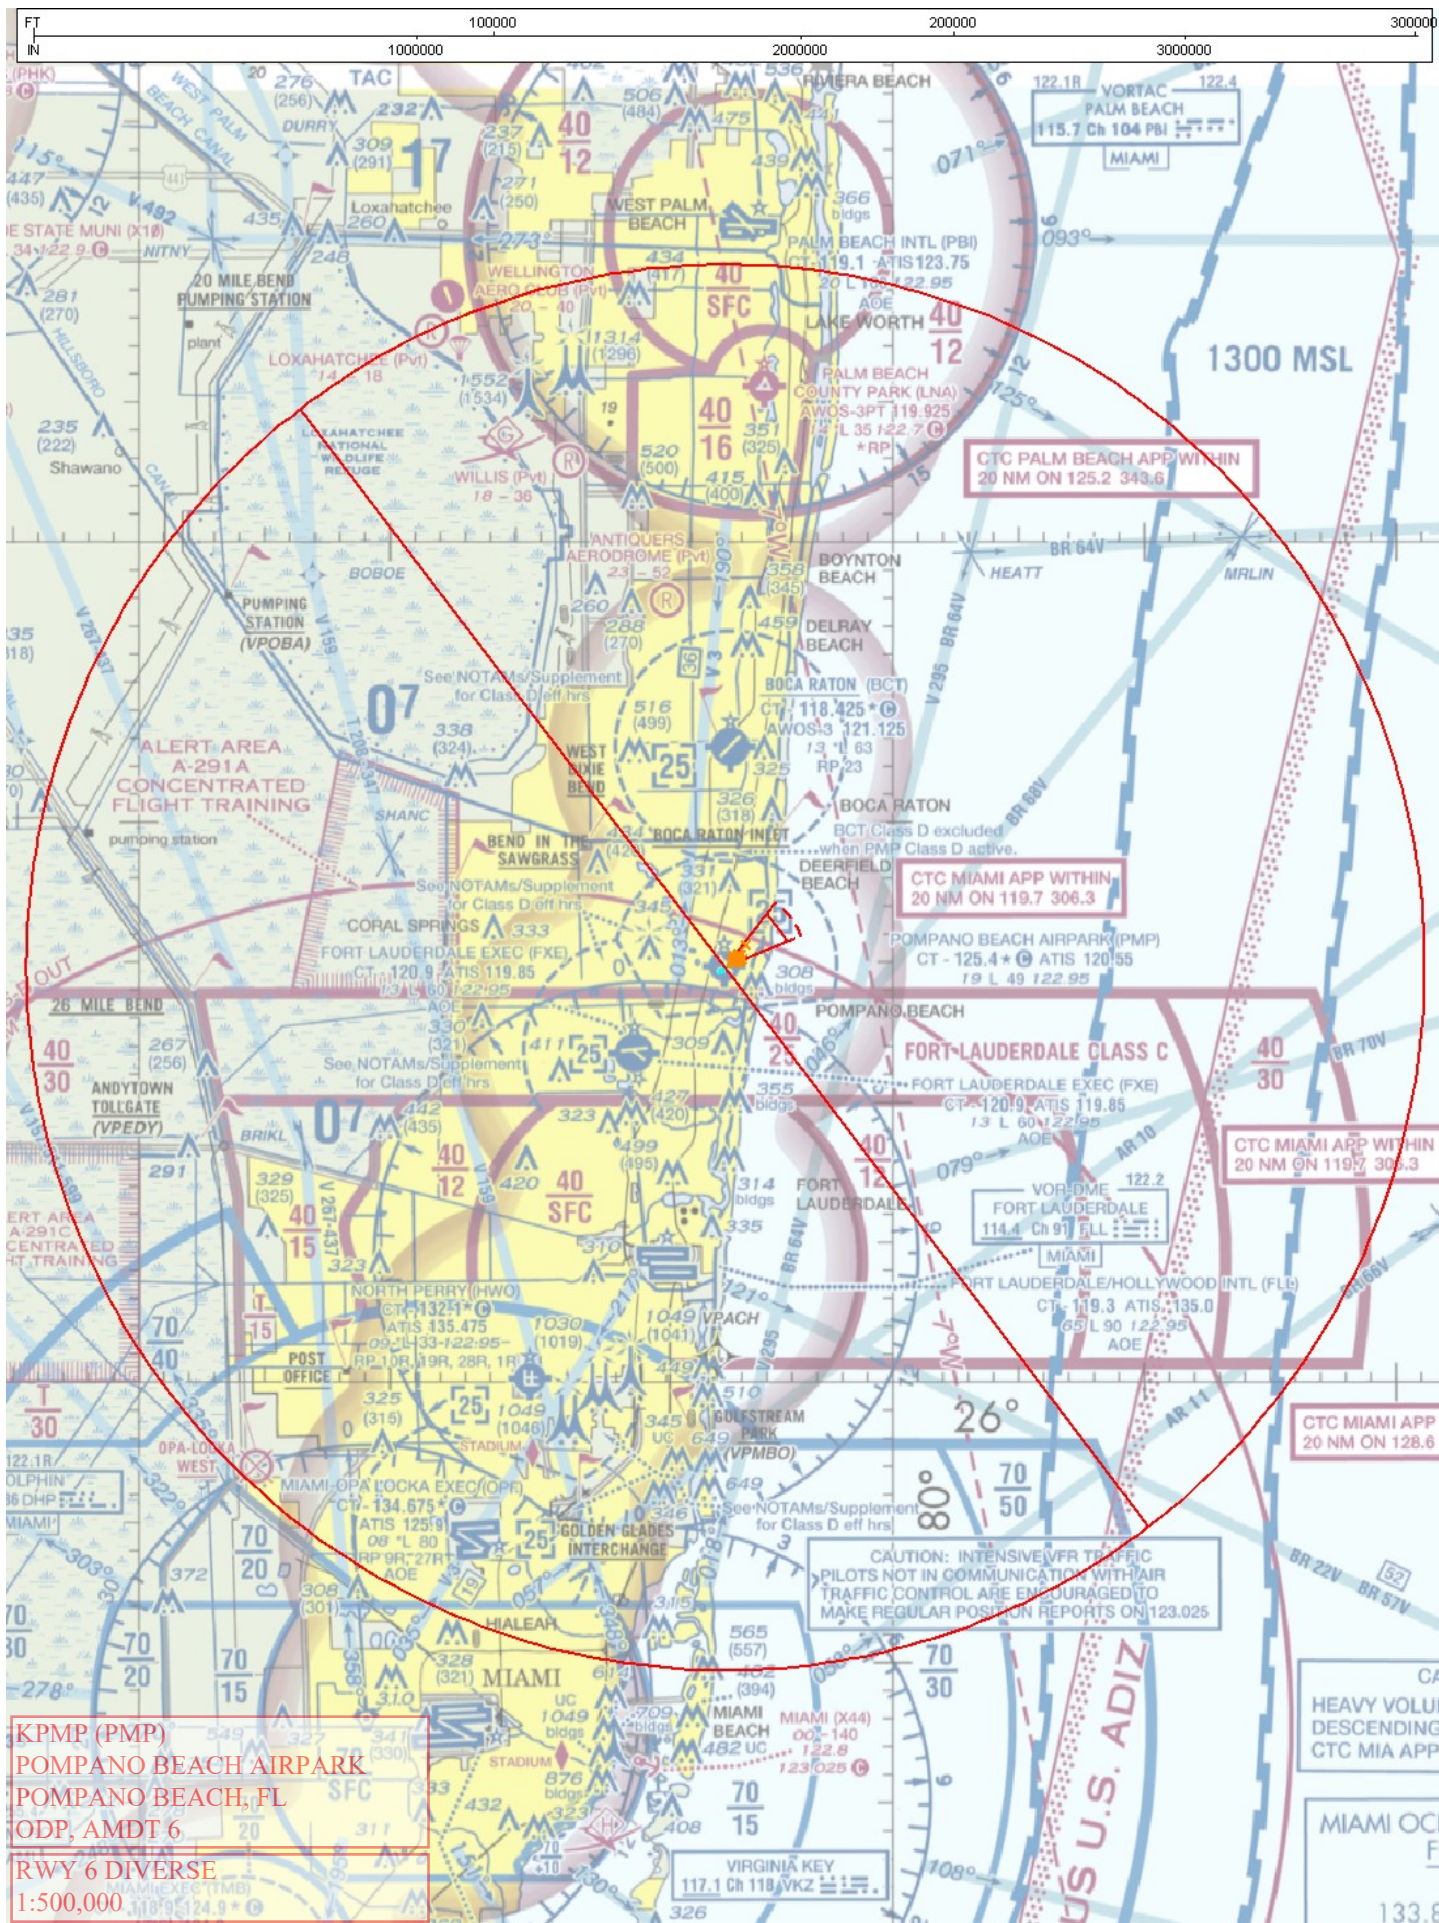




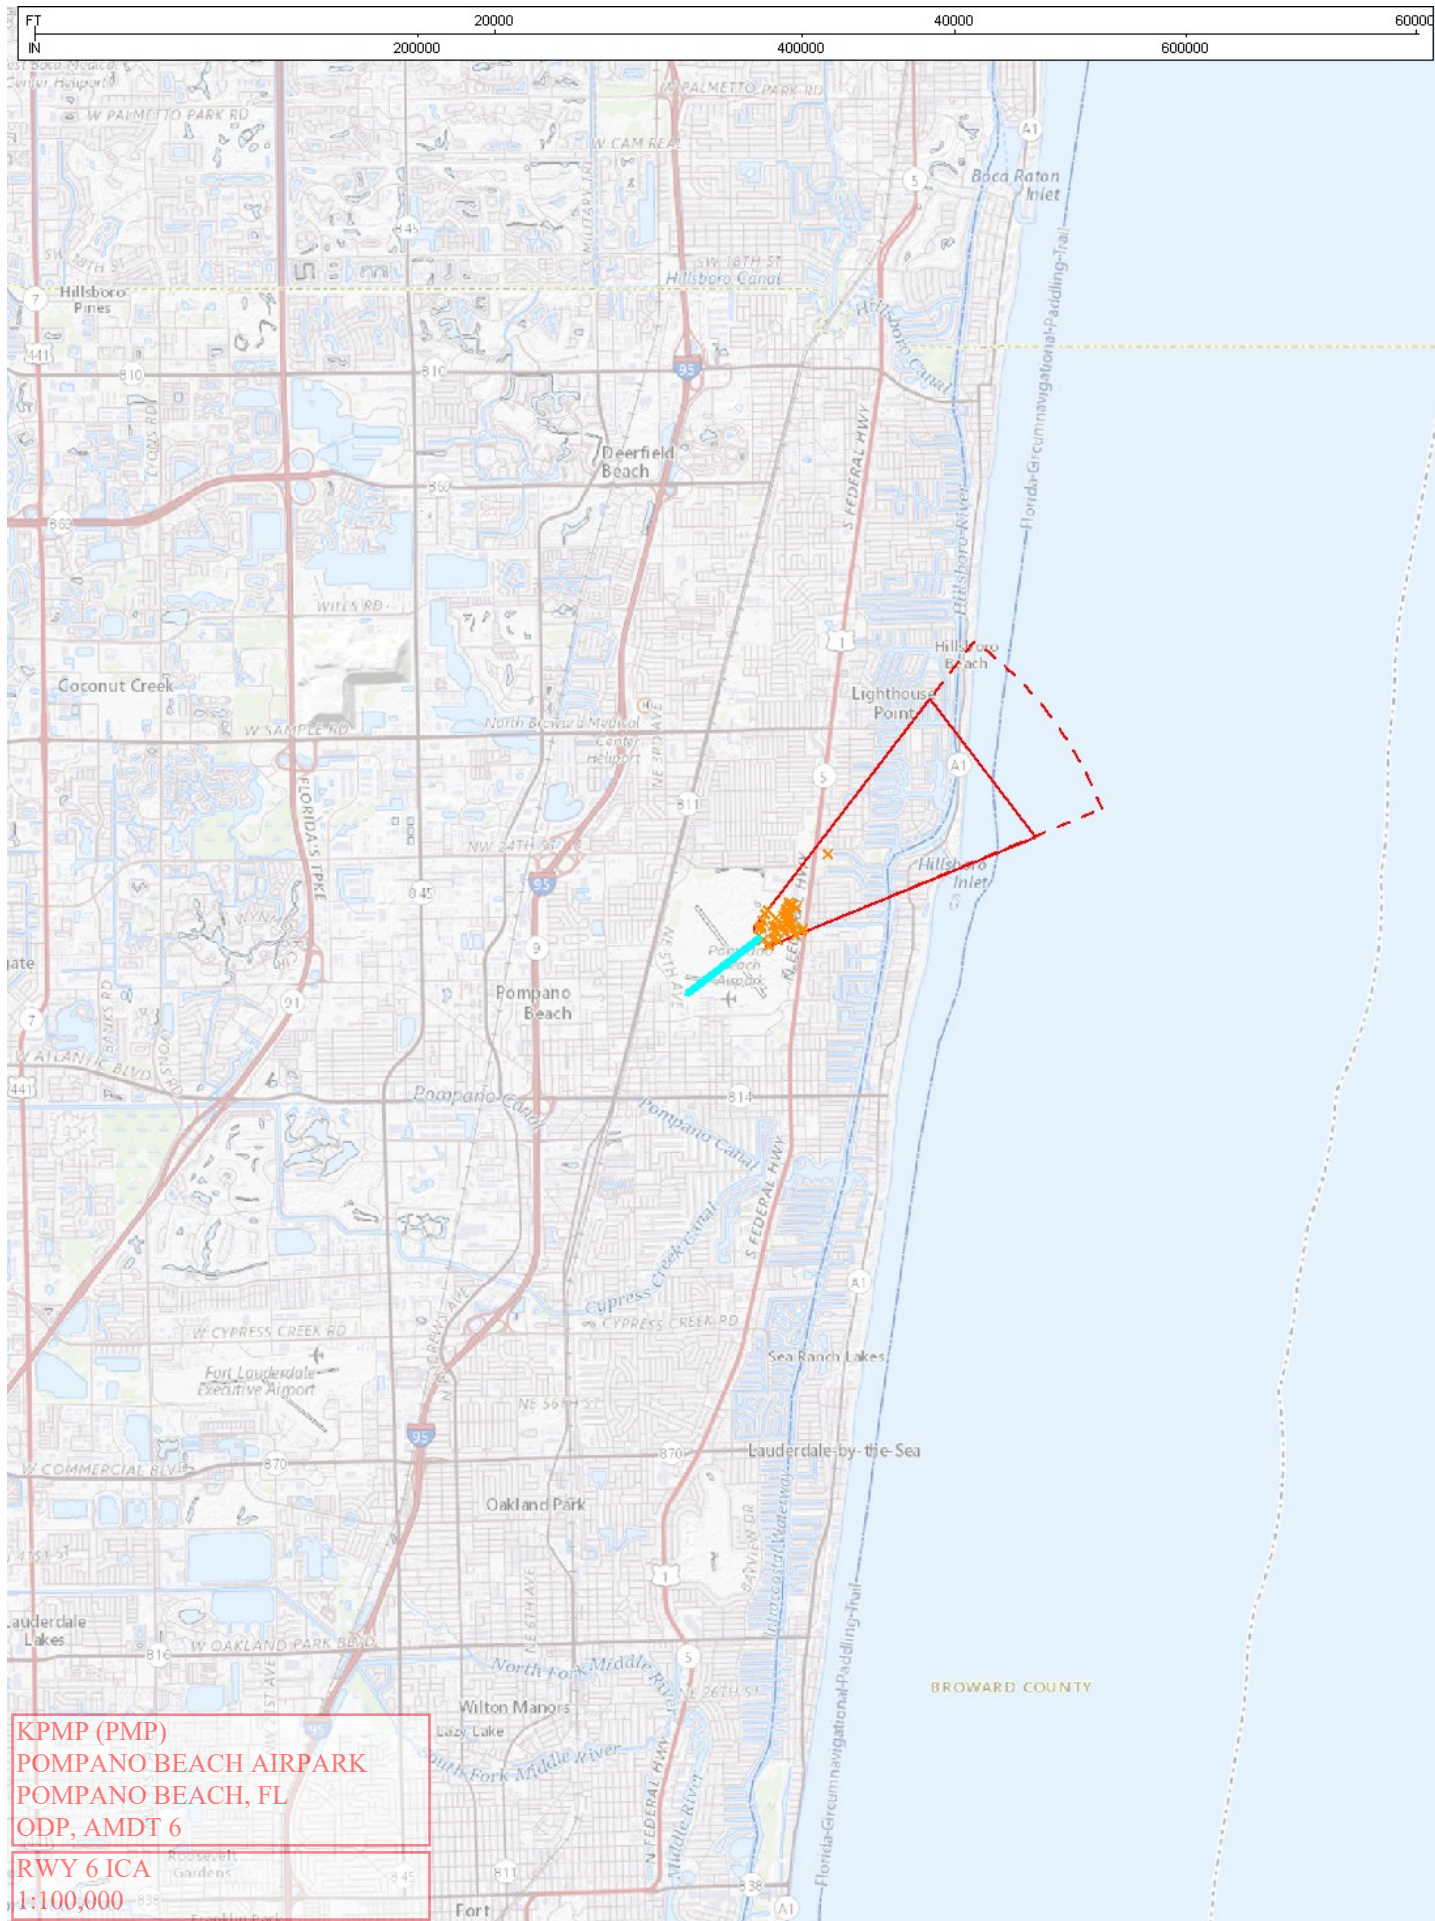




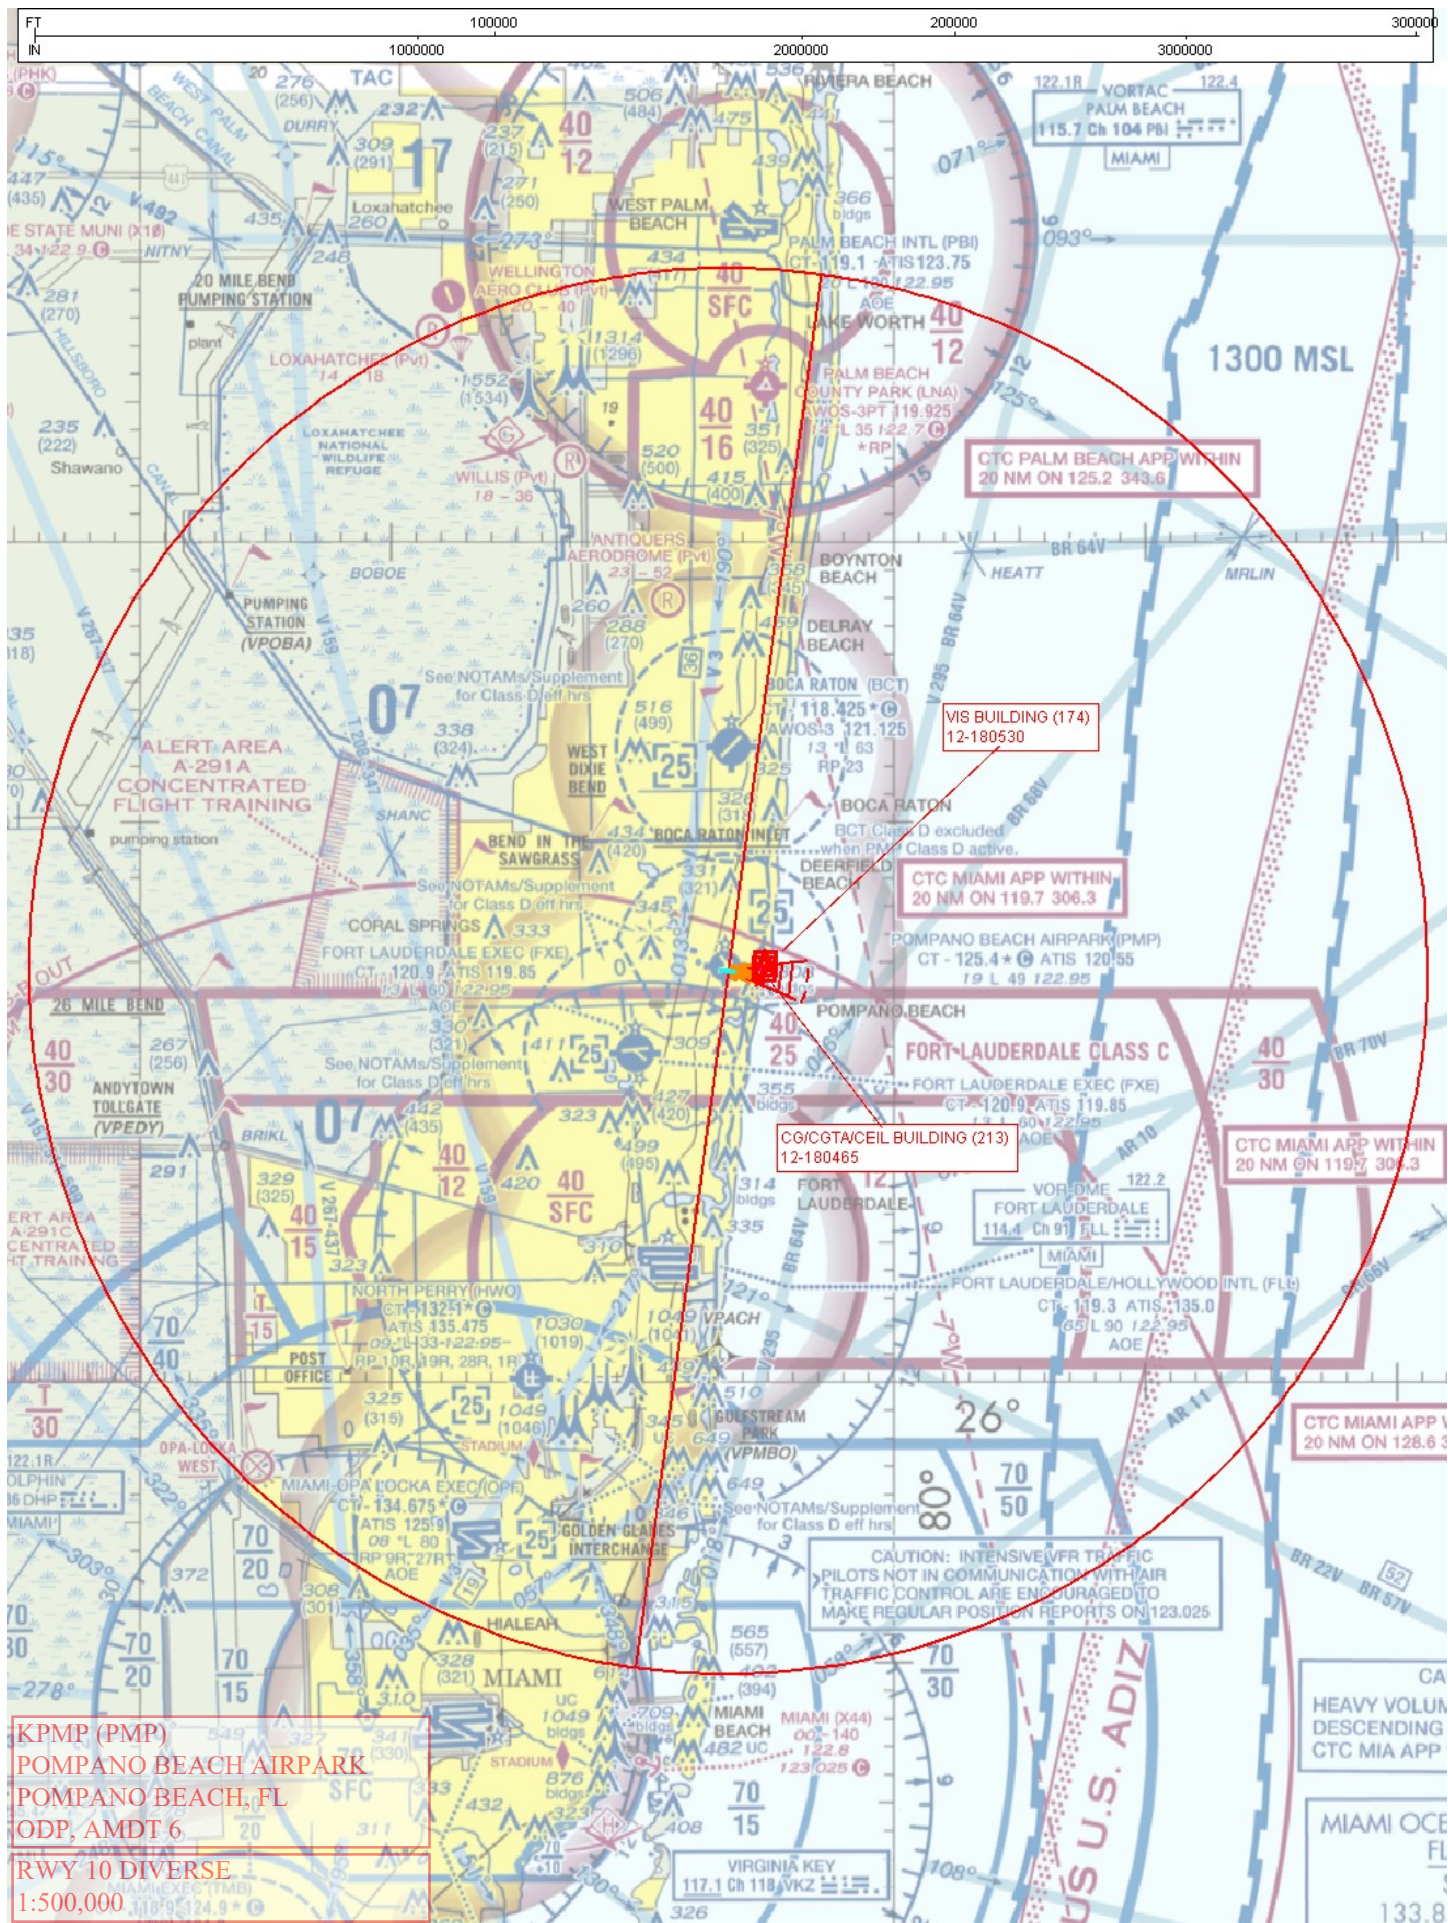




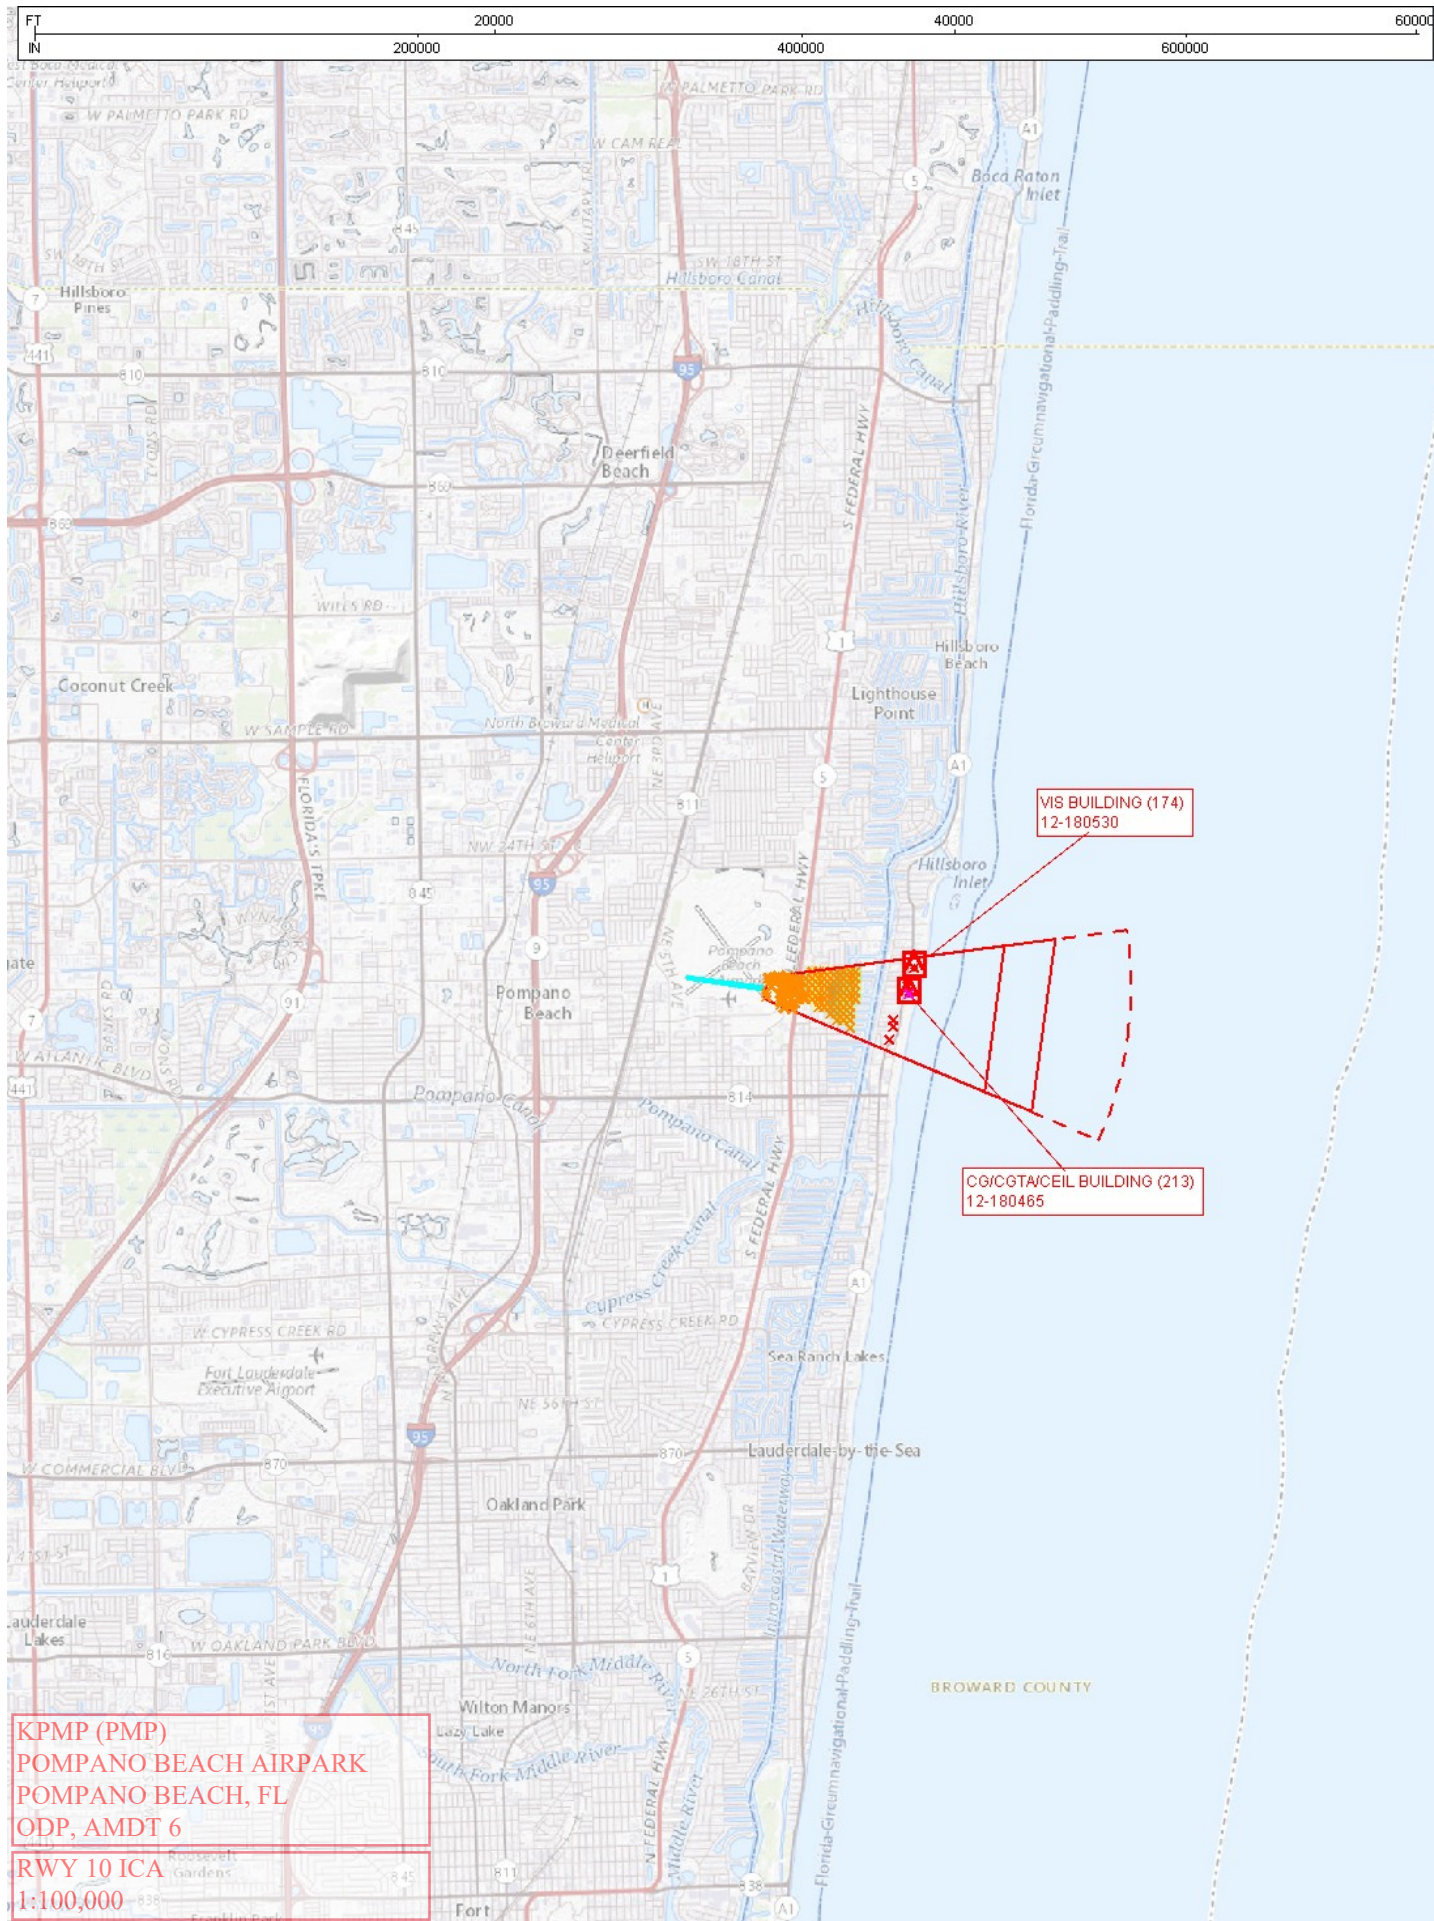




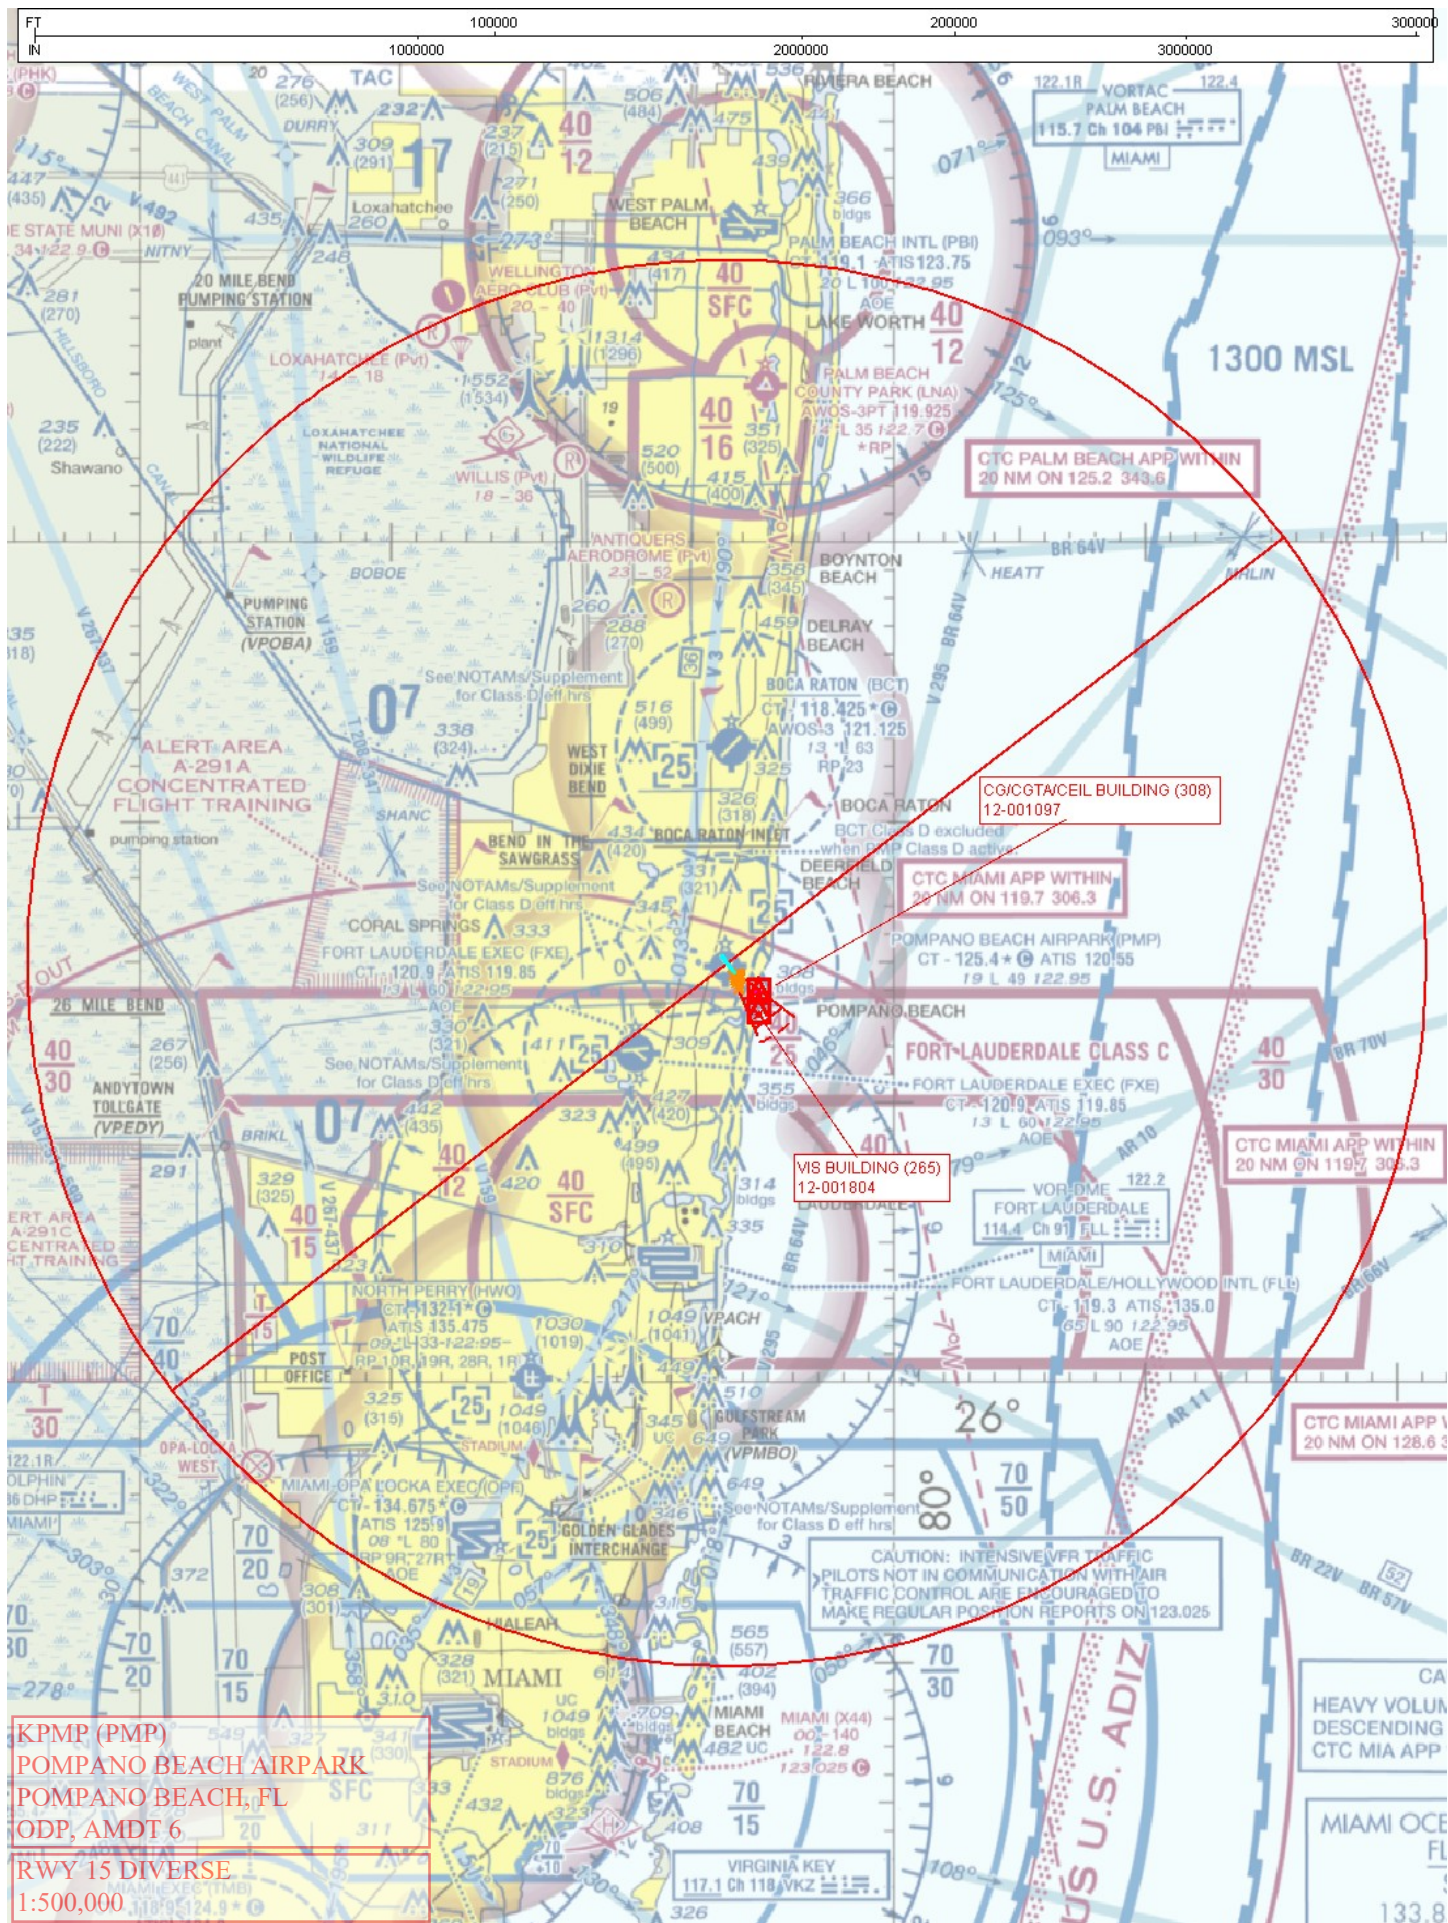




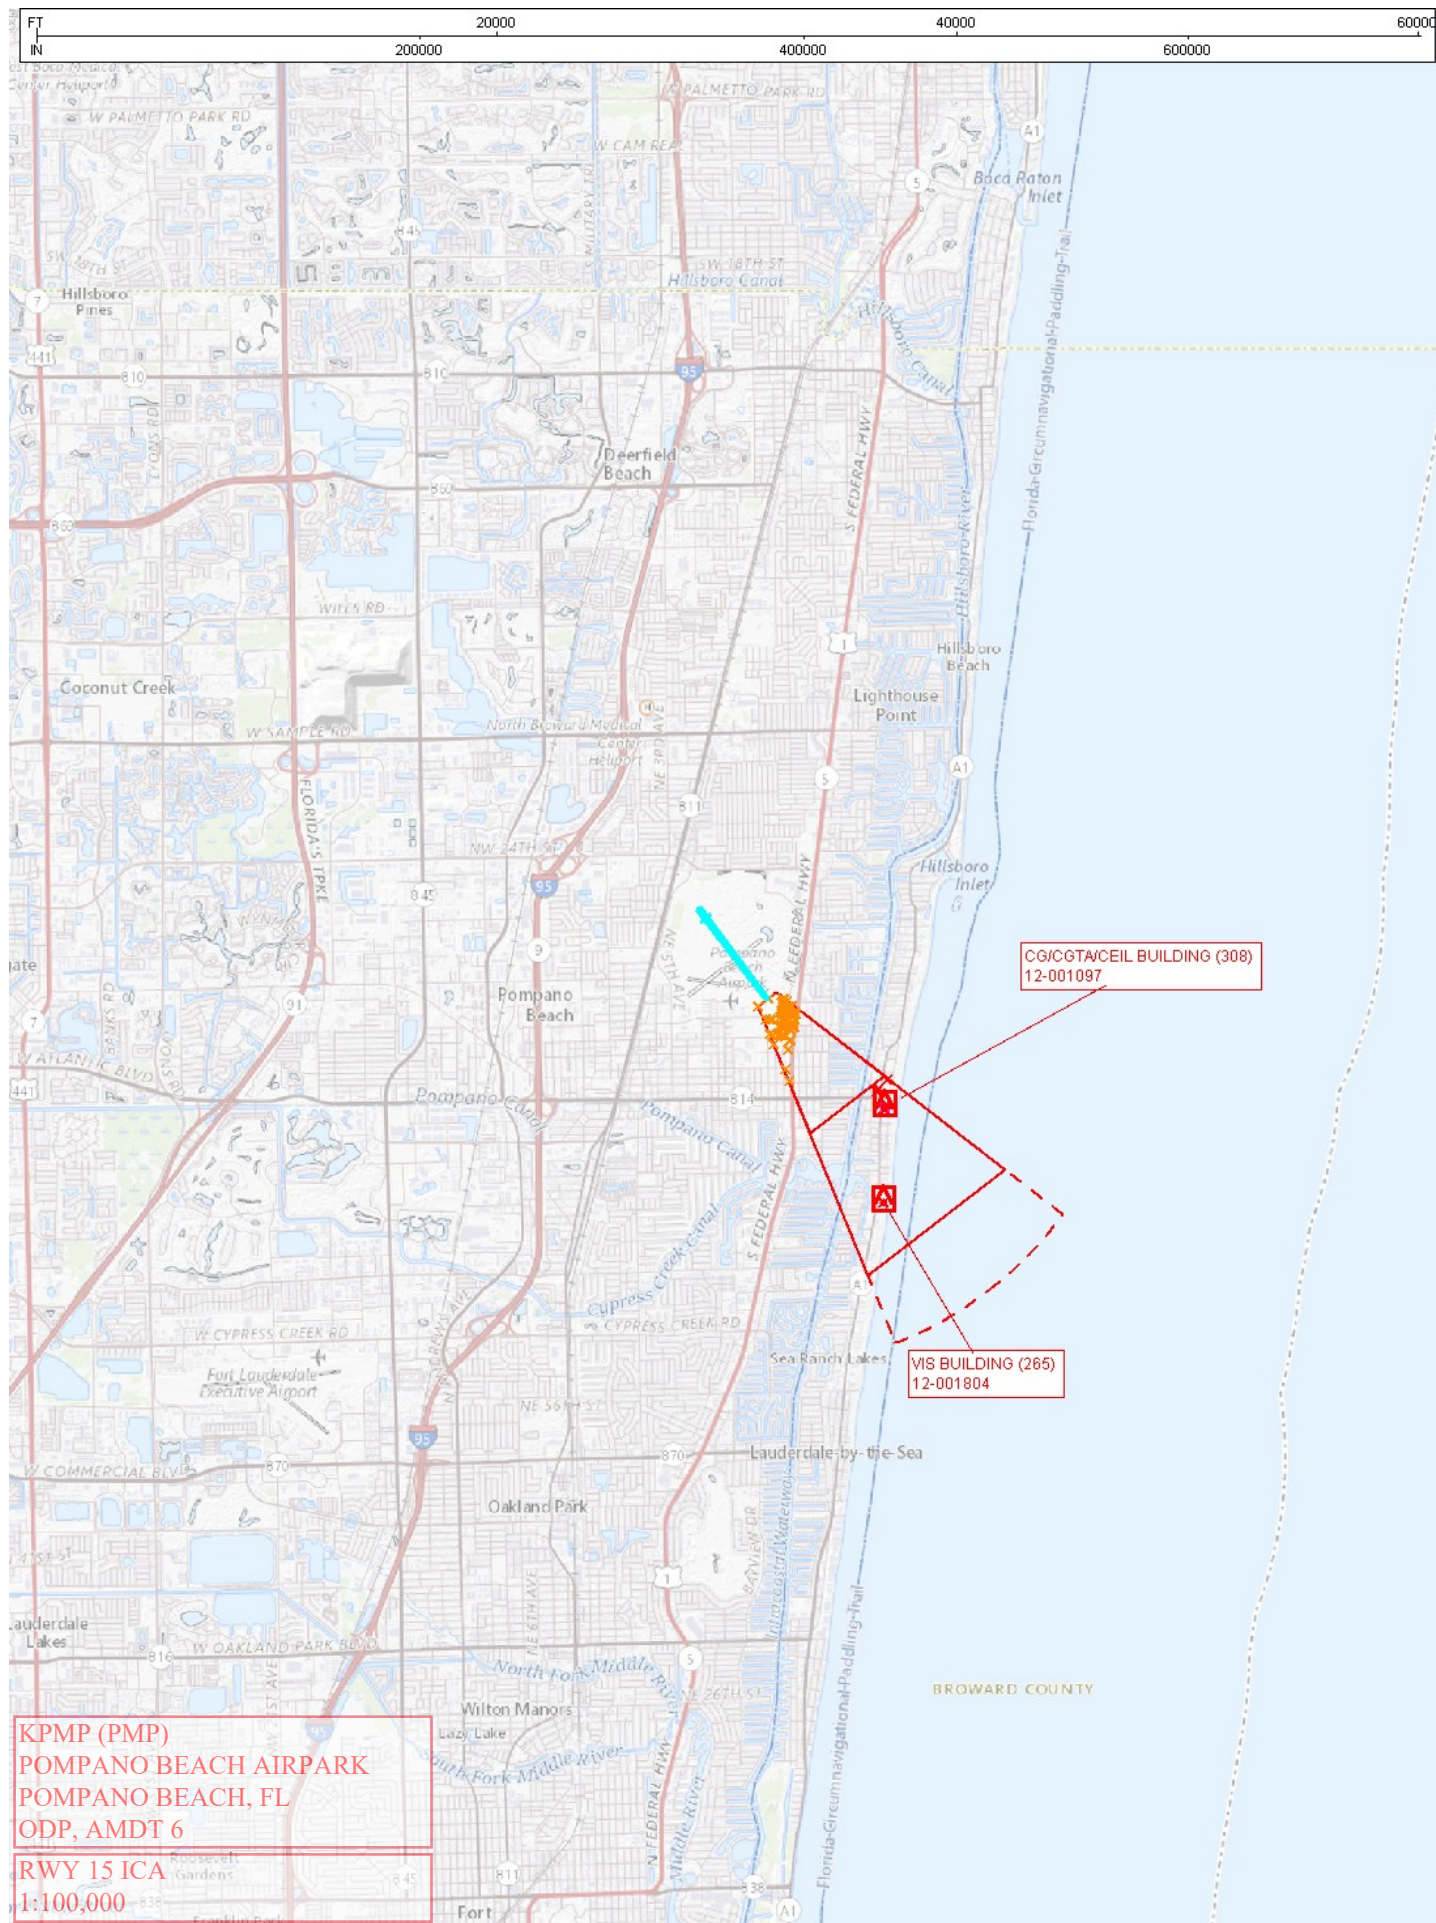




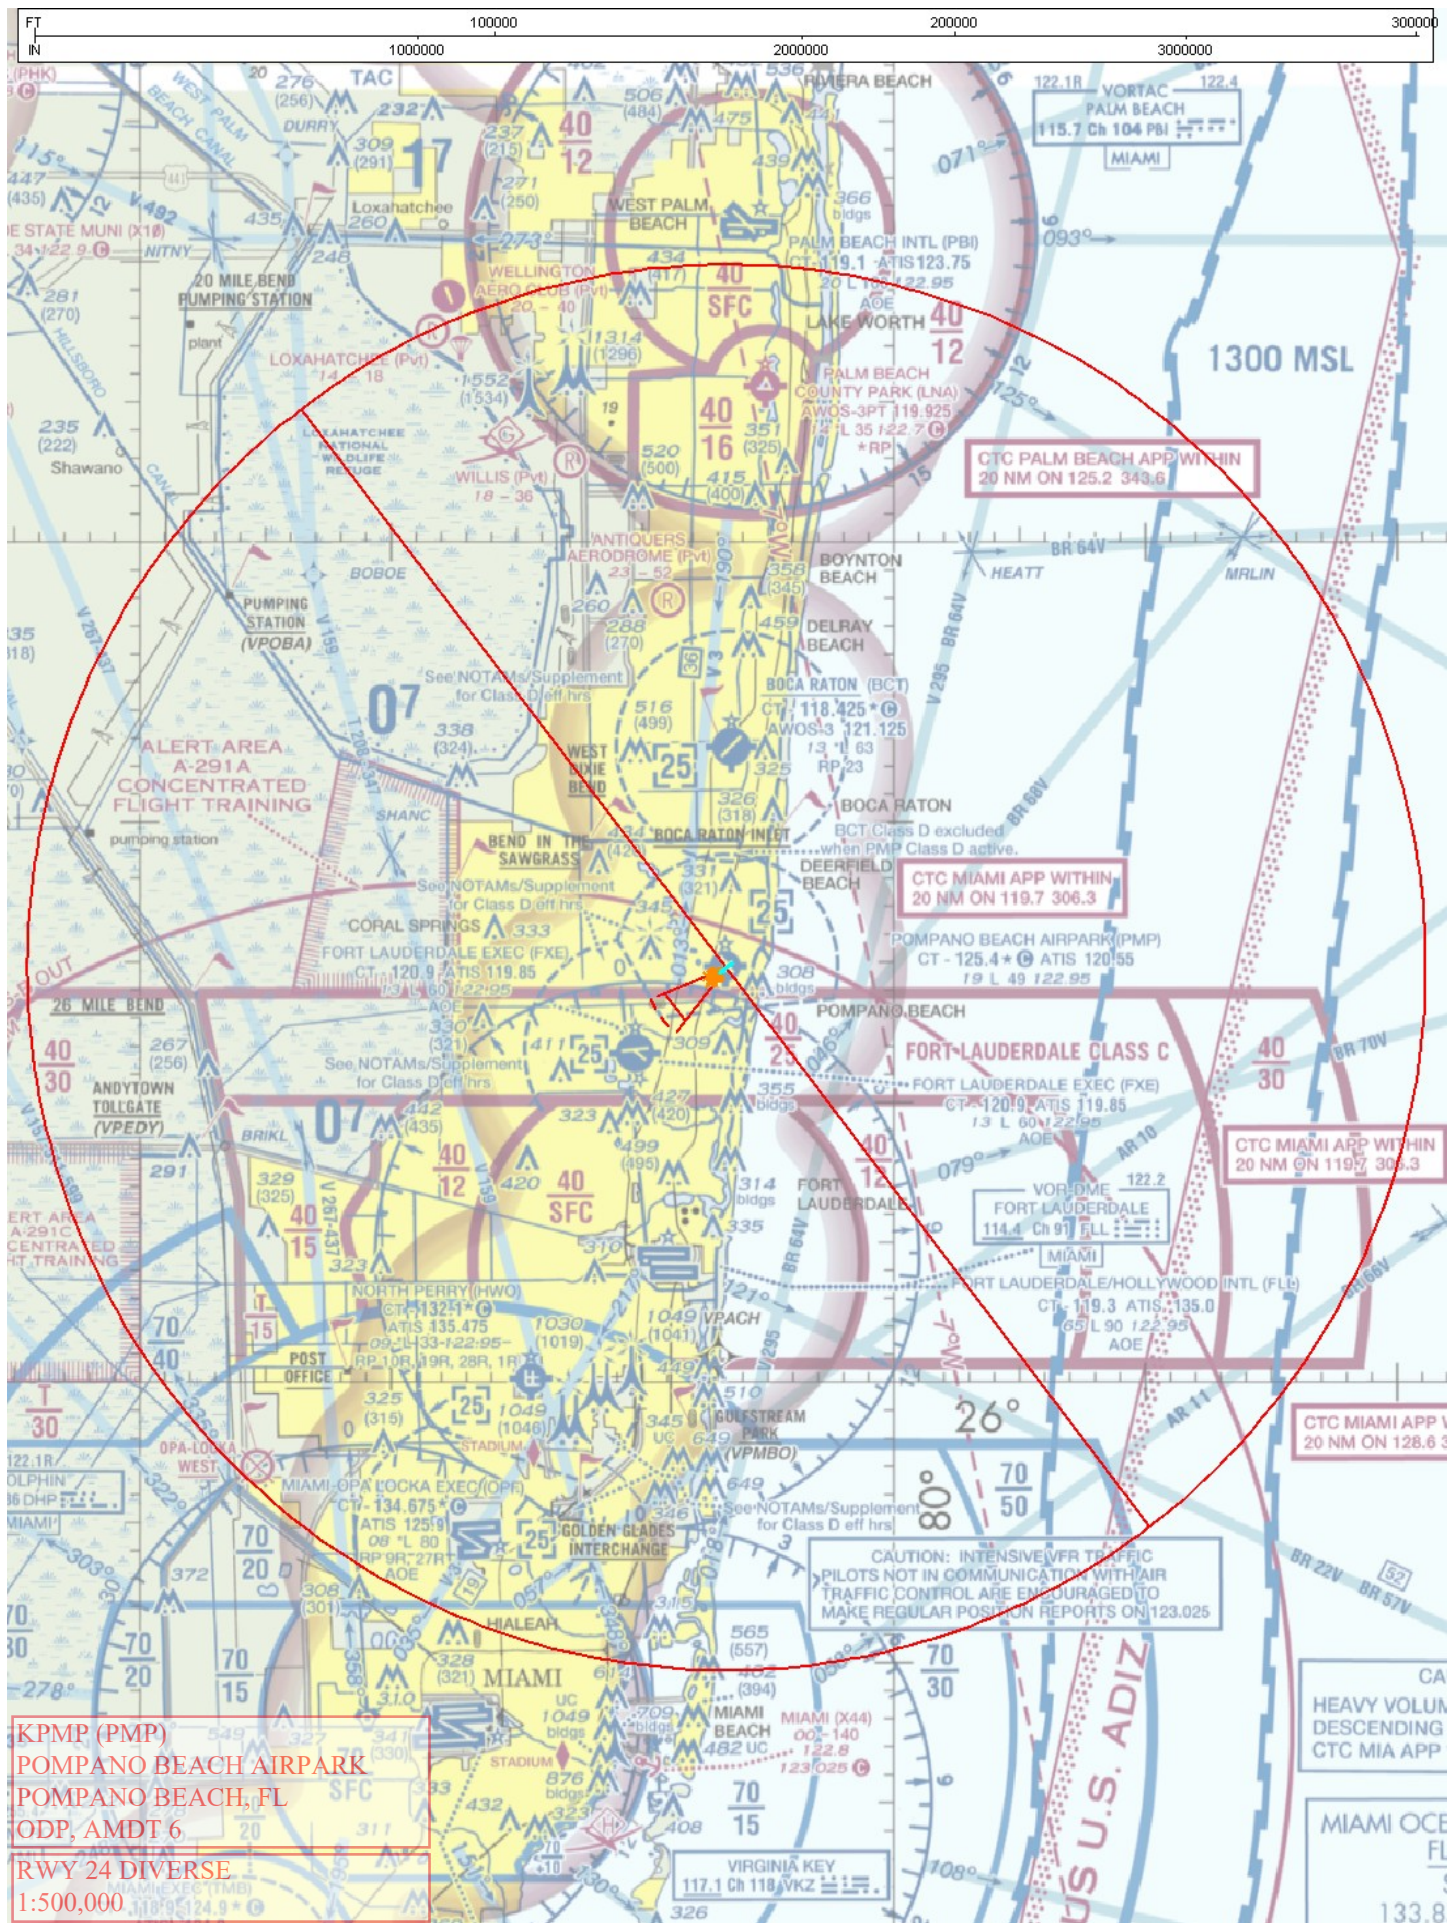




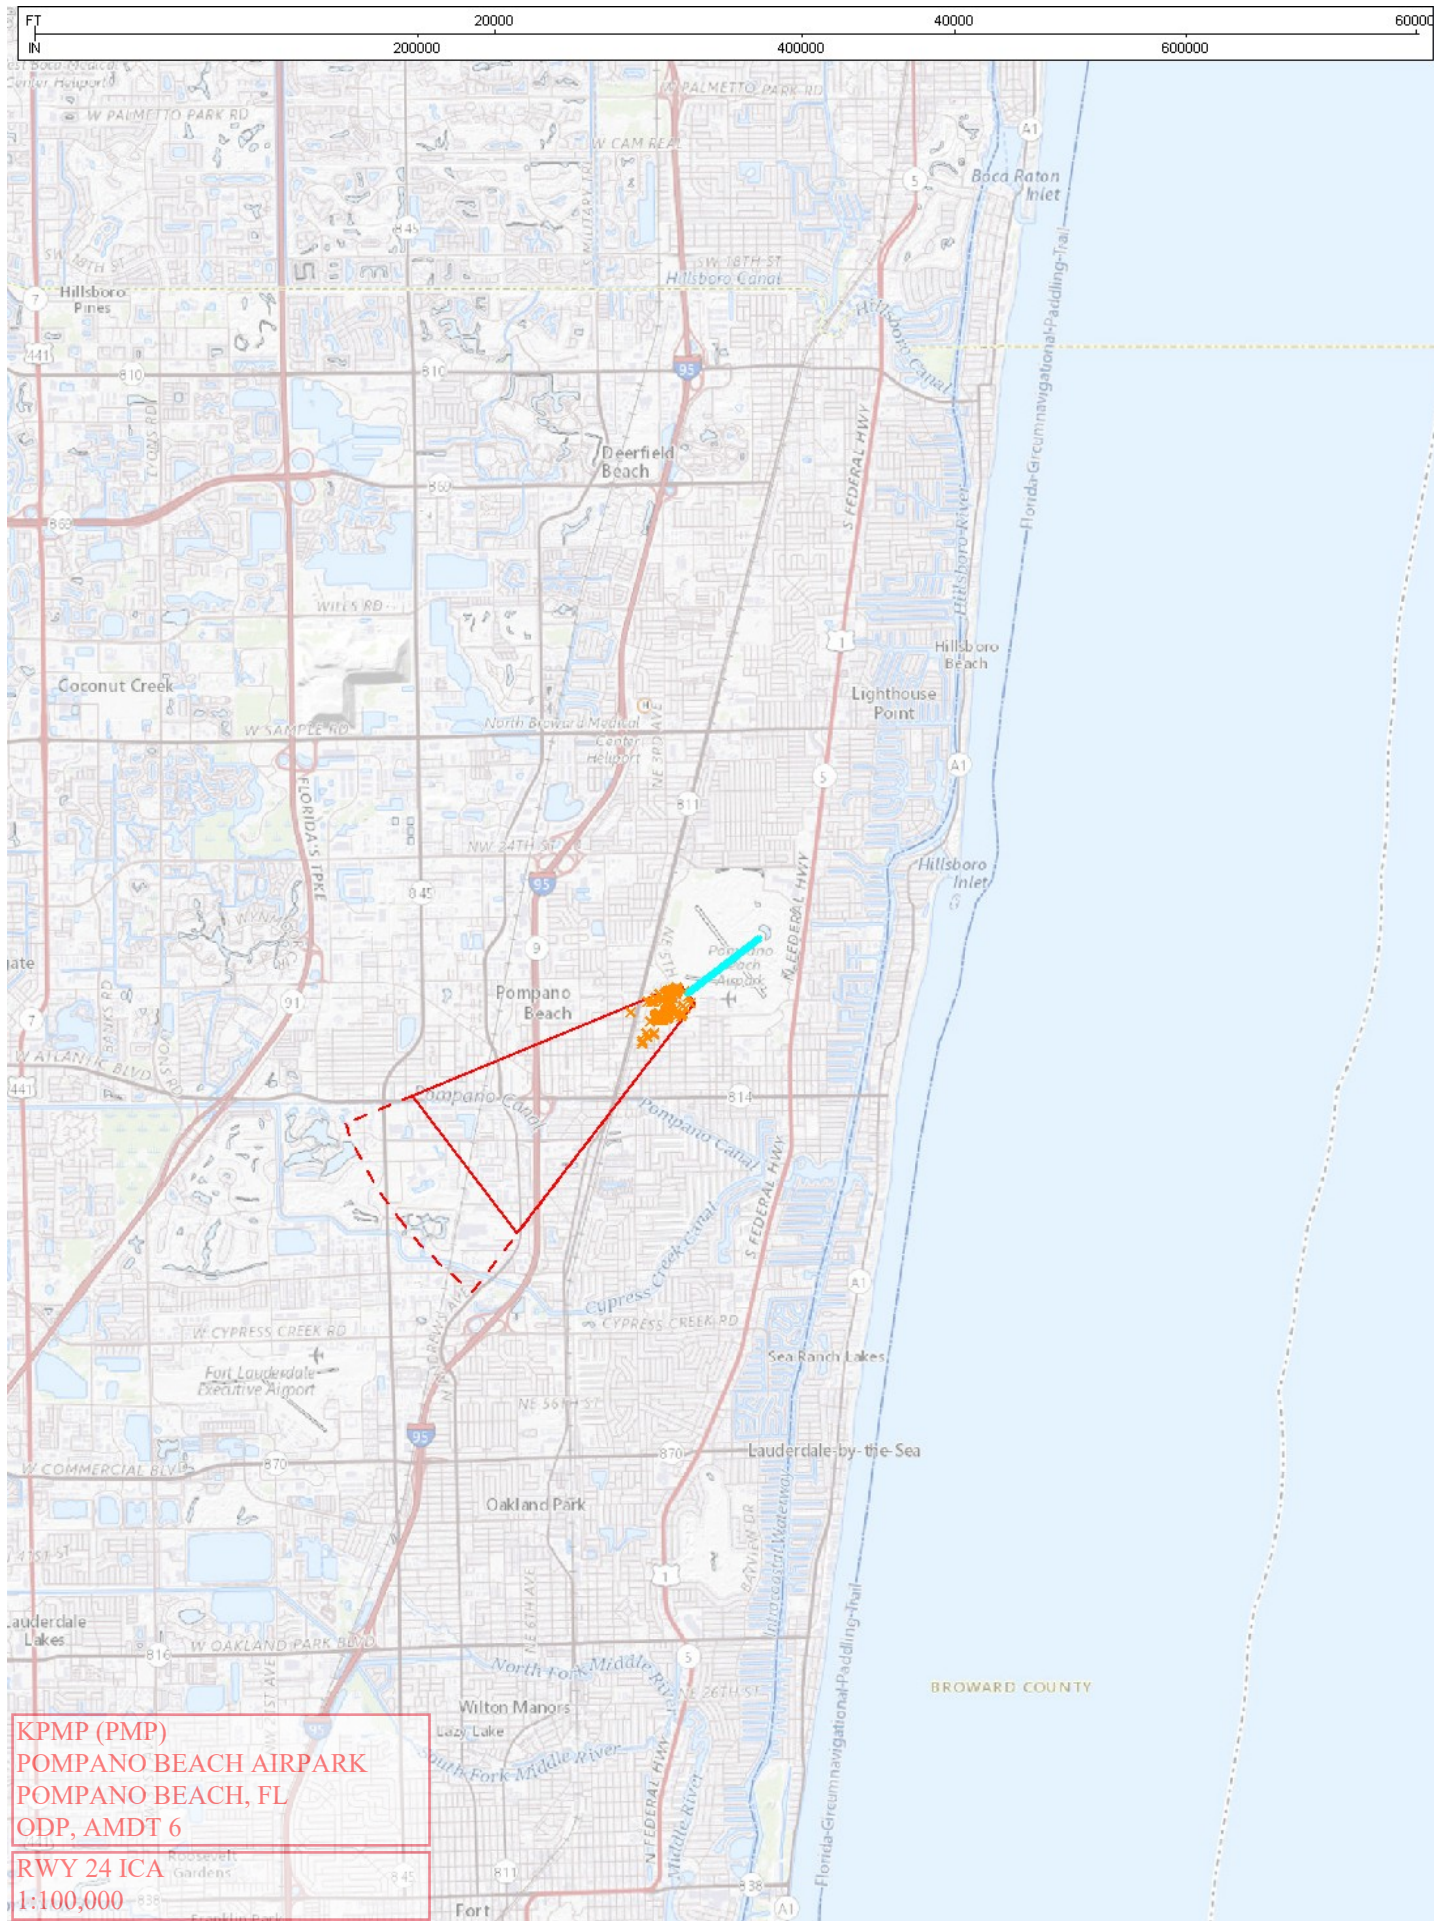




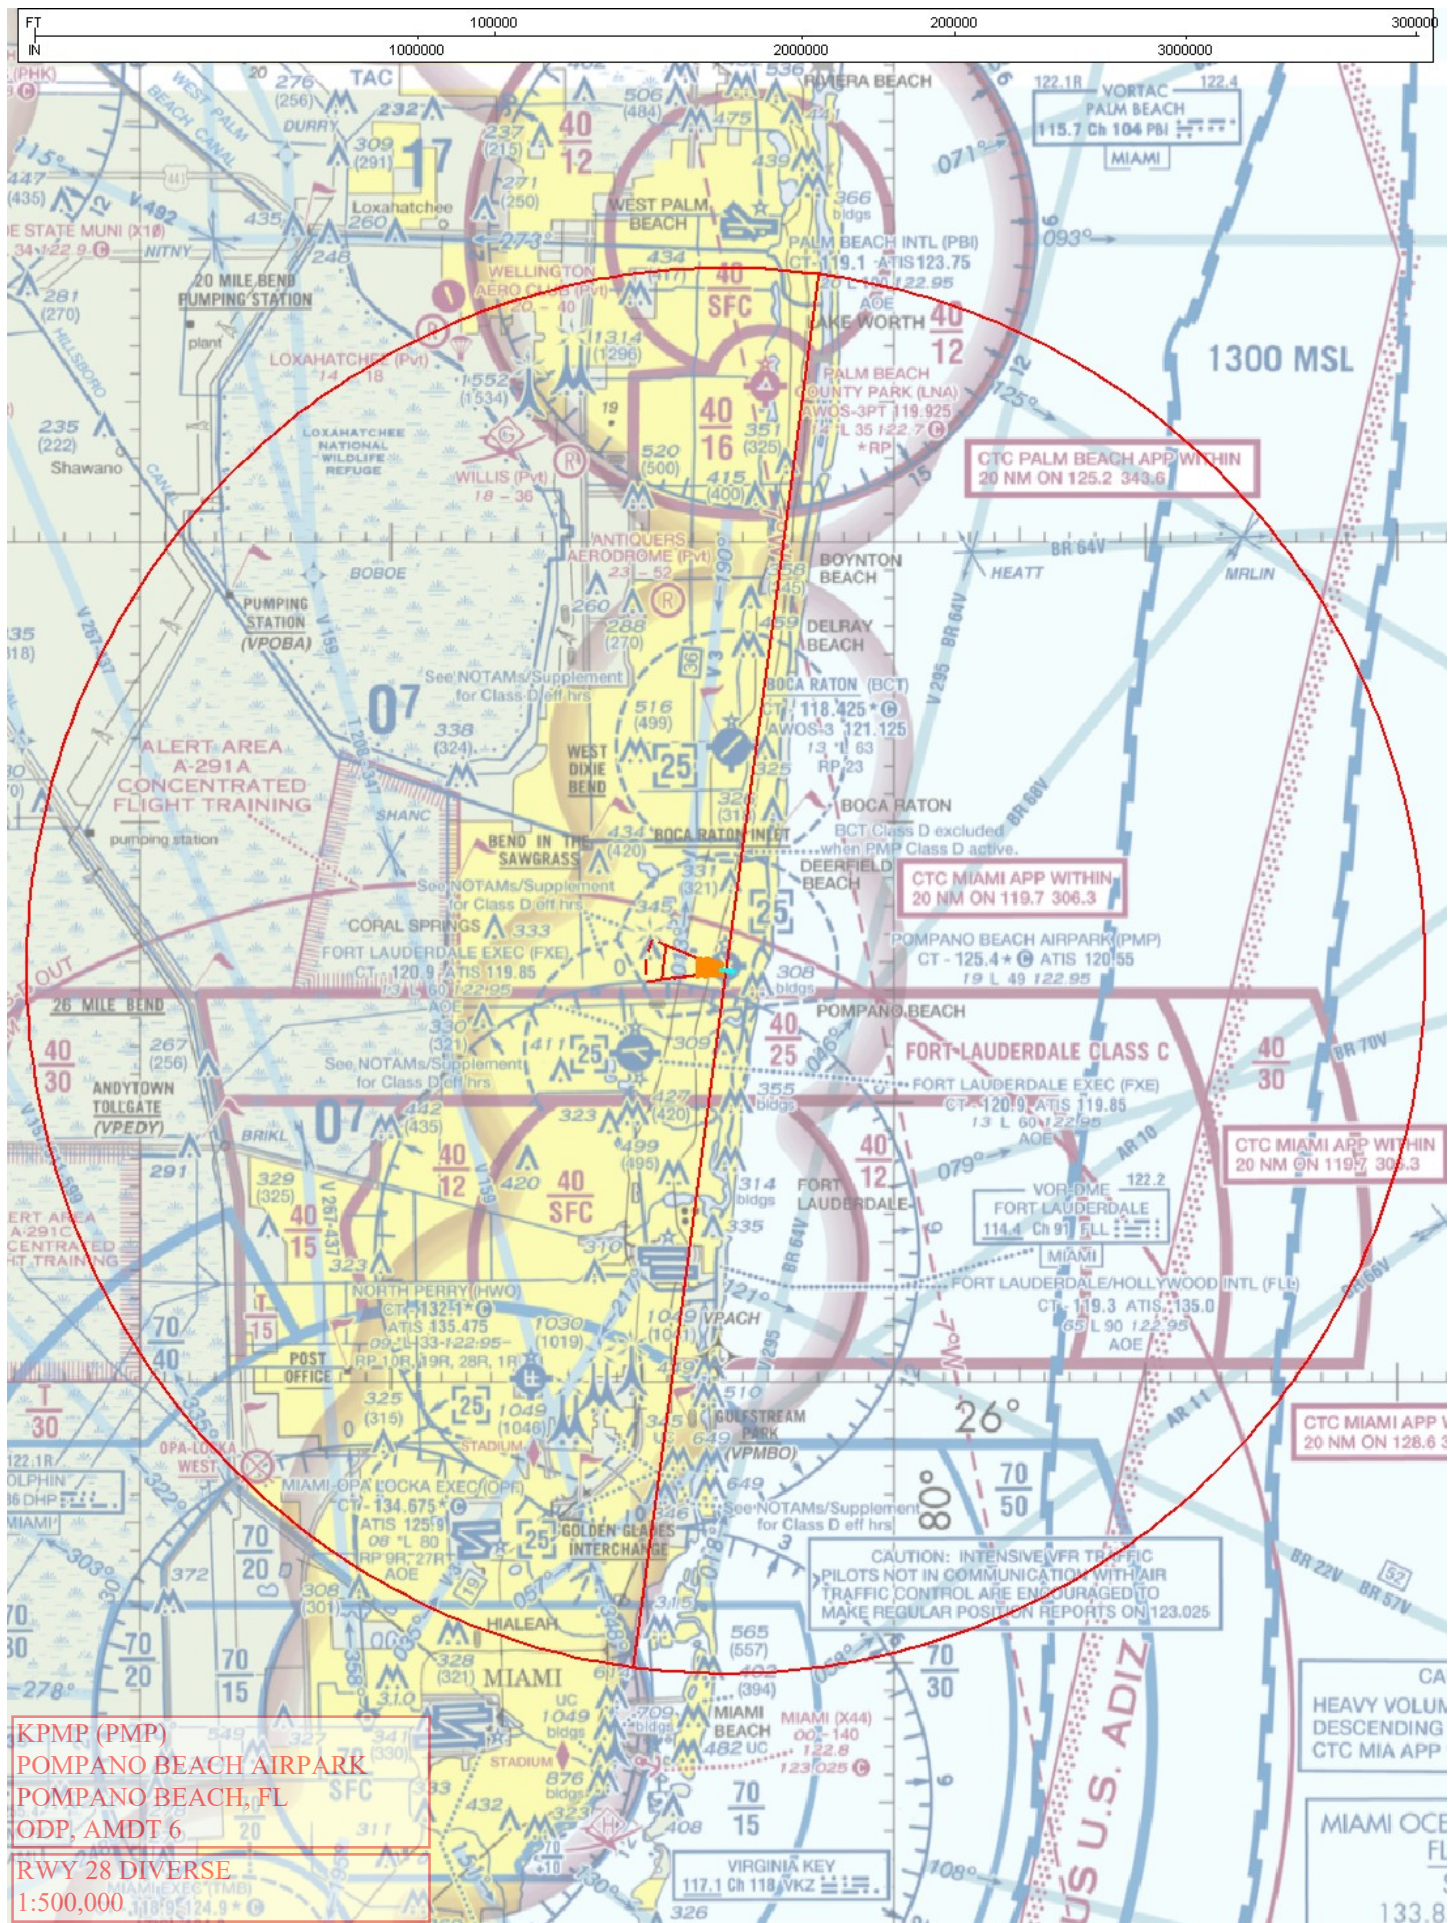



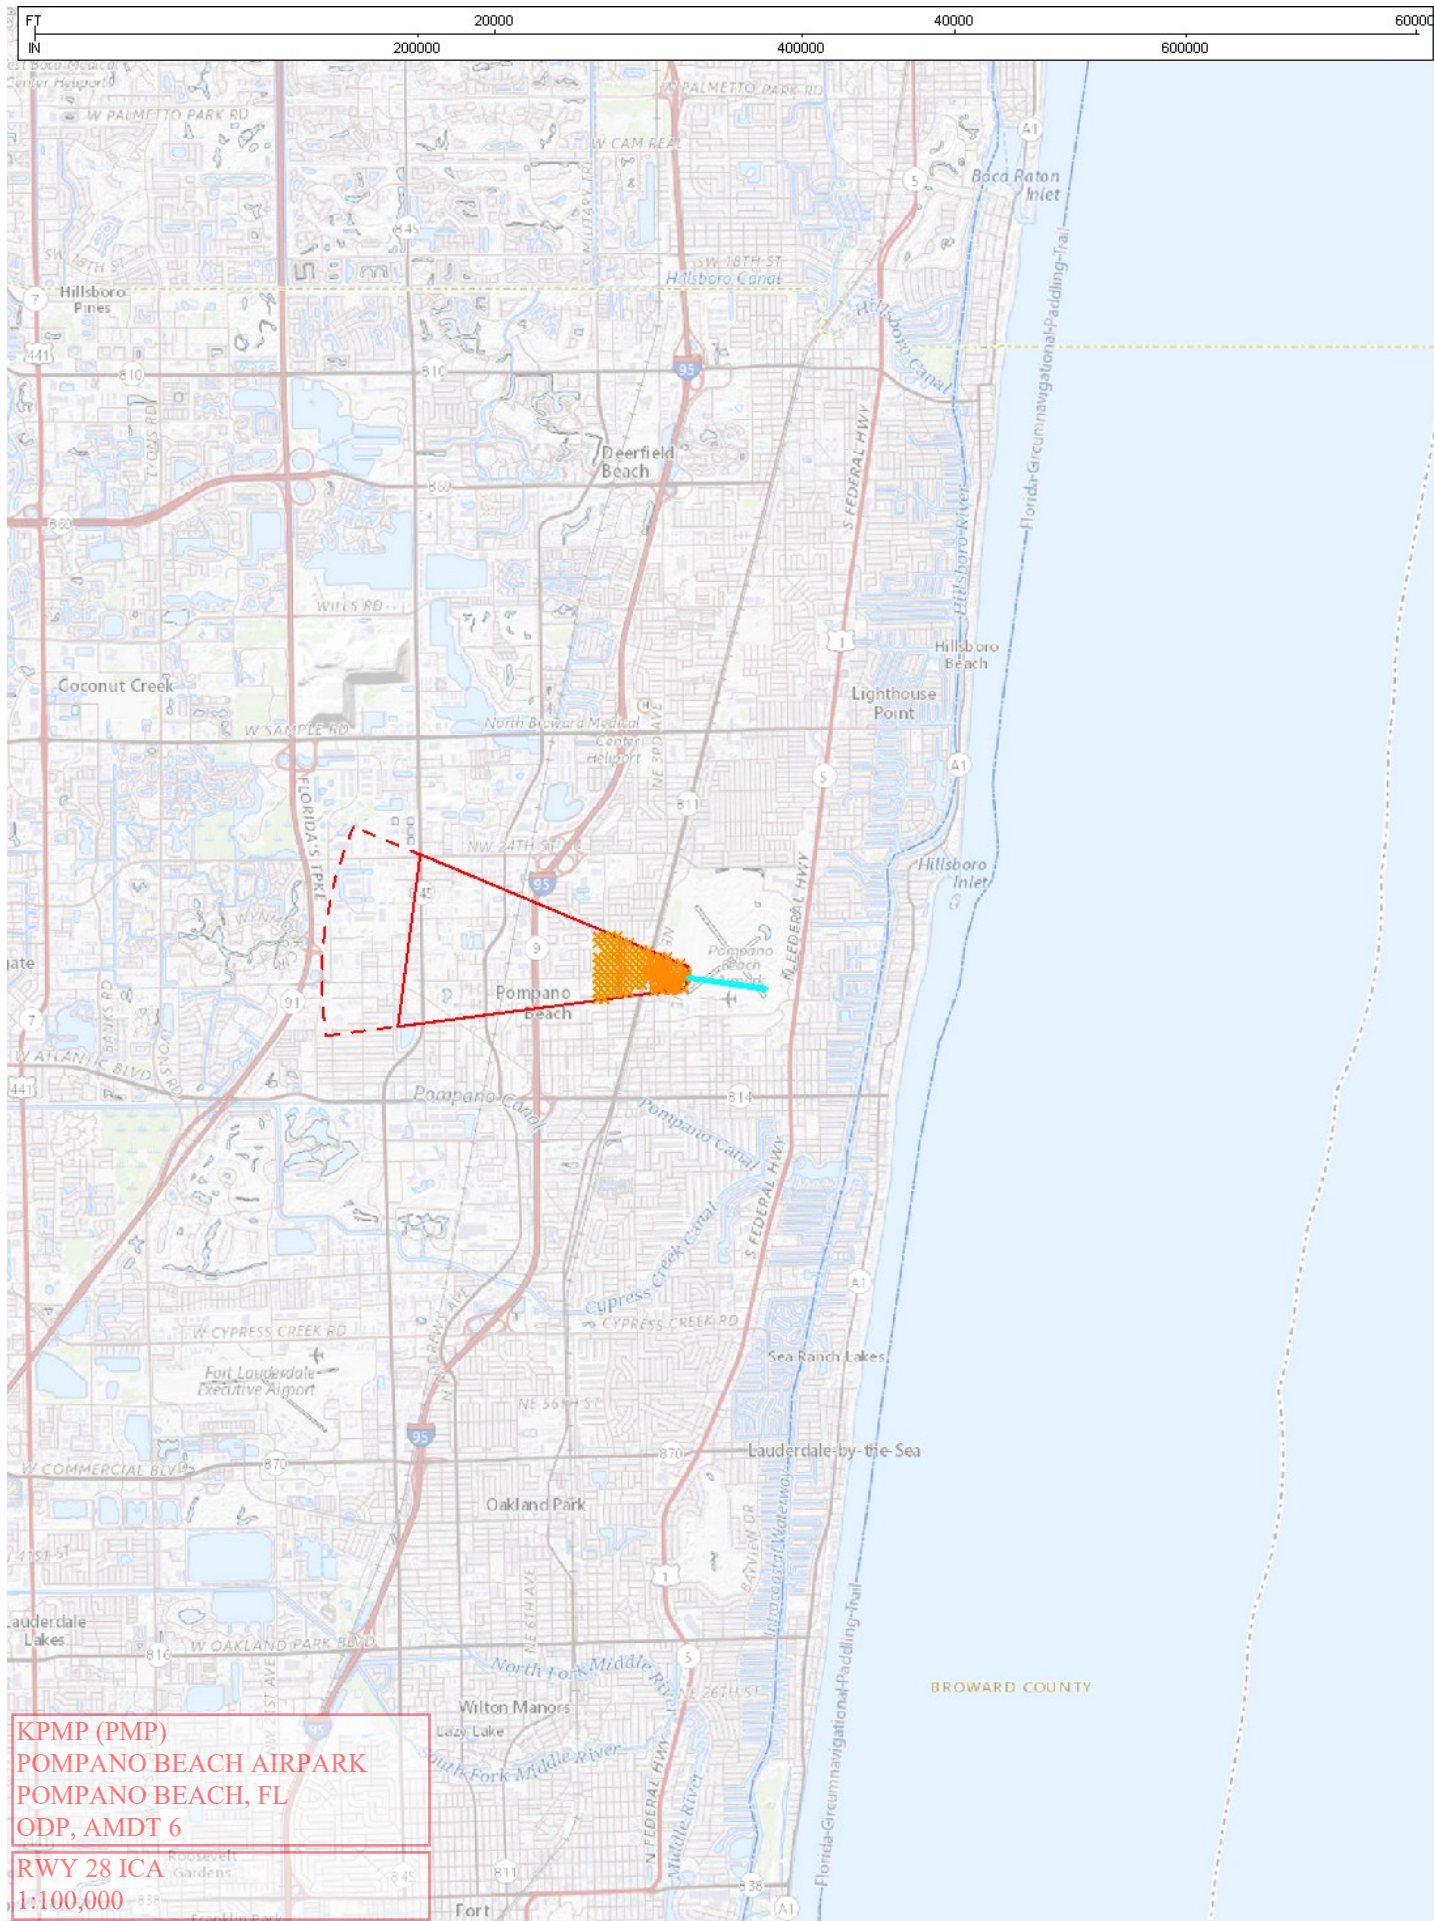



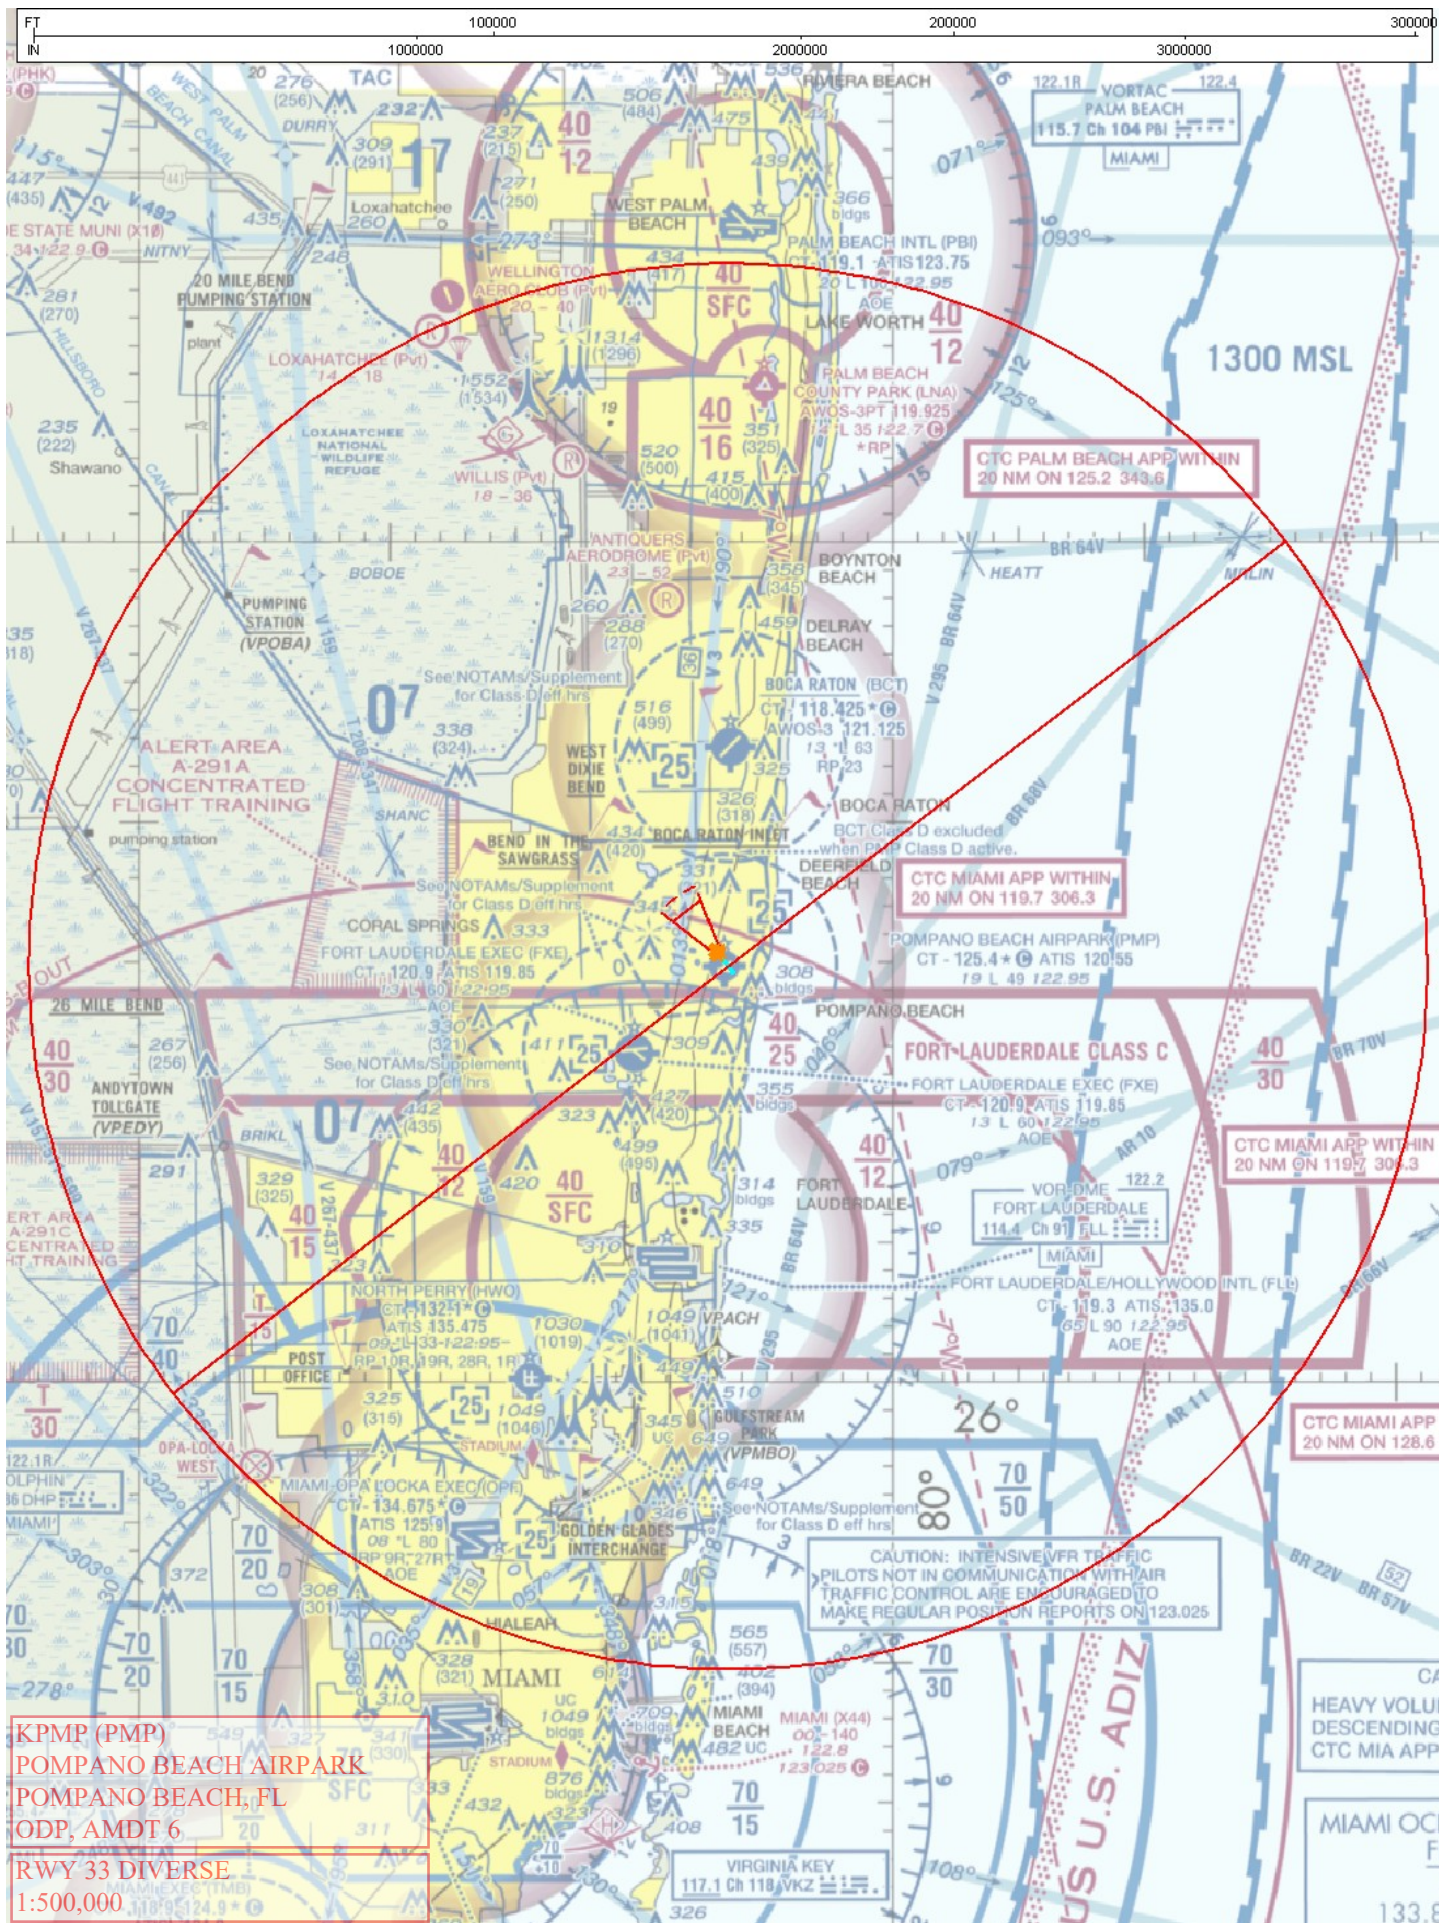

KPMP (PMP)  
POMPANO BEACH AIRPARK  
POMPANO BEACH, FL  
ODP, AMDT 6

RWY 33 DIVERSE  
1:500,000

CAUTION: INTENSIVE VFR TRAFFIC  
PILOTS NOT IN COMMUNICATION WITH AIR  
TRAFFIC CONTROL ARE ENCOURAGED TO  
MAKE REGULAR POSITION REPORTS ON 123.025

CA  
HEAVY VOLUME  
DESCENDING  
CTC MIA APP

MIAMI OCE  
FL  
133.8



