

Flight Procedures Cover Page	Task Action: Abbreviated Amendment	Task Type: Textual DP	Estimated Chart Date: 08/07/2025	APWS Task ID: 468C1E04B5C44C4ABBAD7E4FC727FC7A	APWS Project ID: 80FB728083594DA286B85C2CC2F730A2
Procedure: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 0A		Enroute: NO	Specialist: Feronti, Tia		Agreement Number:
Airport ID: M36			Airport City: BRINKLEY		State: AR
Facility ID:	Facility Type:	Flight Inspection Remark Type:			
<div>Procedure Comments: PROCESSED IAW TECHNICAL SUPPORT GROUP (AJF-17) MEMO DATED 07/07/2021, SUBJECT: GUIDANCE FOR PROCEDURAL CHANGES REQUIRING FLIGHT INSPECTION/VALIDATION. CLEAR NOTAM 3/3197. UPDATED TAKEOFF OBSTACLE NOTES. CONTACT DAVID DANNER, AJV-A421, 405-954-5077.</div> <div>QUALITY 23 CHECKED</div>					

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)

25051

BLYTHEVILLE, AR (CON'T)

BLYTHEVILLE MUNI (HKA)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG 05JUN08 (08157) (FAA)

TAKEOFF OBSTACLE NOTES:

Rwy 18, tree 487' from DER, 345' left of centerline, 100' AGL/364' MSL.

Tree 1780' from DER, 748' right of centerline, 100' AGL/364' MSL.

Rwy 36, tree 2393' from DER, 825' right of centerline, 100' AGL/359' MSL.

BOISE CITY, OK

BOISE CITY (17K)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG 22OCT09 (09295) (FAA)

TAKEOFF OBSTACLE NOTES:

Rwy 22, hangars 243' from DER, 226' right of centerline, 35' AGL/4212' MSL.

Vehicle on road 566' from DER, right and left of centerline, up to 15' AGL/4192' MSL.

BRINKLEY, AR

FRANK FEDERER MEML (M36)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

ORIG 20OCT11 (22139) (FAA)

DEPARTURE PROCEDURE:

Rwy 20, climb heading 204° to 700 before proceeding on course.

TAKEOFF OBSTACLE NOTES:

Rwy 2, trees beginning 425' from DER, 138' right of centerline, up to 100' AGL/299' MSL.

Trees beginning 680' from DER, 262' left of centerline, up to 100' AGL/299' MSL.

Rwy 20, trees and terrain beginning 27' from DER, 125' right of centerline, up to 100' AGL/319' MSL.

Trees and terrain beginning 82' from DER, 100' left of centerline, up to 100' AGL/319' MSL.

BRISTOW, OK

JONES MEML (3F7)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 5 10SEP20 (22139) (FAA)

TAKEOFF OBSTACLE NOTES:

Rwy 18, electrical system 16' from DER, 486' right of centerline, 35' AGL/887' MSL.

Terrain 37' from DER, 405' left of centerline, 871' MSL.

Terrain 66' from DER, 249' left of centerline, 874' MSL.

Trees beginning 191' from DER, 486' left of centerline, up to 28' AGL/890' MSL.

Trees beginning 232' from DER, 559' right of centerline, up to 47' AGL/903' MSL.

Trees beginning 312' from DER, 339' left of centerline, up to 36' AGL/899' MSL.

Trees beginning 384' from DER, 309' left of centerline, up to 41' AGL/904' MSL.

Tree, electrical system beginning 391' from DER, 483' right of centerline, up to 44' AGL/907' MSL.

Tree 450' from DER, 572' right of centerline, 44' AGL/909' MSL.

Trees beginning 509' from DER, 560' right of centerline, up to 49' AGL/913' MSL.

Trees beginning 697' from DER, 574' right of centerline, up to 42' AGL/915' MSL.

Tree 725' from DER, 638' right of centerline, 43' AGL/919' MSL.

Trees, electrical system, vehicles on road, buildings, pole beginning 773' from DER, 462' right of centerline, up to 42' AGL/920' MSL.

Trees, electrical system beginning 807' from DER, 115' left of centerline, up to 58' AGL/905' MSL.

Trees beginning 1082' from DER, 52' left of centerline, up to 46' AGL/912' MSL.

Electrical system, building beginning 1178' from DER, 732' right of centerline, up to 32' AGL/934' MSL.

Trees, electrical system beginning 1193' from DER, 434' right of centerline, up to 42' AGL/940' MSL.

Electrical system beginning 1227' from DER, 181' left of centerline, up to 53' AGL/918' MSL.

Pole 2879' from DER, 169' left of centerline, 72' AGL/951' MSL.

Pole 2890' from DER, 344' right of centerline, 77' AGL/955' MSL.

Transmission line 2894' from DER, 967' right of centerline, 70' AGL/960' MSL.

Poles beginning 2897' from DER, 809' right of centerline, up to 78' AGL/964' MSL.

Rwy 36, vehicles on road 35' from DER, 465' left of centerline, 807' MSL.

Tree, electrical system beginning 190' from DER, 492' left of centerline, up to 46' AGL/833' MSL.

Trees, electrical system beginning 238' from DER, 304' left of centerline, up to 51' AGL/839' MSL.

Electrical system 311' from DER, 314' right of centerline, 28' AGL/819' MSL.

Electrical system beginning 411' from DER, 255' right of centerline, up to 35' AGL/834' MSL.

Electrical system beginning 414' from DER, 295' right of centerline, up to 30' AGL/839' MSL.

Electrical system, vehicles on road, trees beginning 421' from DER, 252' right of centerline, up to 57' AGL/847' MSL.

Trees beginning 1012' from DER, 491' right of centerline, up to 72' AGL/849' MSL.

Trees beginning 1068' from DER, 535' right of centerline, up to 73' AGL/851' MSL.

Trees beginning 1143' from DER, 537' right of centerline, up to 75' AGL/853' MSL.

Trees beginning 1338' from DER, 546' right of centerline, up to 83' AGL/860' MSL.

Trees beginning 1446' from DER, 536' right of centerline, up to 85' AGL/863' MSL.

Trees beginning 1500' from DER, 558' right of centerline, up to 88' AGL/865' MSL.


Tree 1692' from DER, 453' left of centerline, 70' AGL/852' MSL.

Trees beginning 2063' from DER, 437' right of centerline, up to 90' AGL/870' MSL.

CON'T


TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)

25051

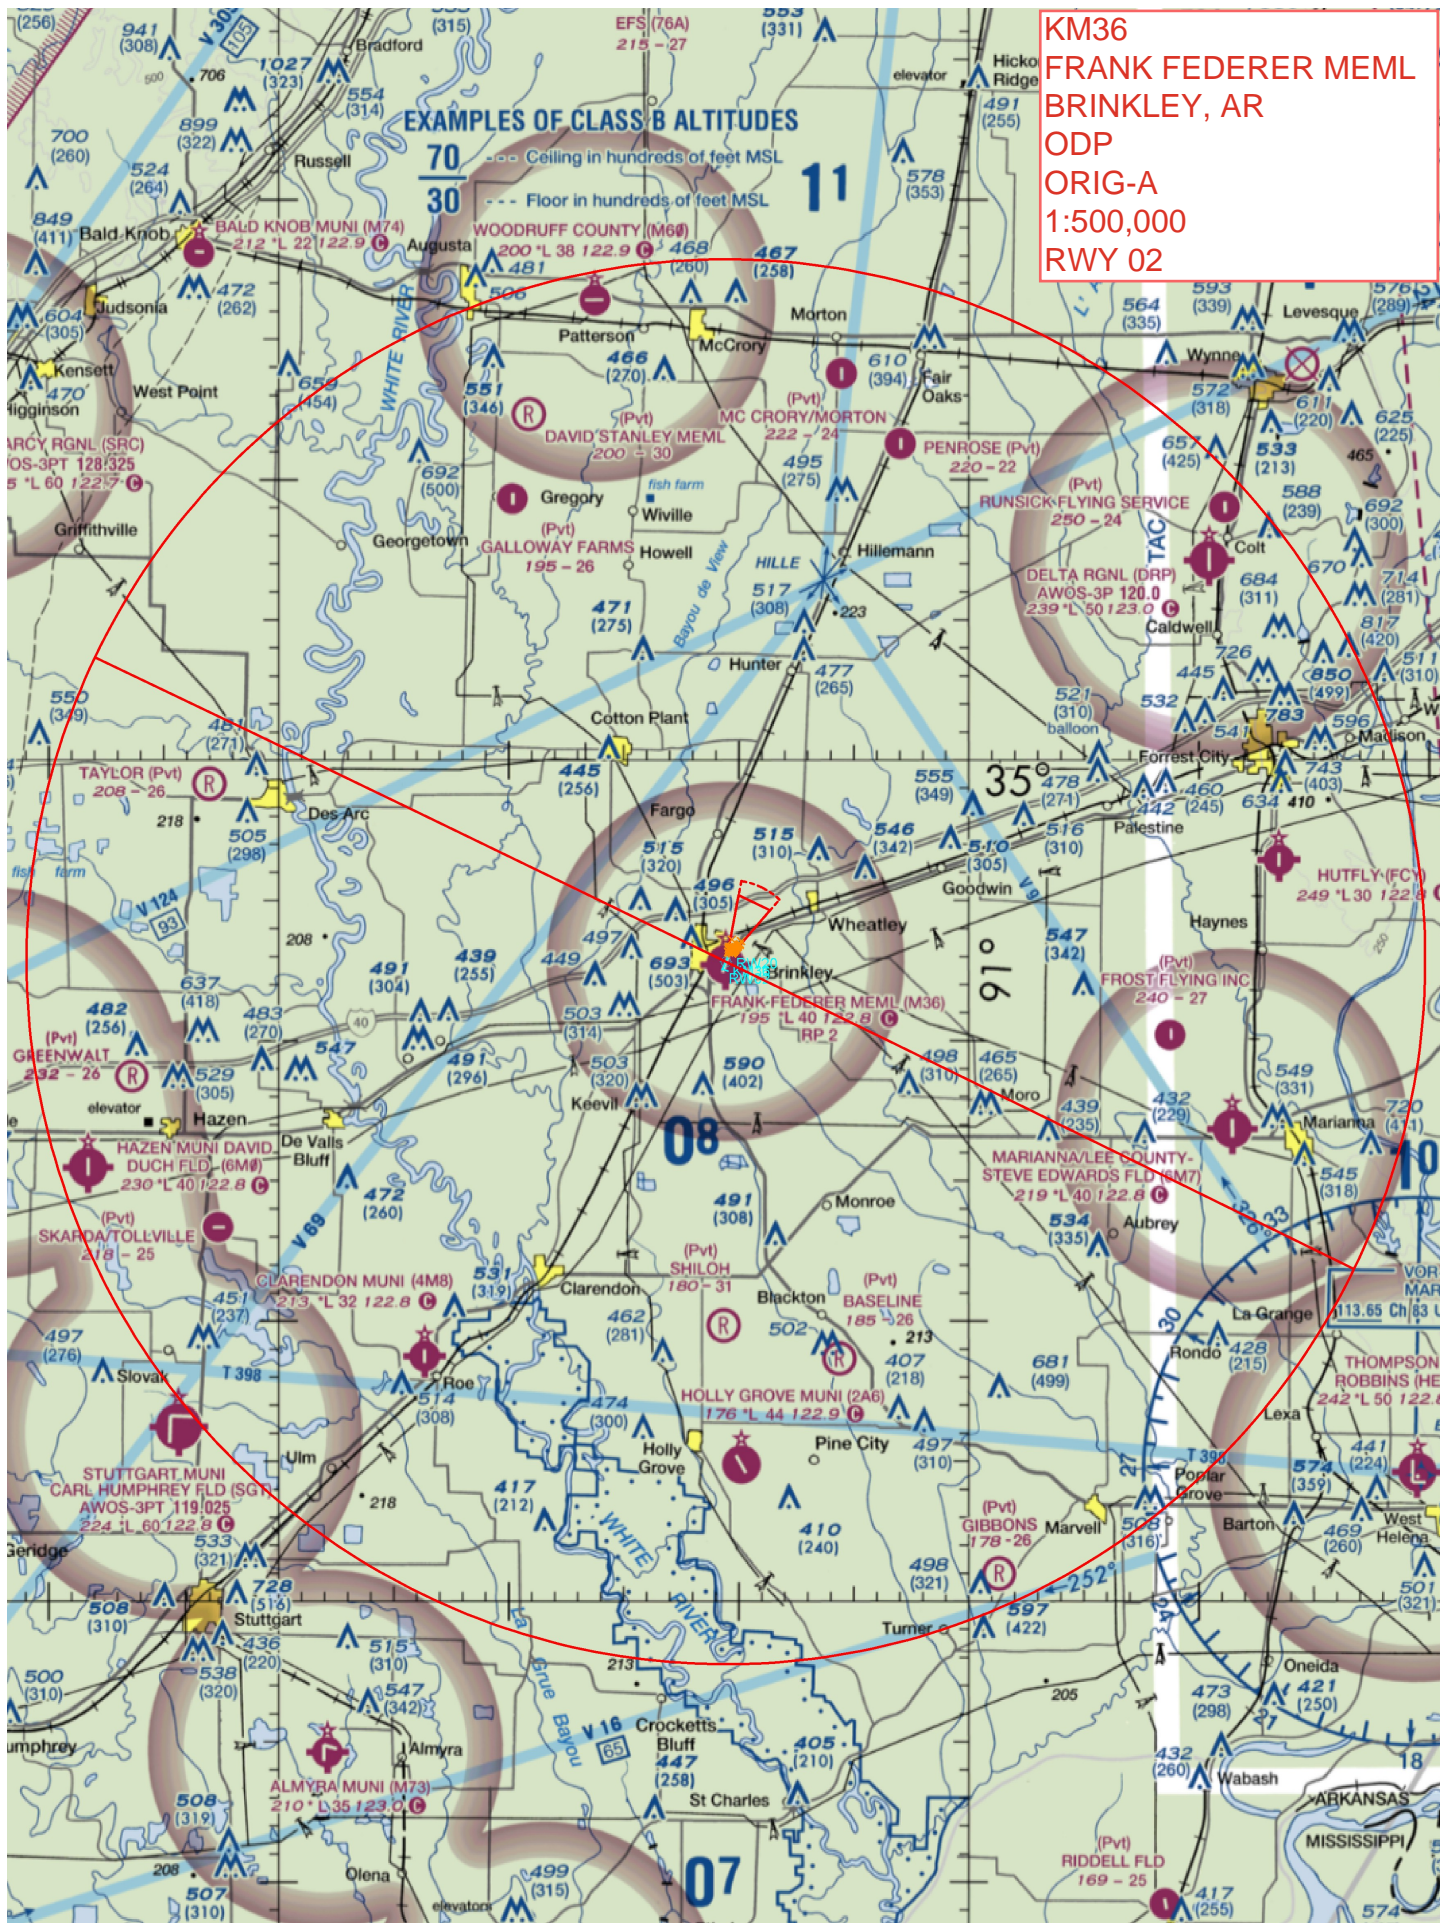



KM36
FRANK FEDERER MEML
BRINKLEY, AR
ODP
ORIG-A
1:100,000
RWY 02

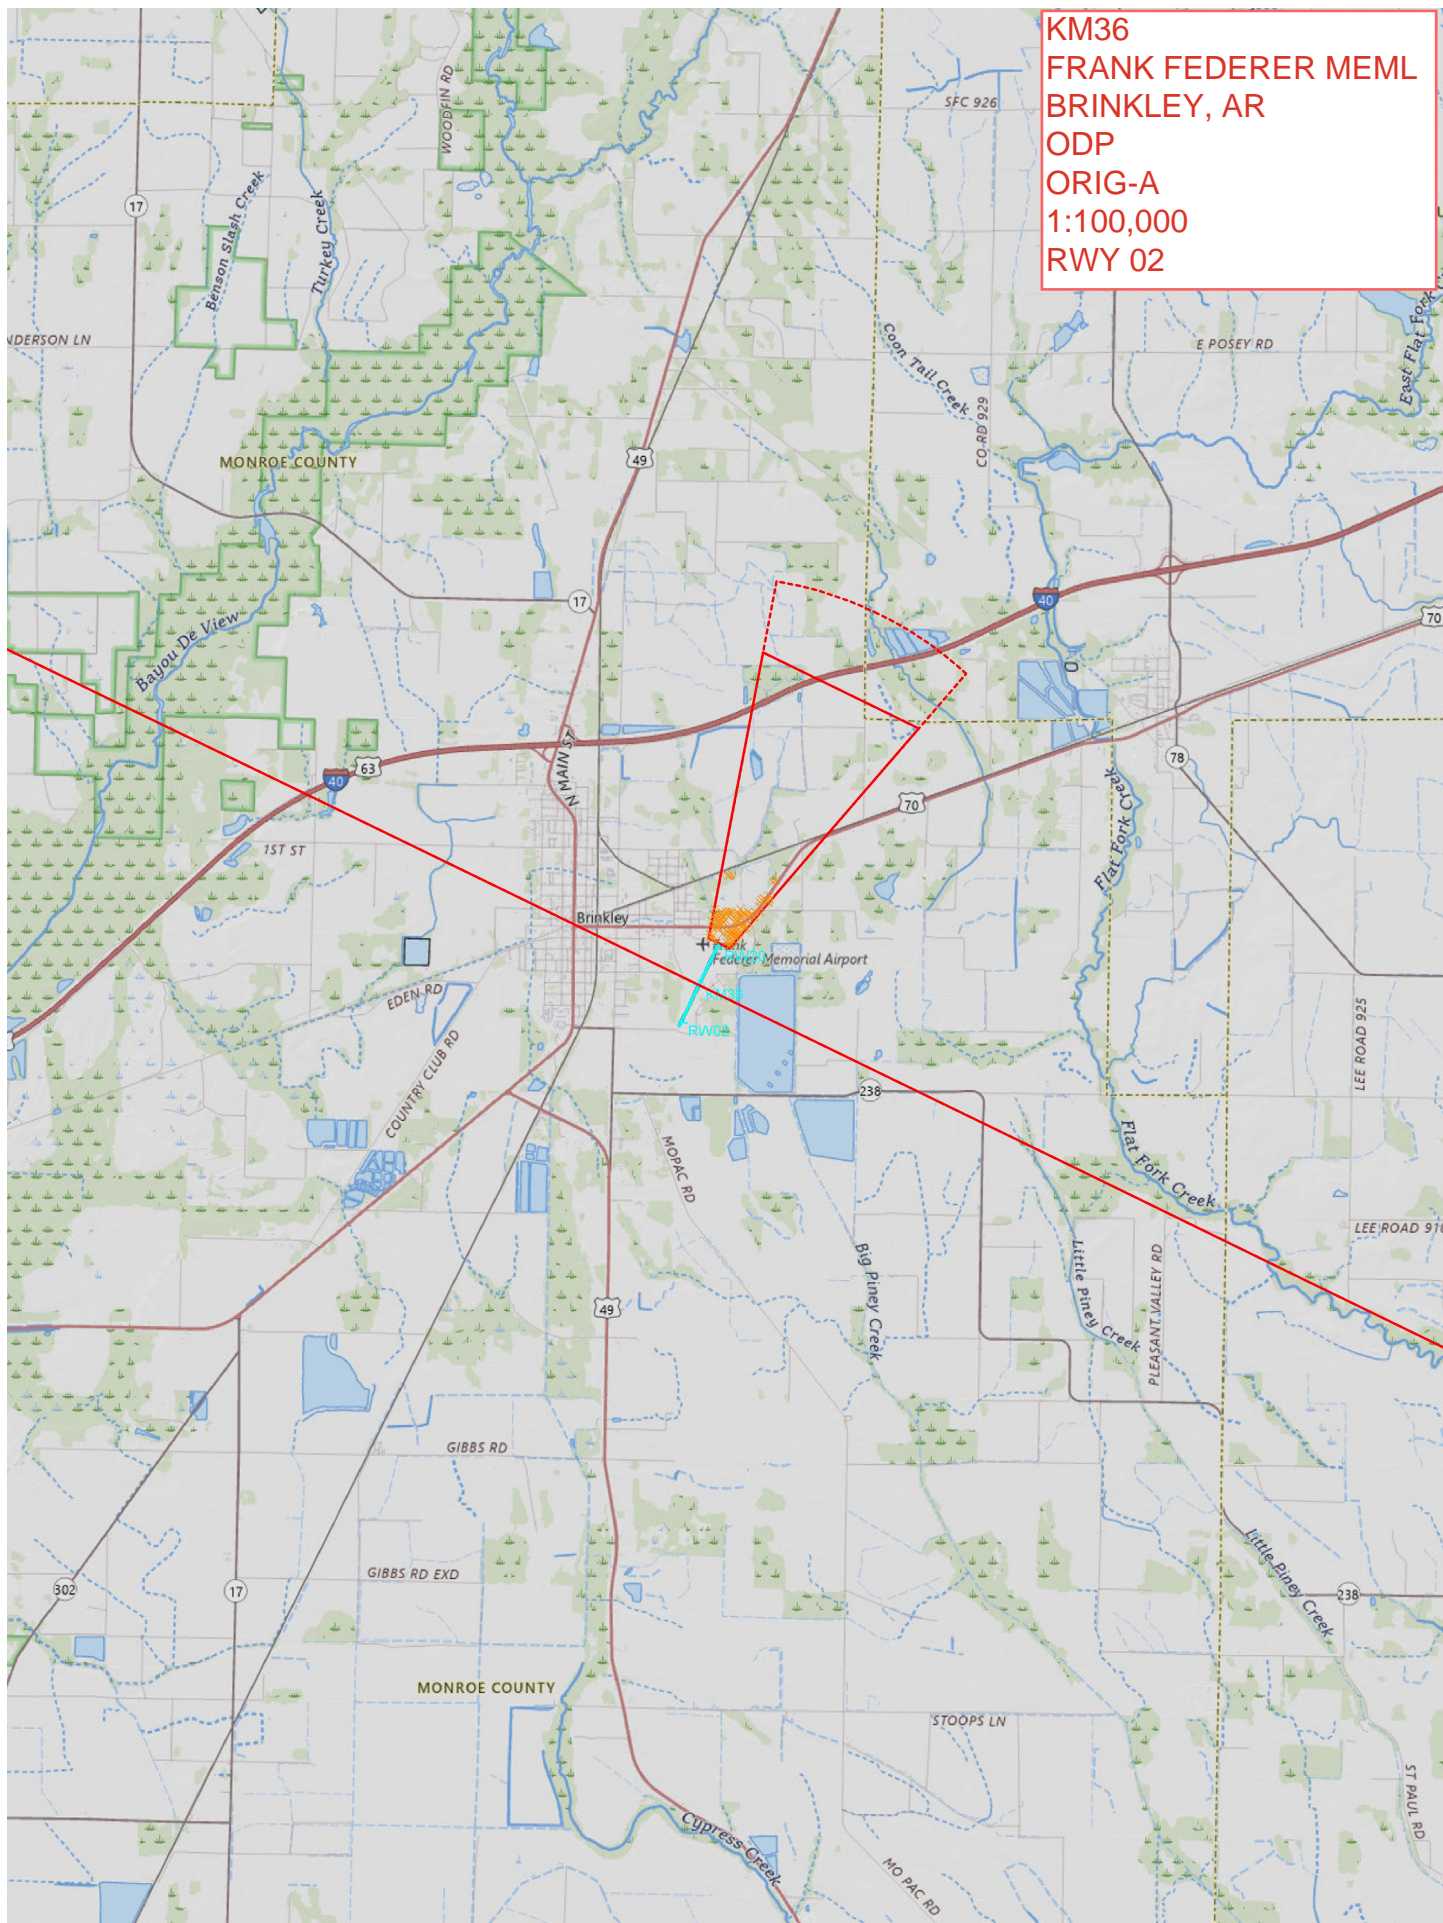

KM36
FRANK FEDERER MEML
BRINKLEY, AR
ODP
ORIG-A
1:100,000
RWY 20

