

Flight Procedures Cover Page	Task Action: FLIGHT CHECK	Task Type: Textual DP	Estimated Chart Date: 01/25/2024	APWS Task ID: 84E111E5265F4A34A405A45ED73DD35E	APWS Project ID: 4E14385D25284BD0B406148953C69986
Procedure: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 4		Enroute: NO	Specialist: Schutrum, Steven		Agreement Number:
Airport ID: KHYA			Airport City: HYANNIS		State: MA
Facility ID:	Facility Type:	Flight Inspection Remark Type: New FC Slot			
<div>Procedure Comments: ACTIVE AIRPORT DATA USED.</div> <div>CANCELS NOTAM FDC 3/4497.</div> <div>CONTACT: MICHAEL GARRITY, AJV-A423, (405) 954 5602.</div> <div><div>Digitally signed by MICHAEL GARRITY Oct 26, 2023</div><div>QUALITY 20 CHECKED</div></div>					

FIPC BASIC FORM						
PROCEDURE: TAKEOFF MINIMUMS AND OBSTACLE DP AMDT 4			AIRPORT NAME: CAPE COD GATEWAY		AIRPORT ID: KHYA	SPECIAL CONTROL NO: YP-10-178-23
FAC ID: KHYA		CITY: HYANNIS			ST: MA	ORIG CHART DATE: 01/25/2024
DFL TYPE: PROC/T	THIRD PARTY: <input type="checkbox"/> YES	EST. TIME ON SITE: 0.4	REIMB. NUMBER:	PTS TASK ID: 84E111E5265F4A34A405A45ED73DD35E		
PREFLIGHT NOTES						
REVIEWER:					DATE:	
COMMENTS:					CHECK ONE: <input type="checkbox"/> FLT CK REQ <input type="checkbox"/> NFCR <input type="checkbox"/> REJECT	
						YES
					CPV COMPLETE? <input checked="" type="checkbox"/> X <input type="checkbox"/> NO	
PROCEDURE RESULTS						
INSPECTION DATE: 10/24/2023	CREW #: VN137	N #: N68	INSTRUMENT PROCEDURE STATUS: <input checked="" type="checkbox"/> SAT <input type="checkbox"/> SAT W/CHANGES <input type="checkbox"/> UNSAT		ARINC CODING: <input type="checkbox"/> SAT <input type="checkbox"/> SAT/GOLD <input type="checkbox"/> UNSAT	
FLIGHT INSPECTOR SIGNATURE: bob s pressler @ 10/24/2023 15:33			PRINTED NAME: PRESSLER, ROBERT STEPHEN			NOTAM INITIATED? <input type="checkbox"/> YES <input checked="" type="checkbox"/> NO
FLIGHT INSPECTOR REMARKS: SAT						
IN-FLIGHT OBSTACLE REPORT						
OBSTRUCTION ID #:	COORDINATES OR LOCATION:	GNSS ALTITUDE (MSL):	BAROMETRIC ALTITUDE (MSL):	HEIGHT ABOVE GROUND LEVEL:		



23250

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)



HOULTON, ME (CON'T)

HOULTON INTL (HUL) (CON'T)

Rwy 19, sign and terrain beginning 19' from DER, 300' left of centerline, up to 481' MSL.

Tree 31' from DER, 405' right of centerline, 508' MSL.

Trees beginning 149' from DER, 281' right of centerline, up to 517' MSL.

Terrain 445' from DER, 471' left of centerline, 485' MSL.

Fence 641' from DER, 500' left of centerline, 492' MSL.

Traverse way 764' from DER, 605' left of centerline, 15' AGL/504' MSL.

Traverse ways beginning 903' from DER, 600' left of centerline, up to 15' AGL/506' MSL.

Tree 2407' from DER, 501' right of centerline, 544' MSL.

Trees beginning 2423' from DER, 413' right of centerline, up to 548' MSL.

Trees beginning 2424' from DER, 347' left of centerline, up to 582' MSL.

Trees beginning 2898' from DER, 133' right of centerline, up to 75' AGL/562' MSL.

Tree 3223' from DER, 468' left of centerline, 626' MSL.

Tree 3358' from DER, 1015' left of centerline, 673' MSL.

Trees beginning 3838' from DER, 273' left of centerline, up to 703' MSL.

Trees beginning 4177' from DER, 1150' left of centerline, up to 760' MSL.

Trees beginning 4469' from DER, 133' left of centerline, up to 72' AGL/829' MSL.

Tree 5117' from DER, 36' right of centerline, 608' MSL.

Tree 1 NM from DER, 13' right of centerline, 641' MSL.

Trees beginning 1.6 NM from DER, 2274' right of centerline, up to 772' MSL.

Tree 1.7 NM from DER, 2831' right of centerline, 792' MSL.

Tree 1.8 NM from DER, 2939' right of centerline, 794' MSL.

Trees beginning 1.9 NM from DER, 1822' right of centerline, up to 77' AGL/798' MSL.

Trees beginning 2 NM from DER, 1571' right of centerline, up to 823' MSL.

Trees beginning 2.1 NM from DER, 1607' right of centerline, up to 75' AGL/873' MSL.

Trees beginning 2.2 NM from DER, 2186' right of centerline, up to 61' AGL/880' MSL.

Tree 2.4 NM from DER, 4335' left of centerline, 851' MSL.

Tree 2.5 NM from DER, 2356' left of centerline, 875' MSL.

Rwy 23, electrical system 54' from DER, 210' left of centerline, 485' MSL.

Trees beginning 132' from DER, 486' left of centerline, up to 512' MSL.

Trees beginning 264' from DER, 267' left of centerline, up to 522' MSL.

Tree 639' from DER, 449' right of centerline, 501' MSL.

Trees beginning 644' from DER, 110' right of centerline, up to 565' MSL.

Trees beginning 651' from DER, 372' left of centerline, up to 526' MSL.

Trees beginning 721' from DER, 2' left of centerline, up to 544' MSL.

Trees and terrain beginning 883' from DER, 1' right of centerline, up to 569' MSL.

Trees and terrain beginning 1230' from DER, on centerline, up to 594' MSL.

Trees beginning 1270' from DER, 1' left of centerline, up to 558' MSL.

Trees beginning 1536' from DER, 5' right of centerline, up to 601' MSL.

Trees beginning 1725' from DER, 7' right of centerline, up to 606' MSL.

Trees and poles beginning 1740' from DER, 3' left of centerline, up to 572' MSL.

Trees, antenna, buildings, tank, stack, poles beginning 2253' from DER, 1' right of centerline, up to 622' MSL.

Trees and poles beginning 2561' from DER, 1' left of centerline, up to 67' AGL/585' MSL.

Trees beginning 3318' from DER, 1' left of centerline, up to 70' AGL/602' MSL.

Tree 4535' from DER, 680' left of centerline, 605' MSL.

Tree 4892' from DER, 1324' left of centerline, 609' MSL.

Trees beginning 4914' from DER, 1105' left of centerline, up to 610' MSL.

Tree 4986' from DER, 1198' left of centerline, 612' MSL.

Tree 5002' from DER, 1311' left of centerline, 619' MSL.

Trees beginning 5010' from DER, 1018' left of centerline, up to 621' MSL.

Trees beginning 5070' from DER, 1043' left of centerline, up to 629' MSL.

Trees beginning 5145' from DER, 1153' left of centerline, up to 634' MSL.

Trees beginning 5251' from DER, 975' left of centerline, up to 644' MSL.

Trees beginning 5356' from DER, 1019' left of centerline, up to 647' MSL.

Trees beginning 5609' from DER, 950' left of centerline, up to 663' MSL.

Trees beginning 5728' from DER, 1386' left of centerline, up to 674' MSL.

Trees beginning 5917' from DER, 1819' left of centerline, up to 690' MSL.

Trees beginning 5972' from DER, 1160' left of centerline, up to 691' MSL.

Trees beginning 1 NM from DER, 1562' left of centerline, up to 729' MSL.

Trees beginning 1.1 NM from DER, 1541' left of centerline, up to 759' MSL.

OLD

07 SEP 2023 to 05 OCT 2023

07 SEP 2023 to 05 OCT 2023

HYANNIS, MA

CAPE COD GATEWAY (HYA)

TAKEOFF MINIMUMS AND (OBSTACLE) DEPARTURE PROCEDURES

AMDT 3A 25SEP08 (20366) (FAA)

TAKEOFF MINIMUMS:

Rwy 33, 300-1 or std. w/ min. climb of 354' per NM to 300.

DEPARTURE PROCEDURE:

Rwys 24,33, climb runway heading to 700 before proceeding on course.

TAKEOFF OBSTACLE NOTES:

Rwy 33, pole 3961' from DER, 1531' right of centerline, 97' AGL/235' MSL.




23250

TAKEOFF MINIMUMS, (OBSTACLE) DEPARTURE PROCEDURES, AND DIVERSE VECTOR AREA (RADAR VECTORS)




NE-1

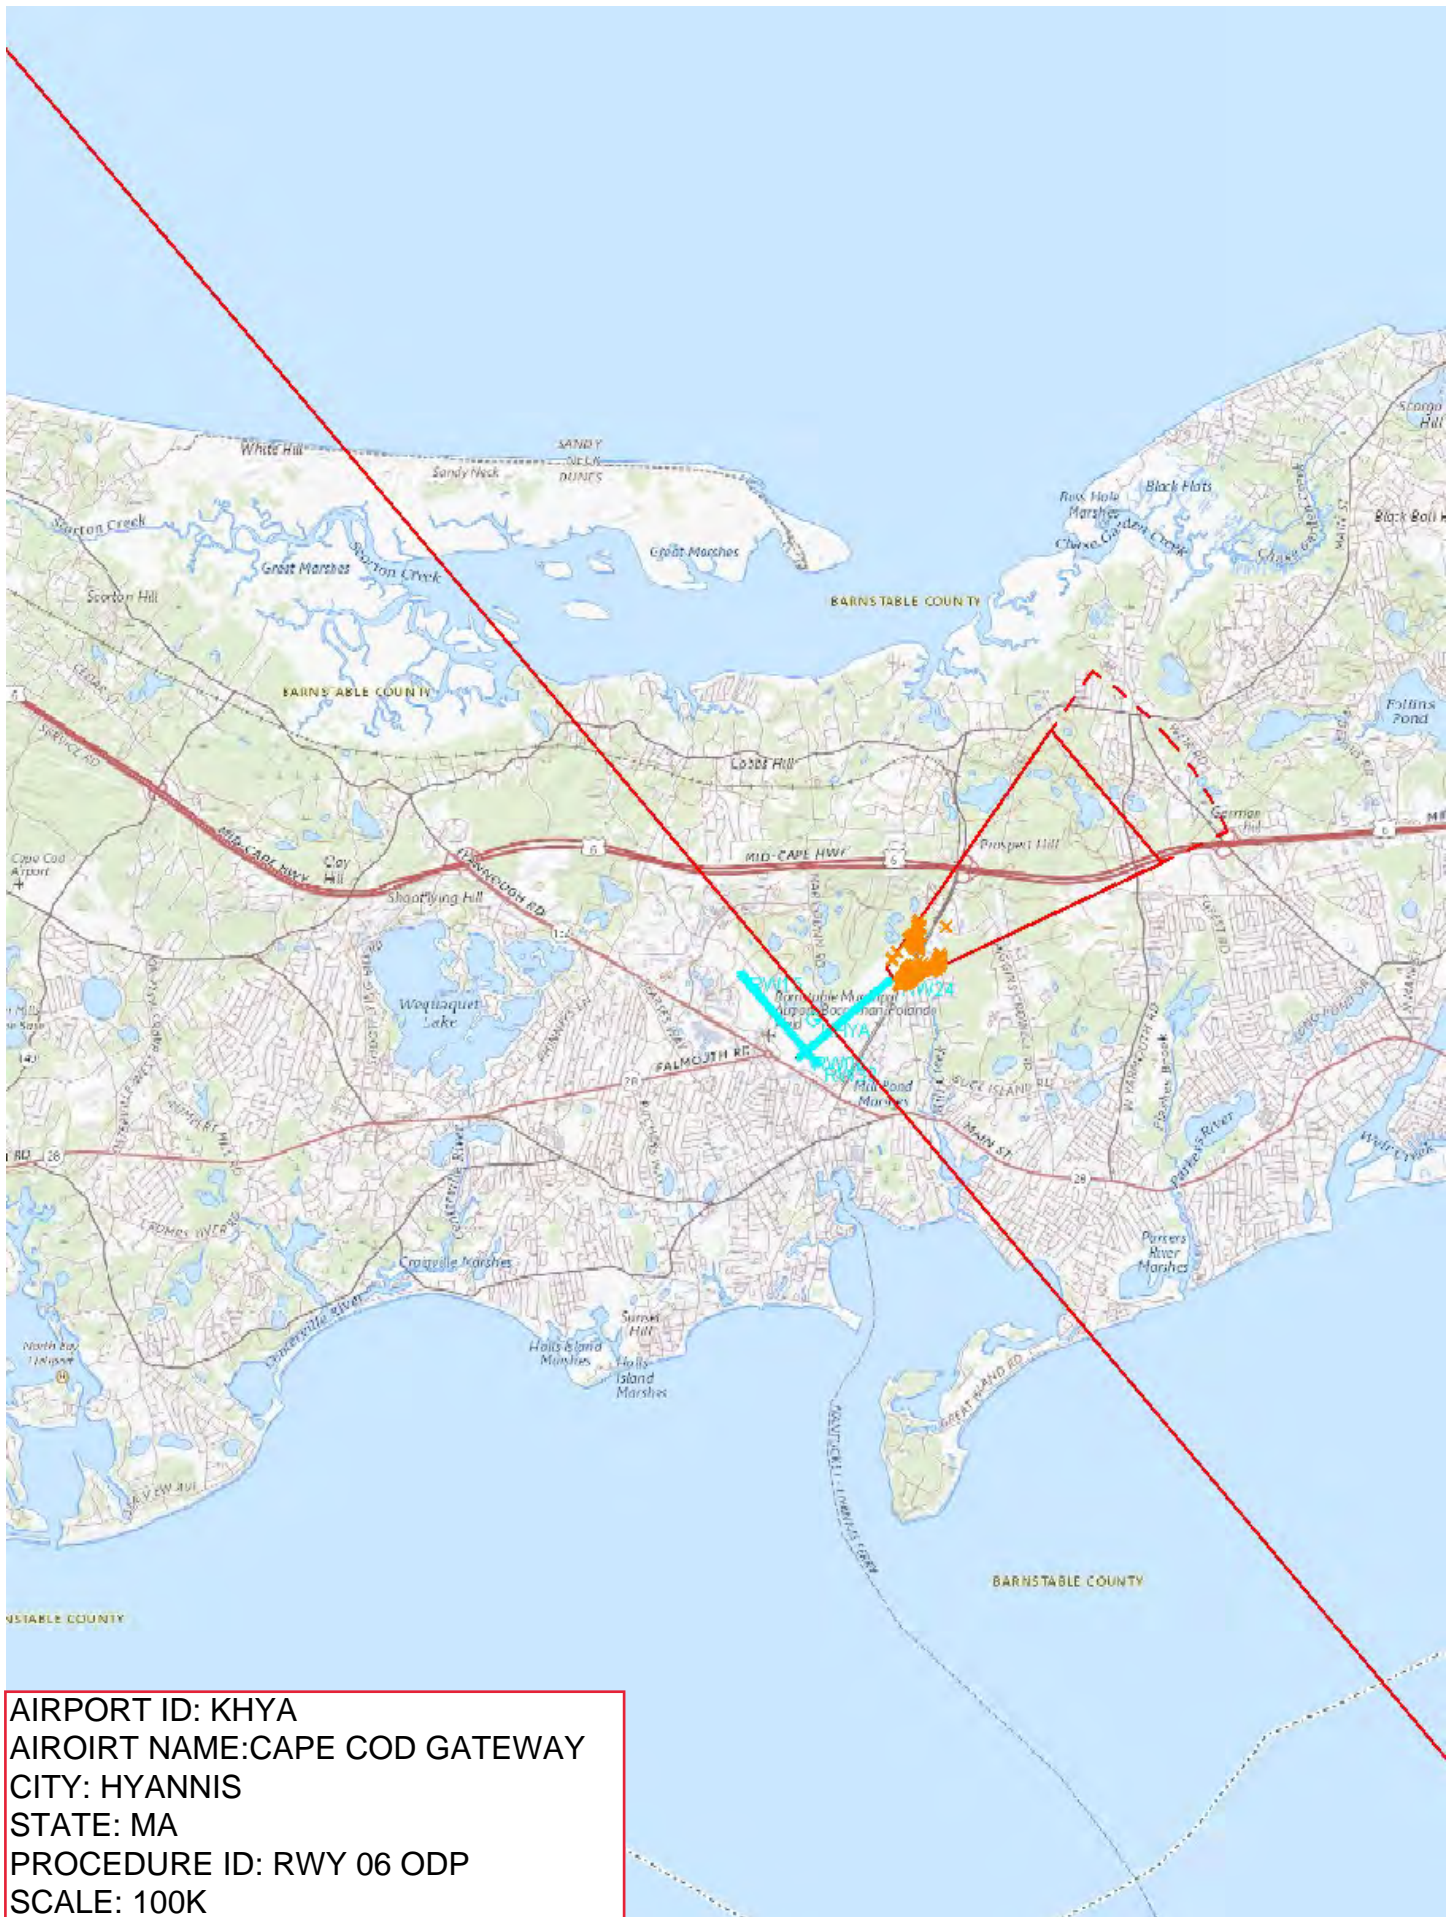

AIRPORT ID: KHYA
AIRPORT NAME: CAPE COD GATEWAY
CITY: HYANNIS
STATE: MA
PROCEDURE ID: RWY 06 ODP
SCALE: 100K



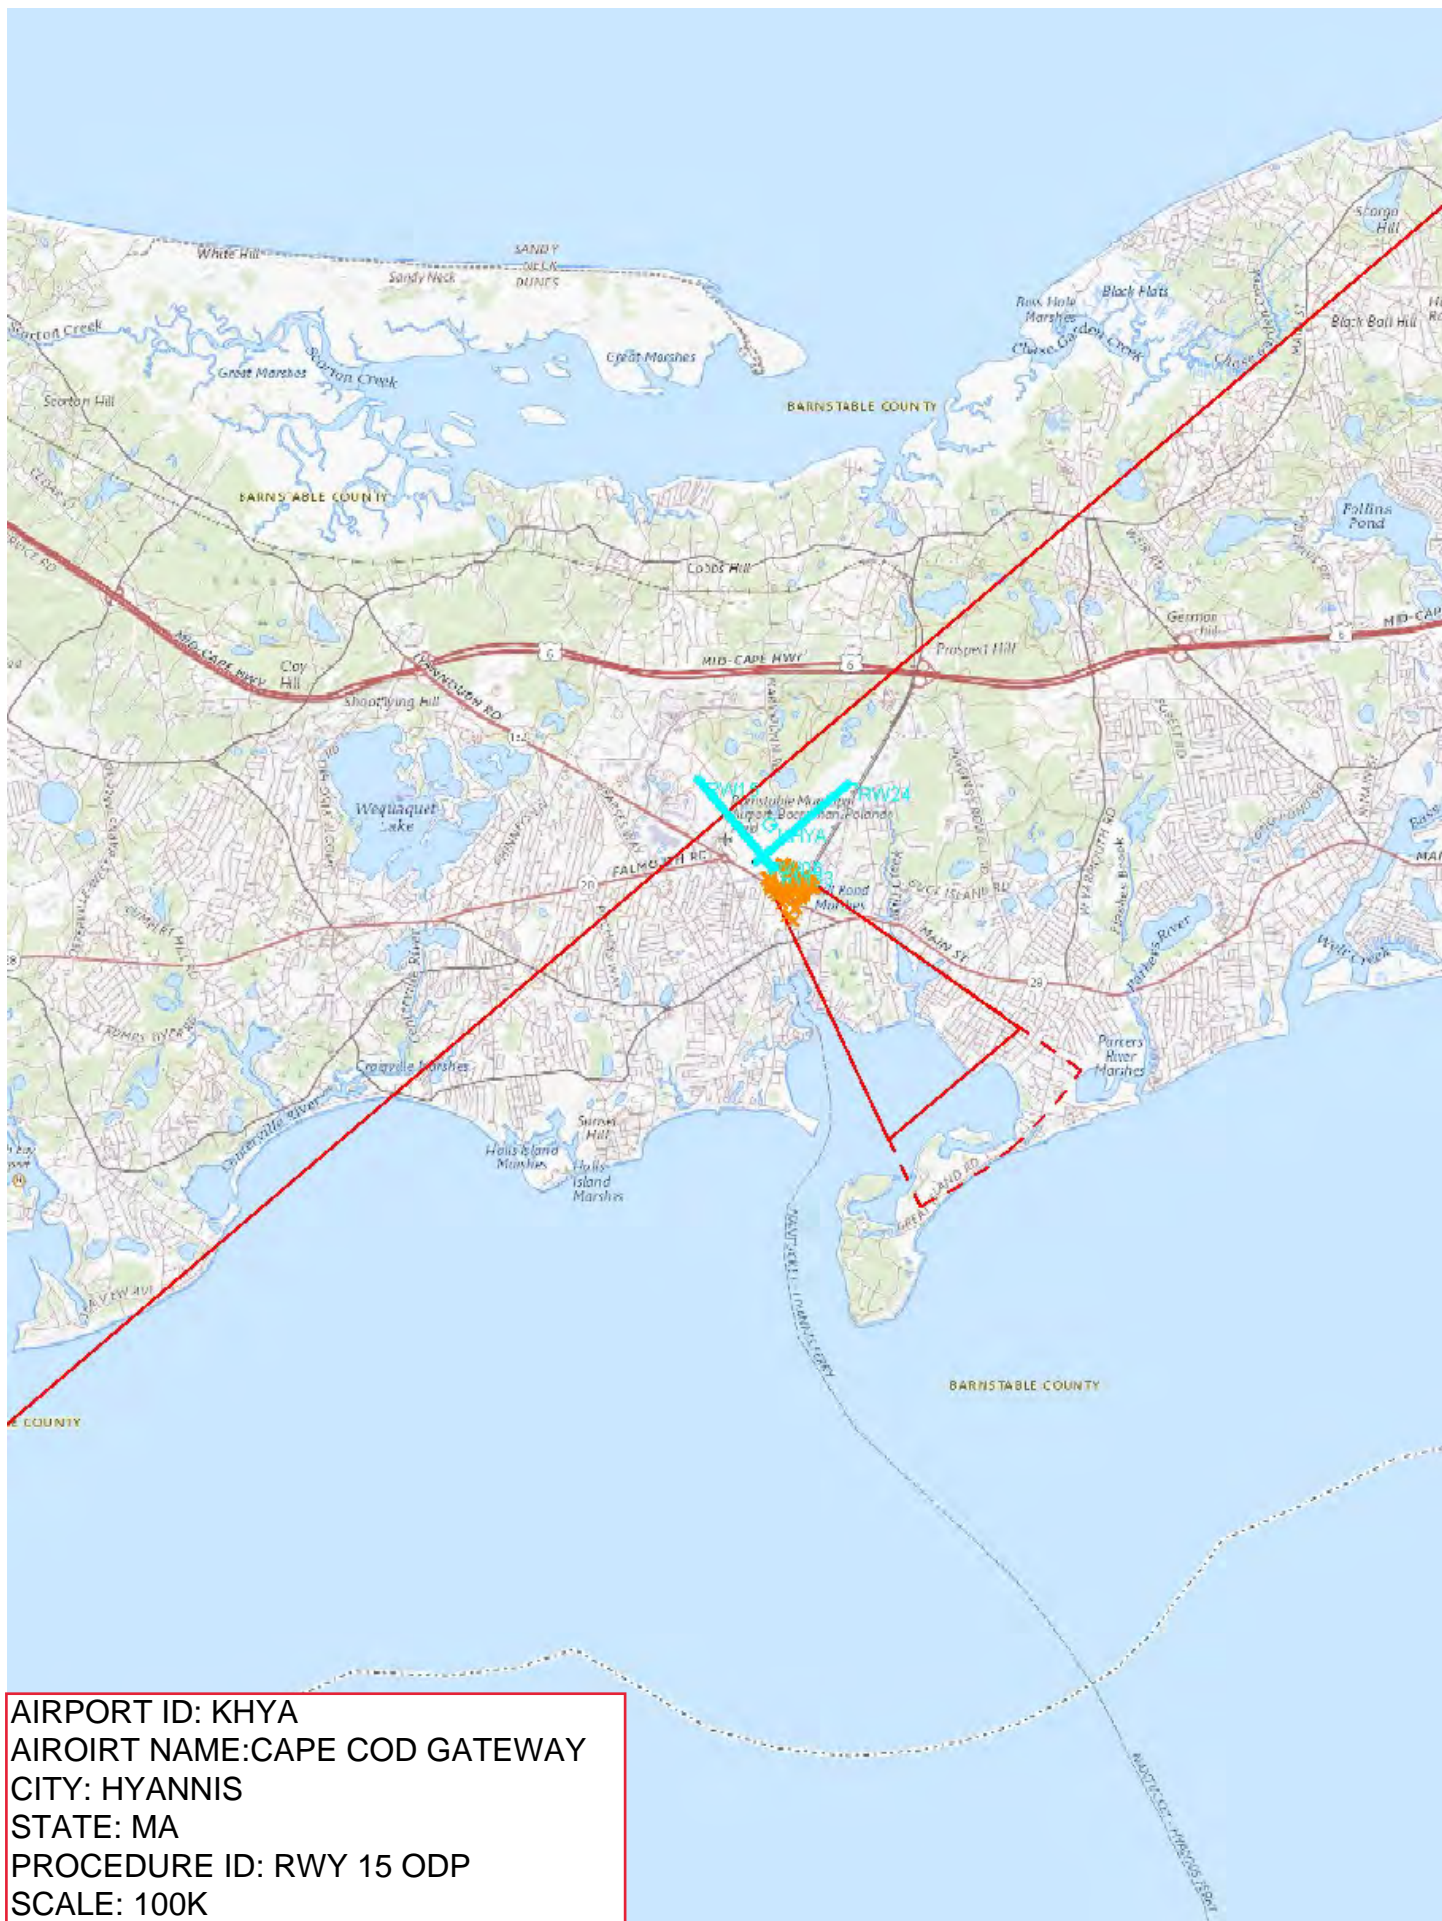

AIRPORT ID: KHya
AIROIRT NAME:CAPE COD GATEWAY
CITY: HYANNIS
STATE: MA
PROCEDURE ID: RWY 15 ODP
SCALE: 100K



