| Flight Procedure Tracking Form | Action: FLIGHT CHECK | Task Type: DP | Date Open: 02/02/2010 | Task #: 20080727160248 02001 | Request #: 20080727160248 |
|---|---|---|---|---|---|
| Procedure: DP SEBASTIAN FL KX26 ORIG | | Airport ID: KX26 | Airport: SEBASTIAN MUNI | | Reimbursable #: |
| City: SEBASTIAN | ST: FL | GPS #: | | Estimated Chart Date: 04/05/2012 | FICO #: |
| Fac ID: | Fac. Type: ProcT | Specialist: THERON CYRUS | | | |

## Procedure Review

P2

| | Rec'd | Rel'd | Full Name | Comments |
|---|---|---|---|---|
| Lead: | 07/31/2011 | 11/16/2011 | KYLE THOMPSON | |
| QA: | 11/16/2011 | 11/23/2011 | STEVEN SZUKALA | |
| Liaison: | 11/23/2011 | | Terrell | |

**Procedure Comments:** ENROUTE **Remark Type:** INFORMATION

pkg 3 of 3

SEBASTIAN, F_ SEBASTIAN MUNI (KX26) TAKEOFF DEP/MINS, ORIG ENROUTE-NO FC: 2.21.12 PUB: 4 5.12

ATTACHED FORMS: 8260-15A.

CONTACT: DON SMITH, JILL OLSON, AJV-352 LEADS, 405.954.1036/0414:




| Airport ID: | KX26 |
|---|---|
| Apt Name: | SEBASTIAN MUNI |
| City: | SEBASTIAN |
| State: | FL |
| Scale: | 1:500,000 |
| Proc ID: | DP RWY 4 |

FM 15A

| No | SEGMENT | OBSTRUCTION | ELEV |
|---|---|---|---|
| 1 | ICA | TREE | 125 |
| | DIVERSE A/B | ASC | |
| | | | |
| | | | |
| | | | |

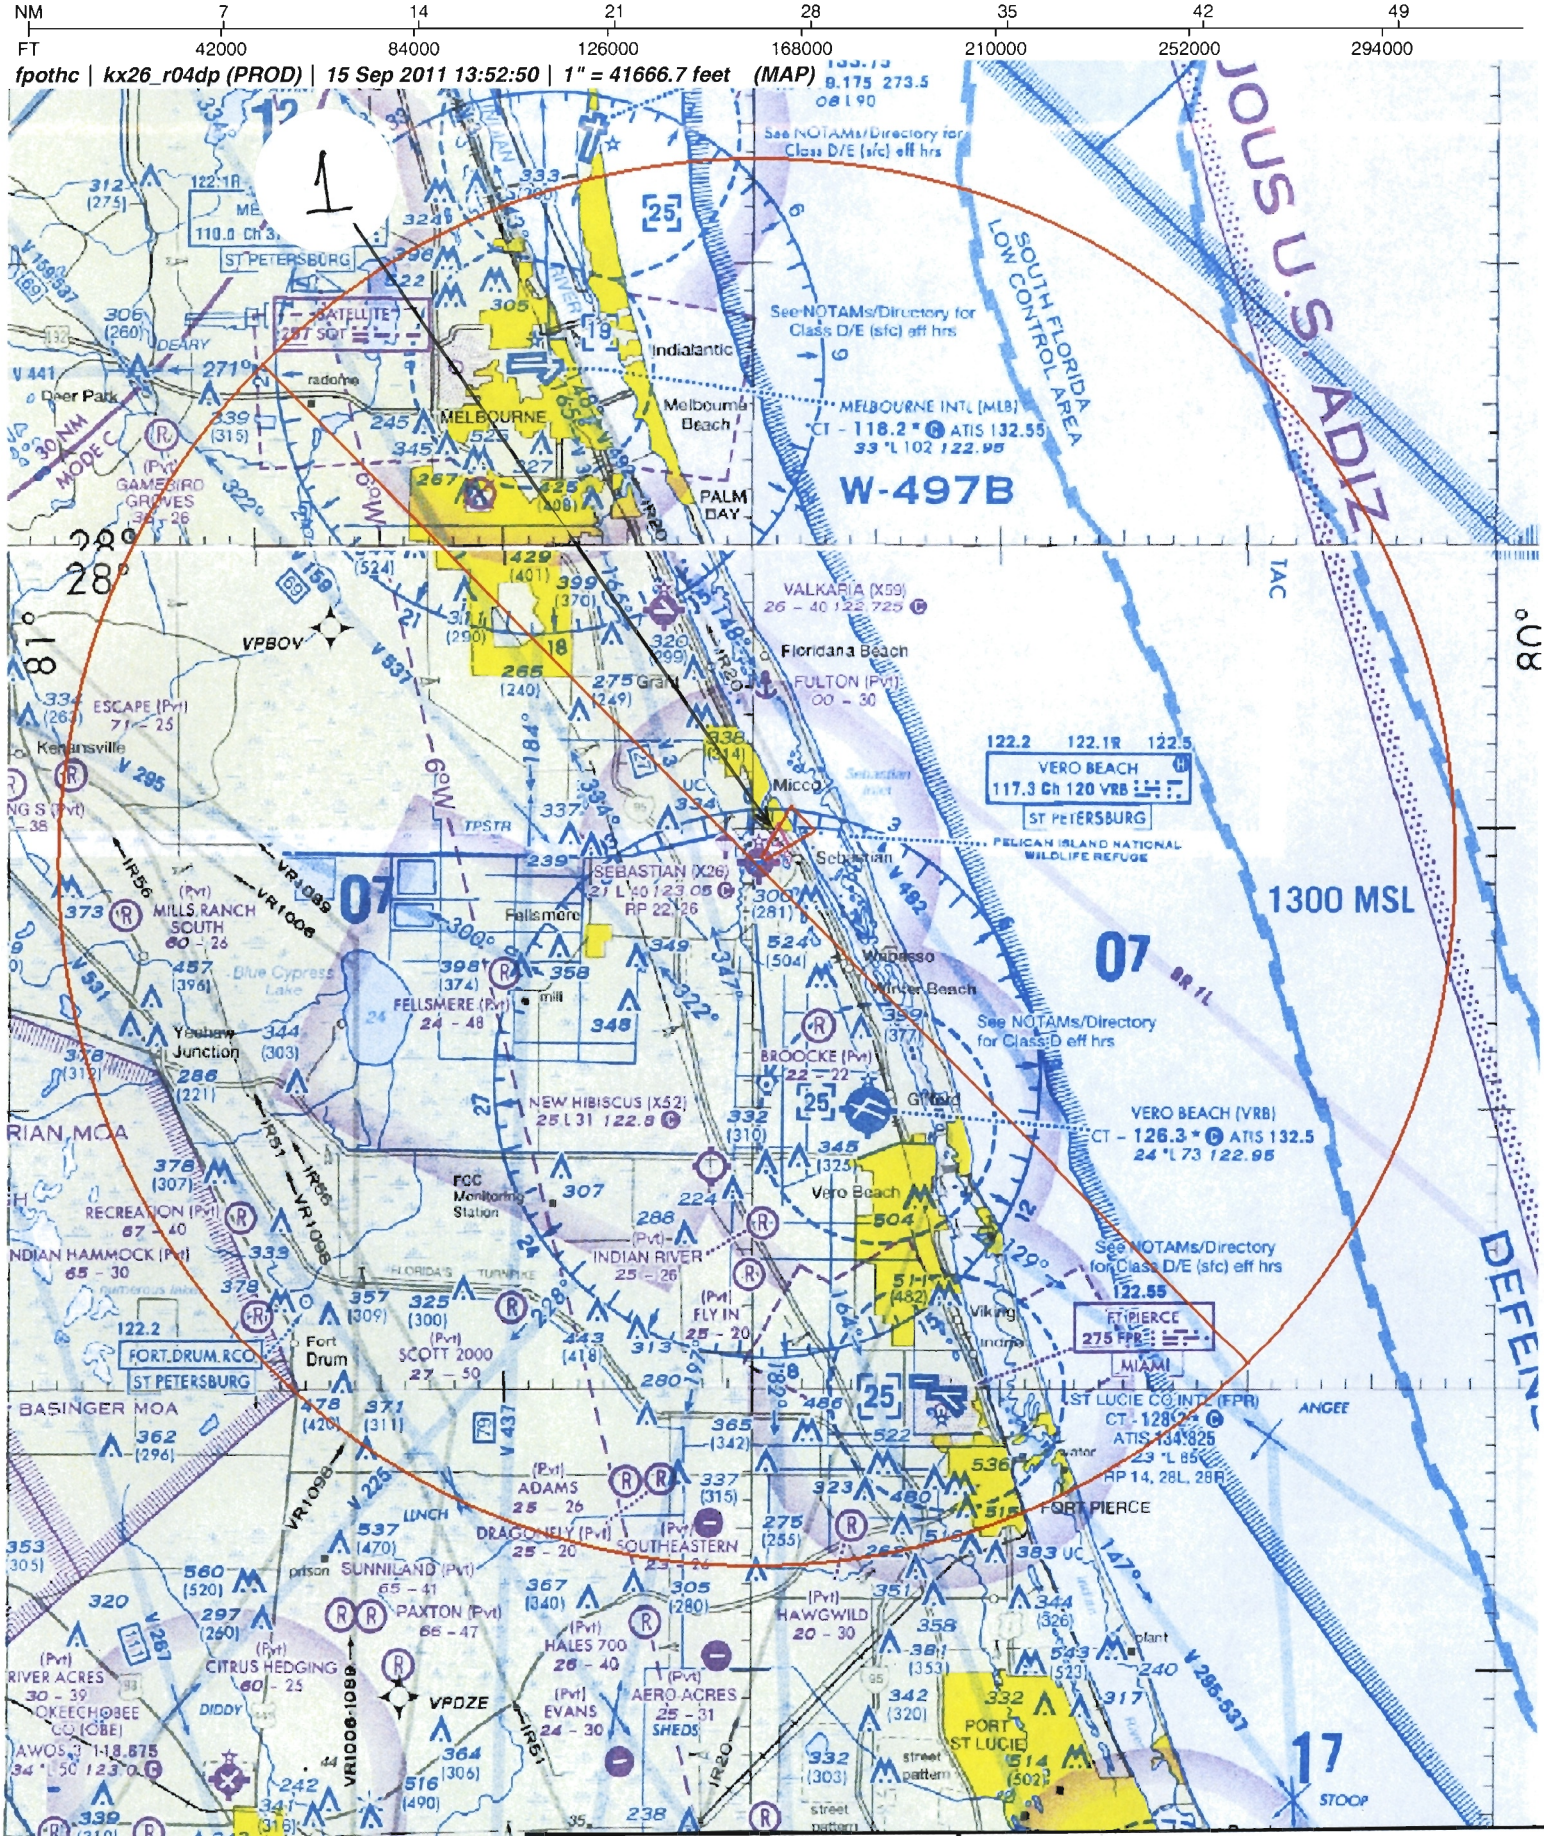


| Airport ID: | KX26 | FM 15A | | | |
|---|---|---|---|---|---|
| Apt Name: | SEBASTIAN MUNI | No | SEGMENT | OBSTRUCTION | ELEV |
| City: | SEBASTIAN | 1 | ICA: CG/CTA /CEIL/VIS | TOWER (12-004576) | 198 |
| State: | FL | | DIVERSE A/B | ASC | |
| Scale: | 1:500,000 | | | | |
| Proc ID: | DP RWY 8 | | | | |




| | | FM 15A | | | |
|---|---|---|---|---|---|
| Airport ID: | KX26 | No | SEGMENT | OBSTRUCTION | ELEV |
| Apt Name: | SEBASTIAN MUNI | 1 | ICA | TREE | 124 |
| City: | SEBASTIAN | | DIVERSE A/B | ASC | |
| State: | FL | | | | |
| Scale: | 1:500,000 | | | | |
| Proc ID: | DP RWY 22 | | | | |


NM 7 14 21 28 35 42 49
FT 42000 84000 126000 168000 210000 252000 294000
fpothc | kx26_r26dp (PROD) | 15 Sep 2011 13:42:35 | 1" = 41666.7 feet (MAP)
1
W-497B
SOUTH FLORIDA LOW CONTROL AREA
TAC
1300 MSL
07
25
12
19
18
17
VERO BEACH 117.3 Ch 120 VRB ST PETERSBURG
VERO BEACH (VRB) CT - 126.3 ATIS 132.5 24 L73 122.95
ST LUCIE CO INTL (FPR) CT - 128.2 ATIS 134.825 RP 14, 28L, 28R
MELBOURNE 110.0 Ch 37 MLB ST PETERSBURG
MELBOURNE INTL (MLB) CT - 118.2 ATIS 132.55
FT PIERCE 275 FPR MIAMI
FORT DRUM RCO ST PETERSBURG
SATELLITE 287 SQT
VALKARIA (X59)
NEW HIBISCUS (X52)
SEBASTIAN (X26)
FELLSMERE (Pvt) 24 - 48
INDIAN RIVER 25 - 26
SUNNILAND (Pvt) 65 - 41
PAXTON (Pvt) 66 - 47
SOUTHEASTERN 25 - 20
AERO ACRES 25 - 31
HAWGWILD 20 - 30
HALES 700 26 - 40
ADAMS 25 - 26
DRAGONFLY (Pvt) 25 - 20
SCOTT 2000 27 - 50
FLY IN 25 - 20
BROOCKE (Pvt) 22 - 22
MILLS RANCH SOUTH 60 - 26
ESCAPE (Pvt) 71 - 25
RECREATION (Pvt) 67 - 40
INDIAN HAMMOCK (Pvt) 65 - 30
RIVER ACRES 30 - 39
CITRUS HEDGING 60 - 25
SUNSET STRIP 32 - 50
RIVER OAK (Pvt) 35 - 41
GAMEBIRD GROVES 35 - 26
VPBOV
VPDOZE
BASINGER MOA
MARIAN MOA
PELICAN ISLAND NATIONAL WILDLIFE REFUGE
See NOTAMs/Directory for Class D/E (sfc) eff hrs
See NOTAMs/Directory for Class D eff hrs
See NOTAMs/Directory for Class D/E (sfc) eff hrs 122.55
Melbourne Beach
Indialantic
PALM BAY
Micco
Sebastian
Fellsmere
Wabasso
Winter Beach
Gifford
Vero Beach
Indrio
Viking
Fort Drum
Sherman
Okeechobee
Kenansville
Floridana Beach
Grant
Yeehaw Junction
Blue Cypress Lake
FORT PIERCE
PORT ST LUCIE
ANGEE
DIDDY
LUNCH
FCC Monitoring Station
prison
plant
water
street
radome
Deer Park
Airport ID: KX26
Apt Name: SEBASTIAN MUNI
City: SEBASTIAN
State: FL
Scale: 1:500,000
Proc ID: DP RWY 26
FM 15A
No SEGMENT OBSTRUCTION ELEV
1 ICA TREE 125
DIVERSE A/B ASC

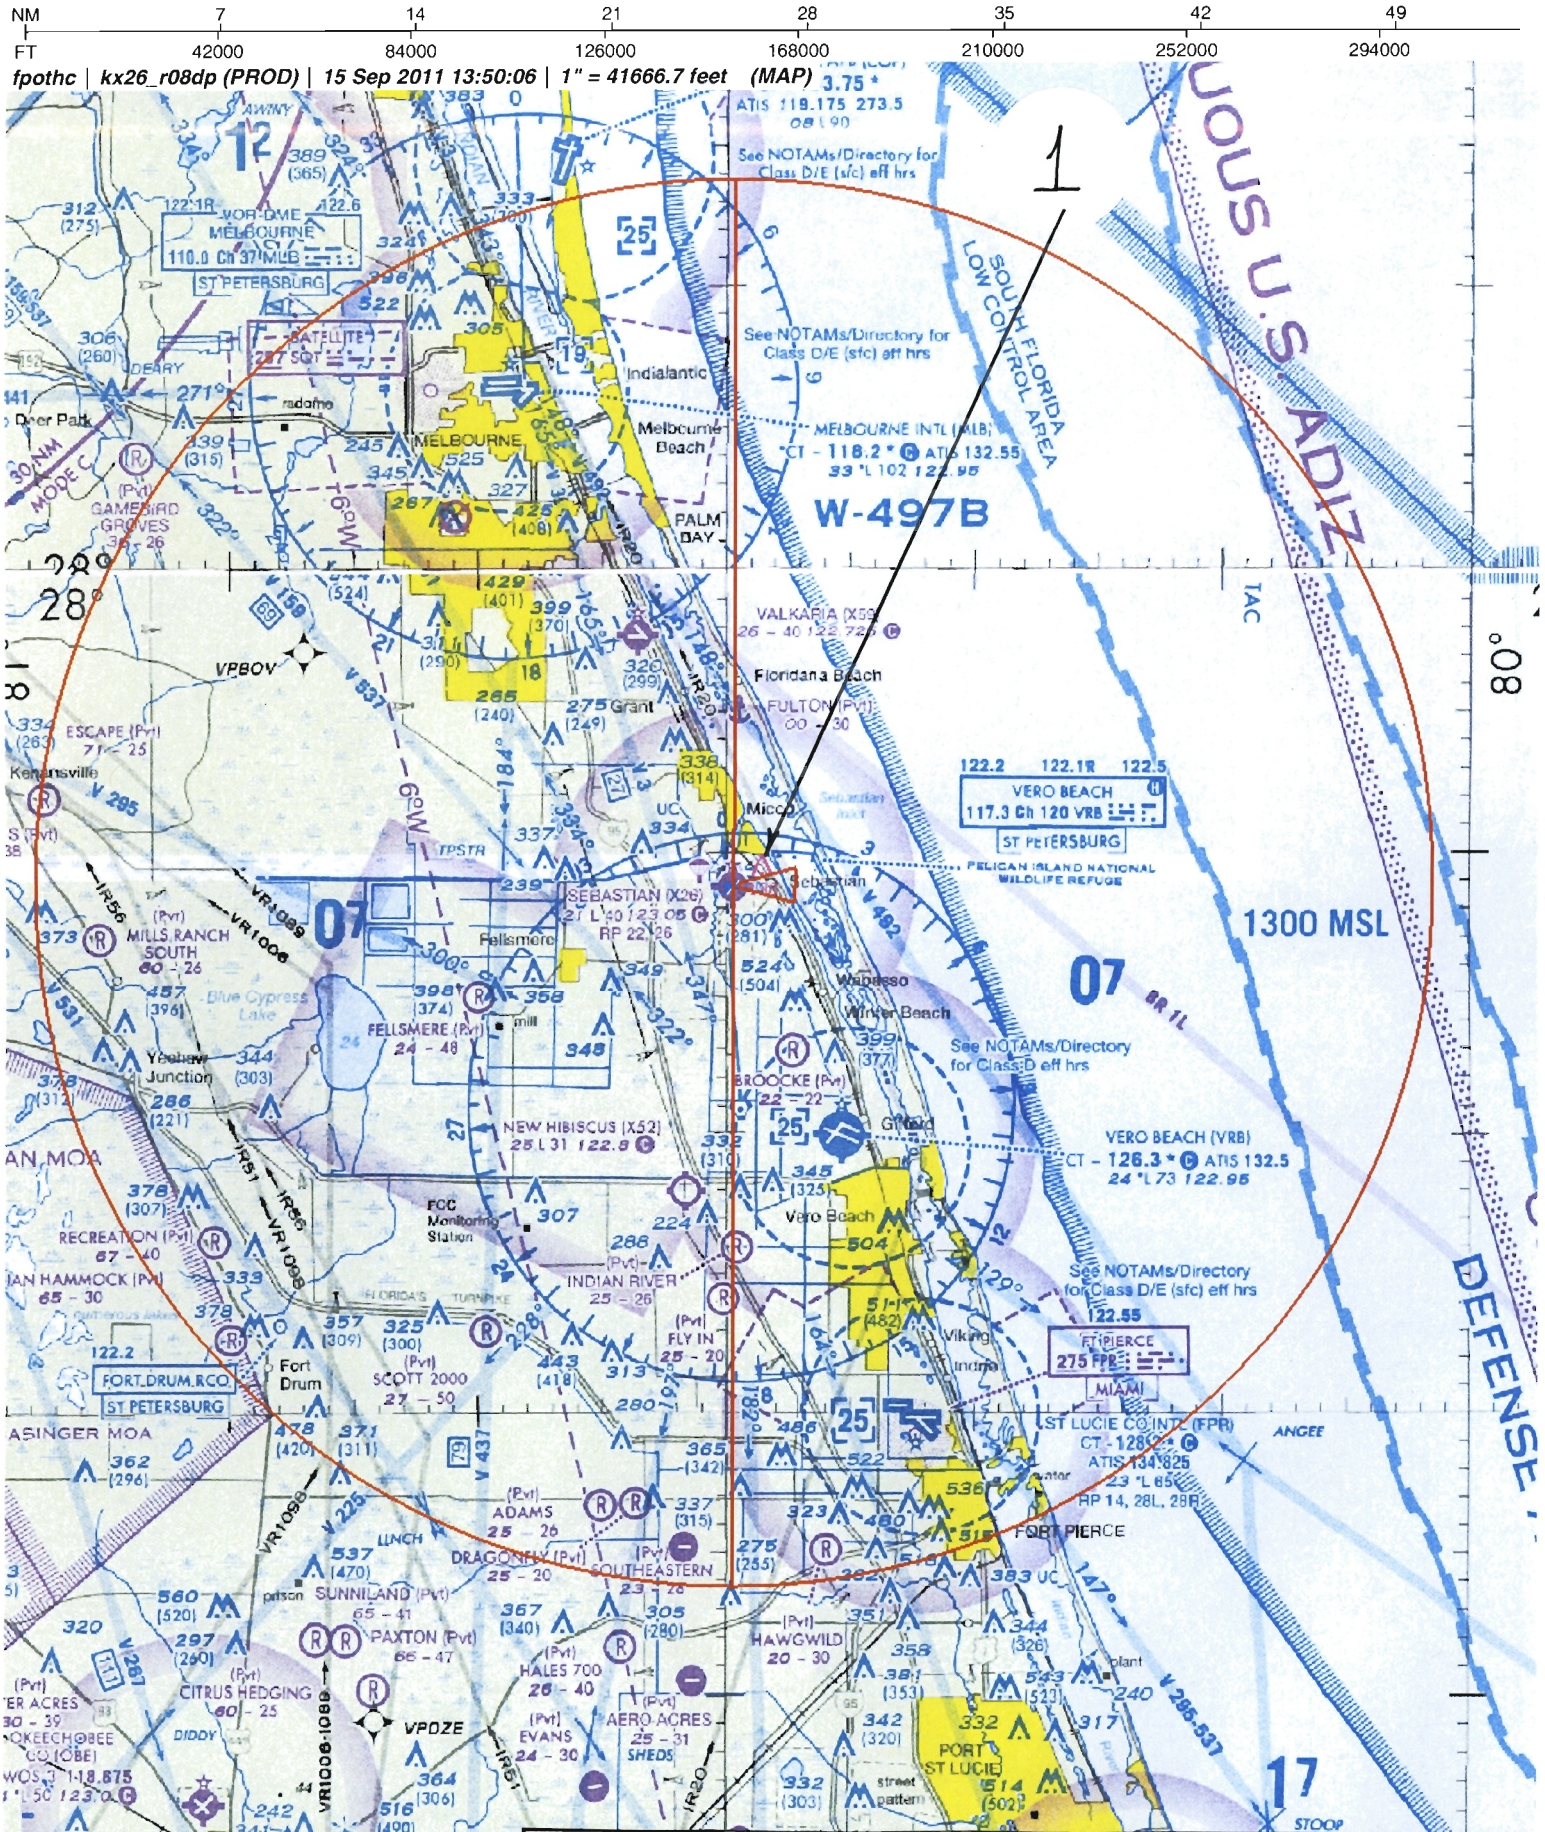


| Airport ID: | KX26 |
|---|---|
| Apt Name: | SEBASTIAN MUNI |
| City: | SEBASTIAN |
| State: | FL |
| Scale: | 1:100,000 |
| Proc ID: | DP RWY 26 |

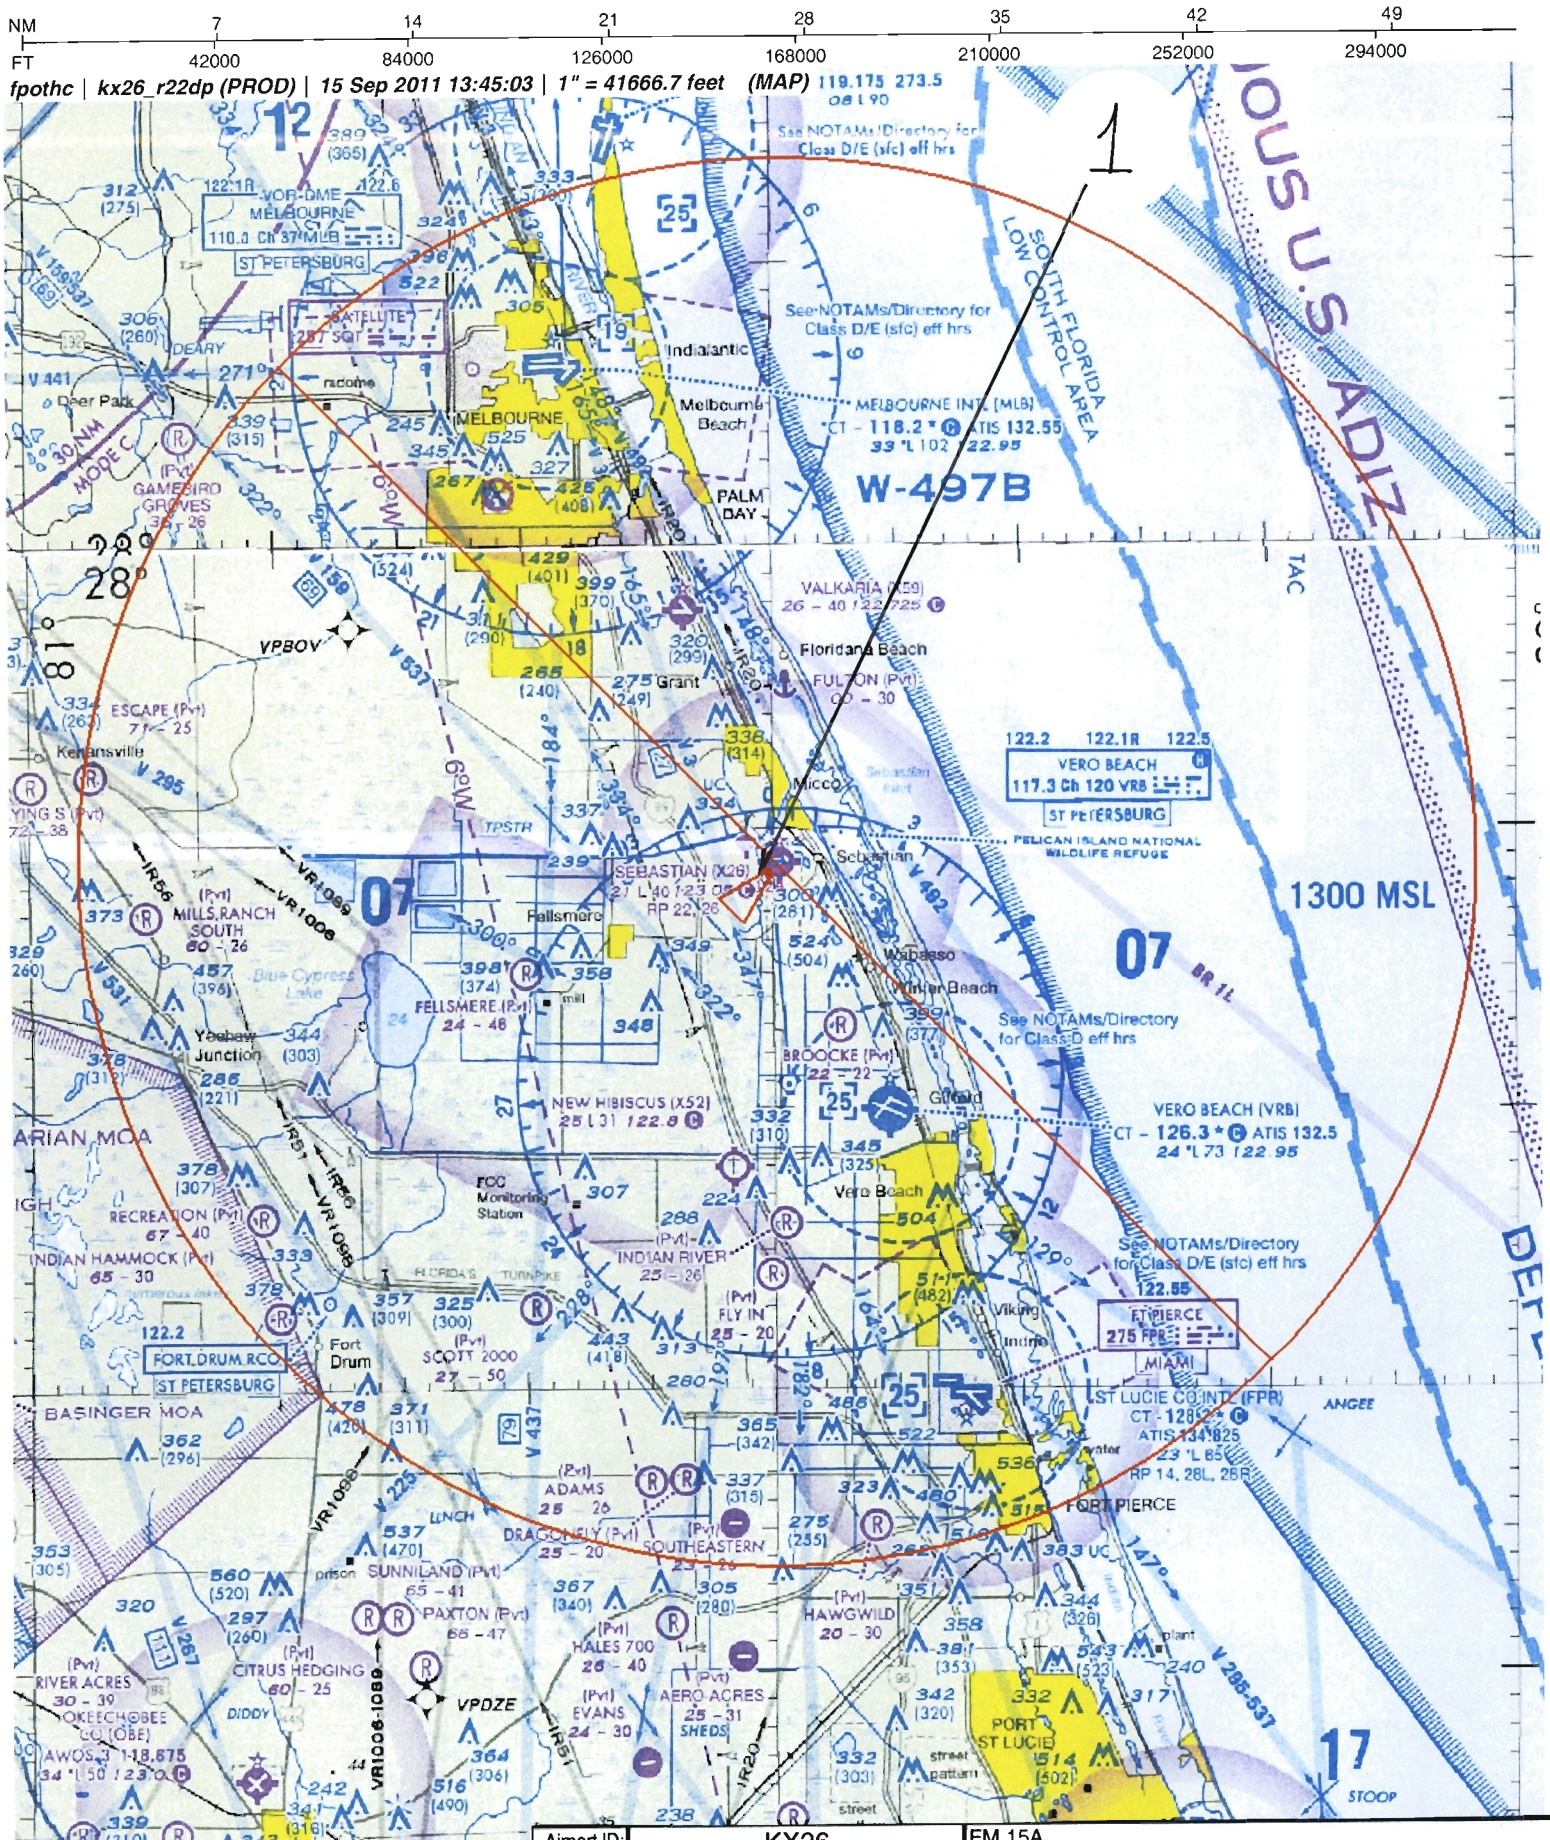FM 15A

| No | SEGMENT | OBSTRUCTION | ELEV |
|---|---|---|---|
| 1 | ICA | TREE | 125 |
| | | | |
| | | | |
| | | | |
| | | | |

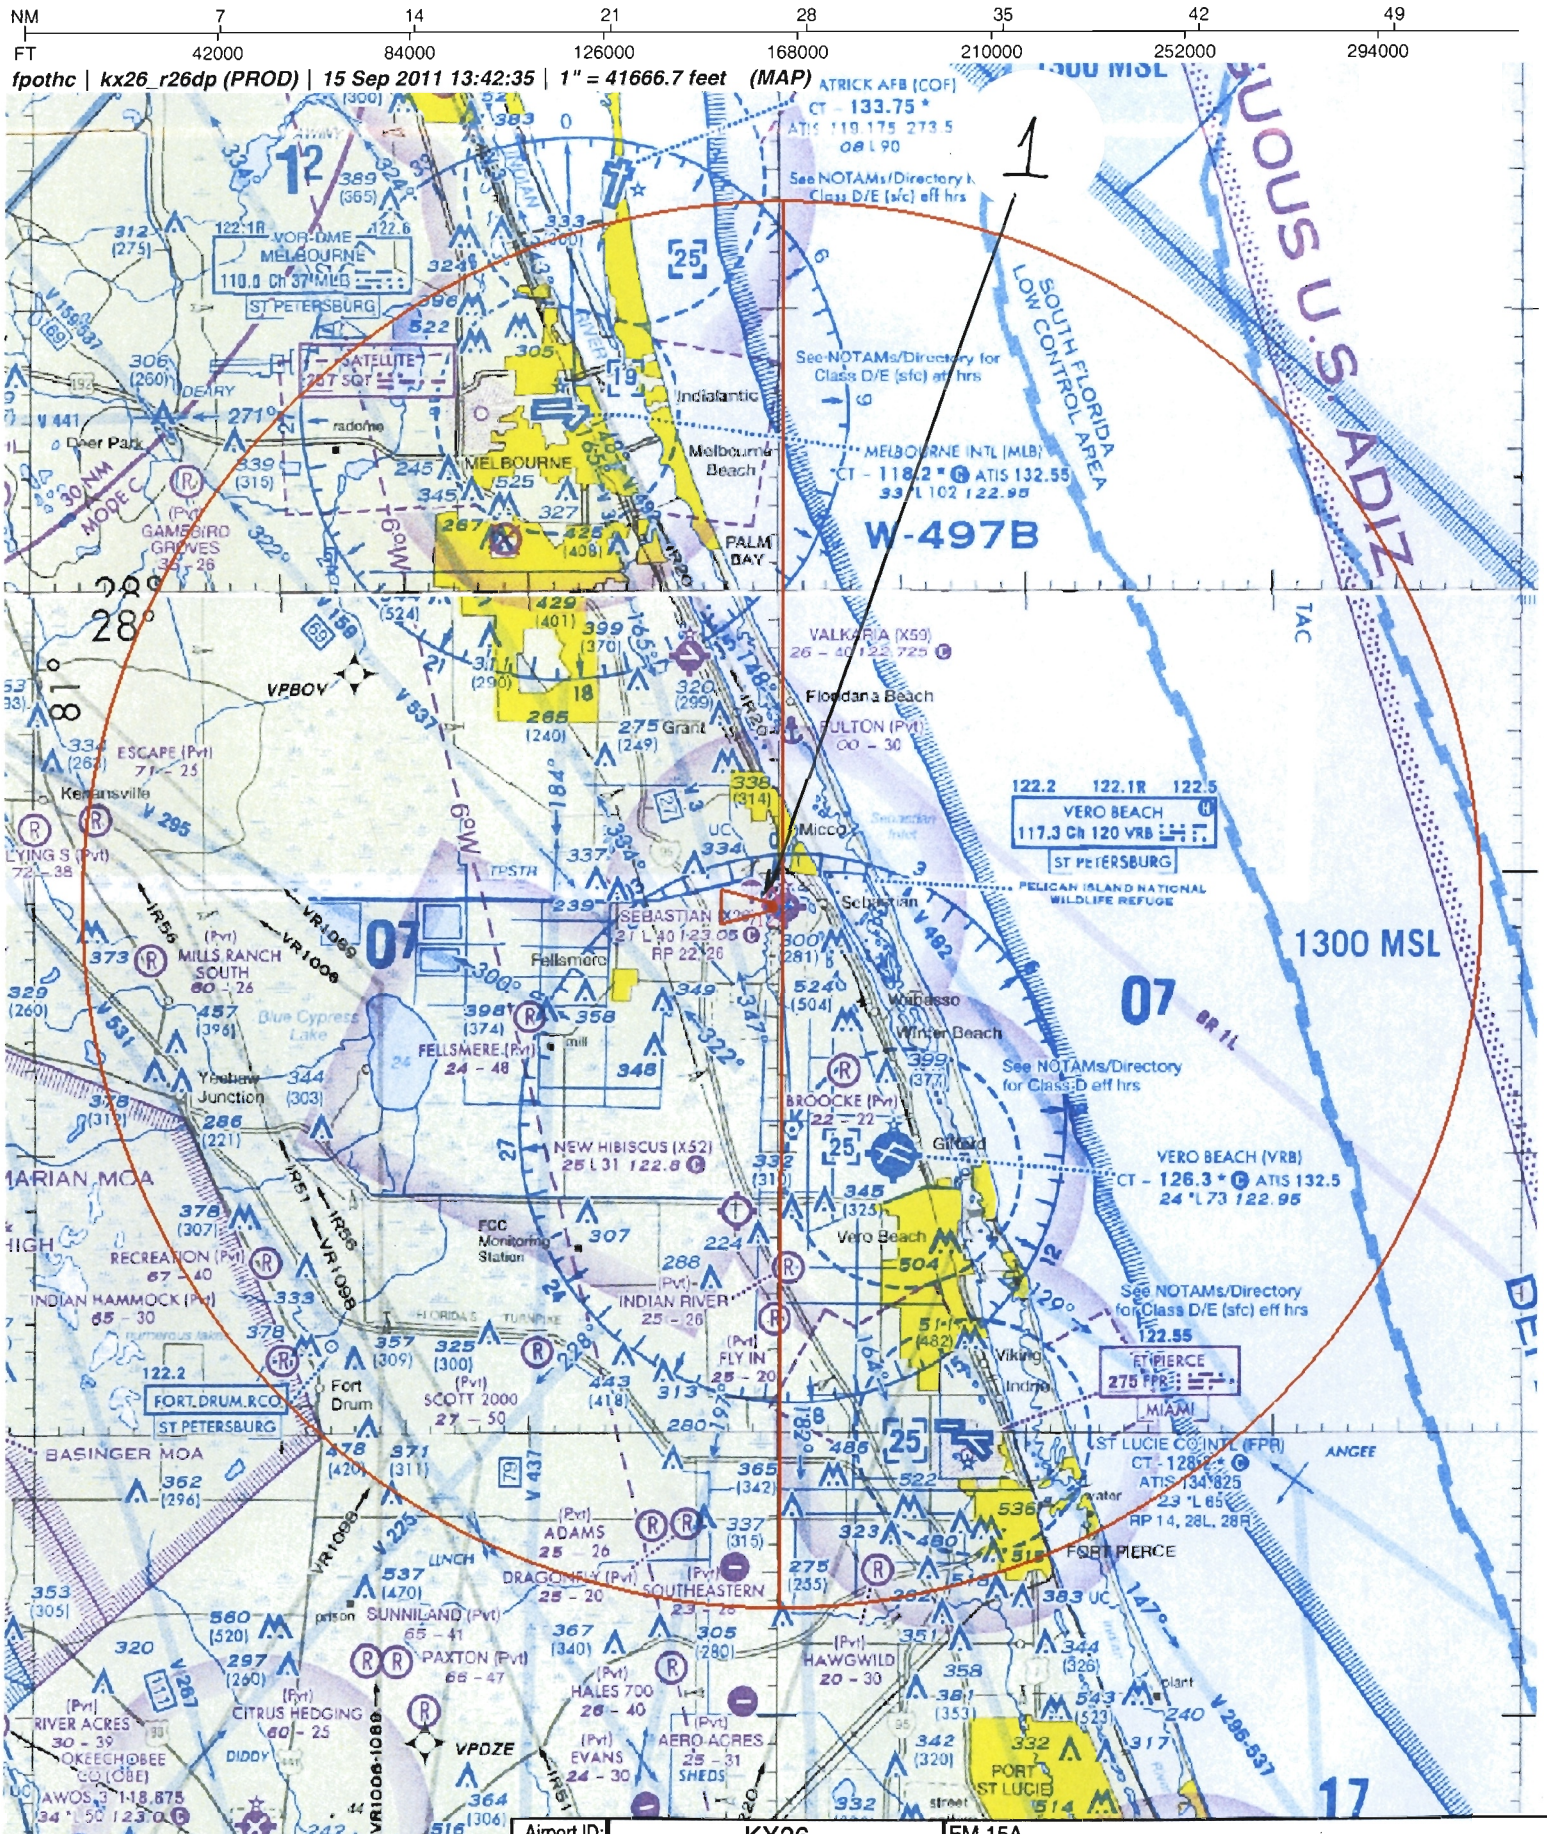

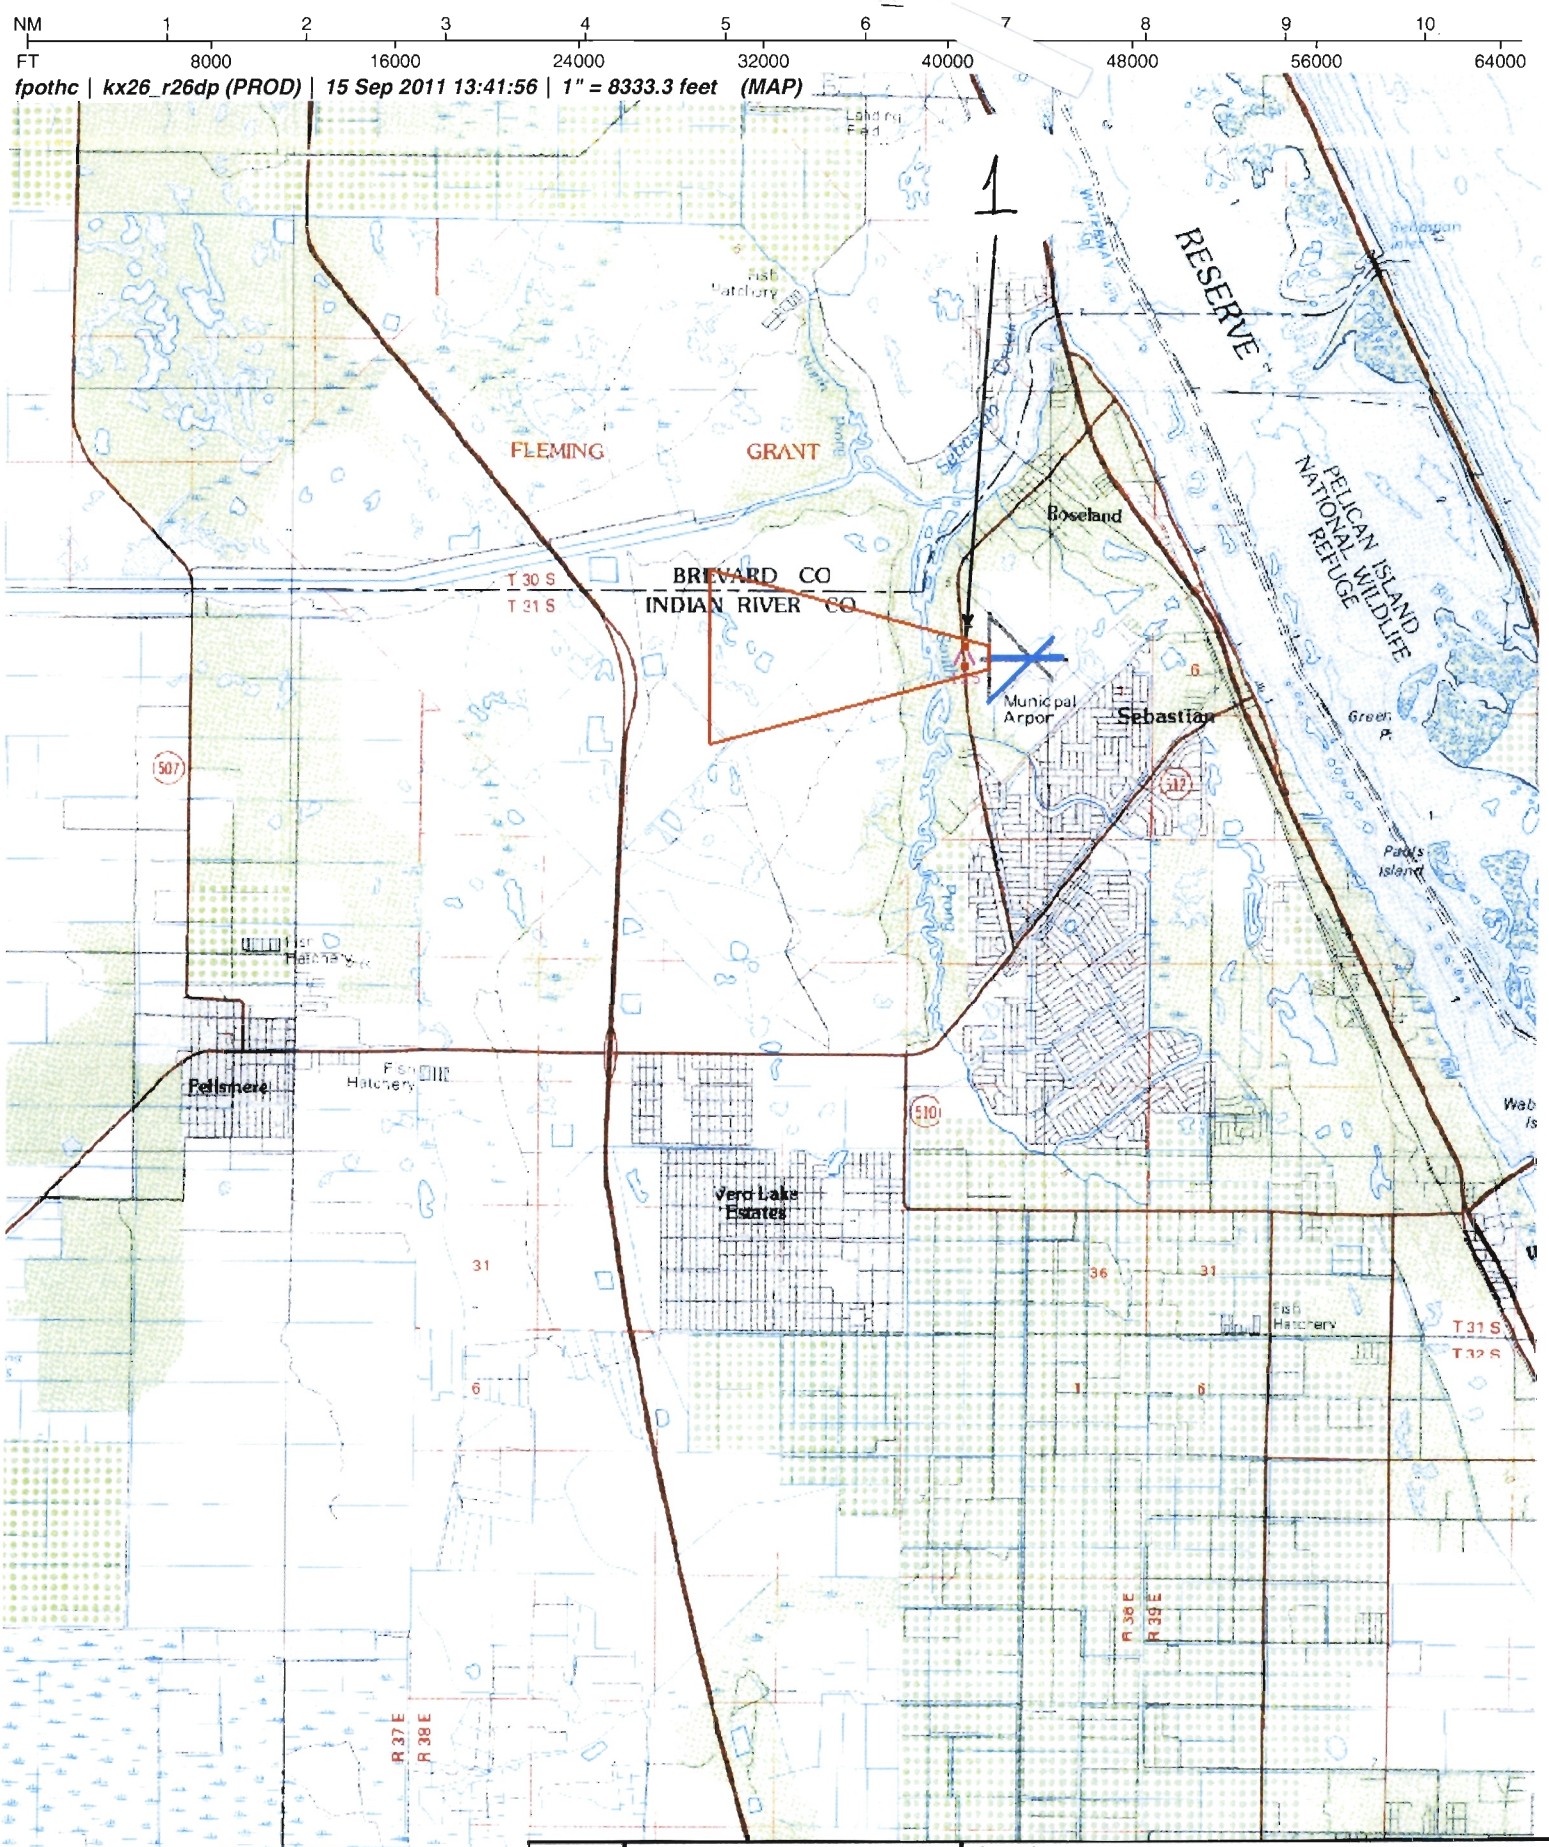
| Airport ID: | KX26 |
|---|---|
| Apt Name: | SEBASTIAN MUNI |
| City: | SEBASTIAN |
| State: | FL |
| Scale: | 1:100,000 |
| Proc ID: | DP RWY 22 |

FM 15A

| No | SEGMENT | OBSTRUCTION | ELEV |
|---|---|---|---|
| 1 | ICA | TREE | 124 |
| | | | |
| | | | |
| | | | |

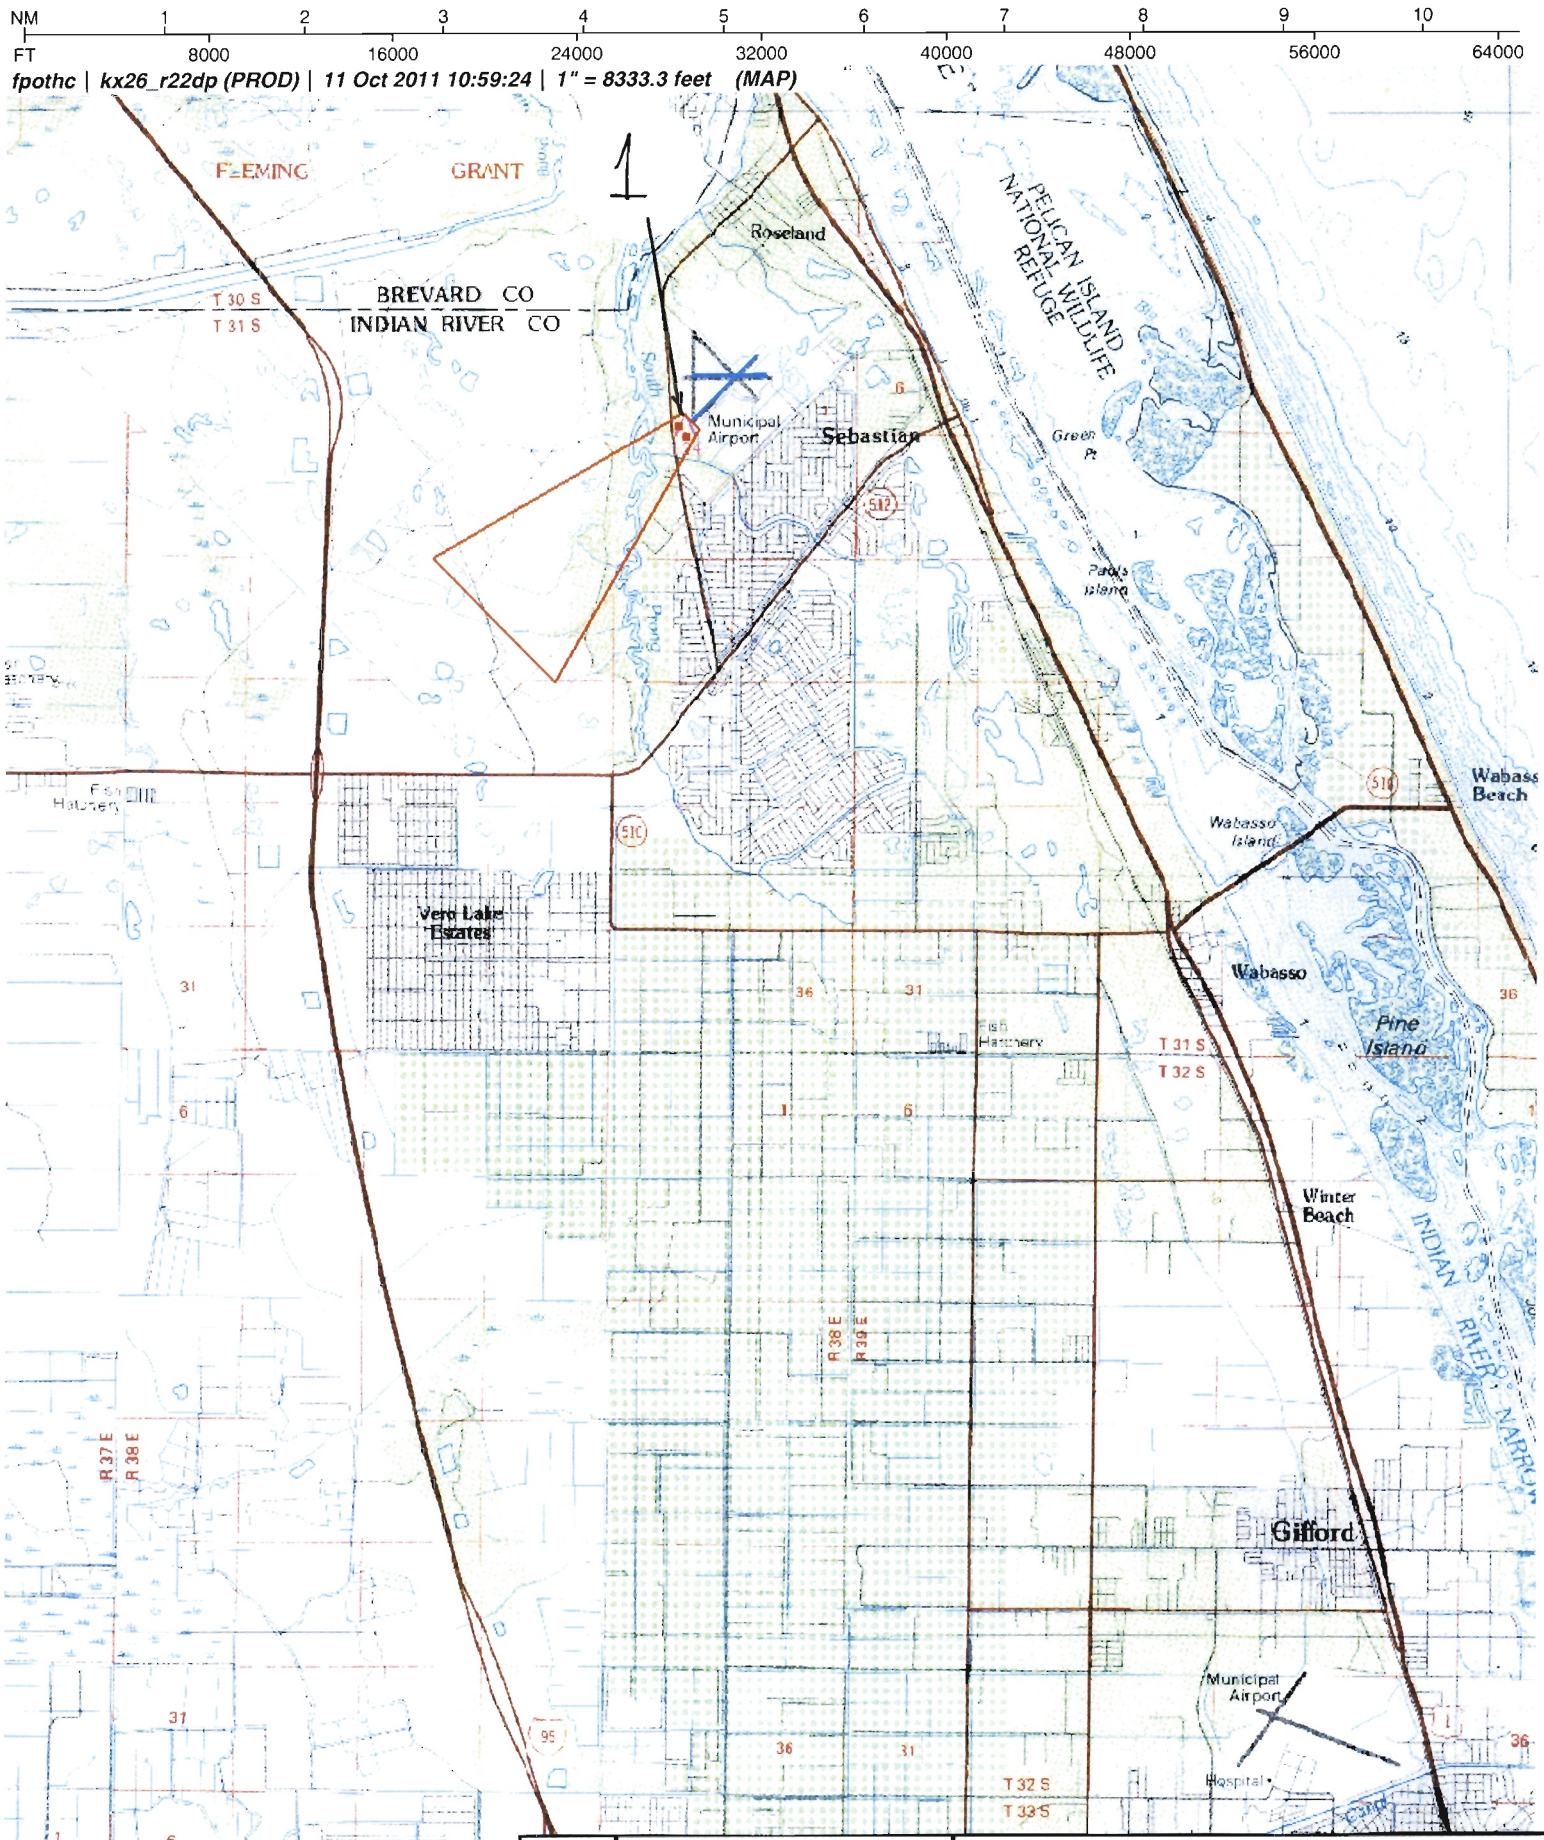


| | |
|---|---|
| Airport ID: | KX26 |
| Apt Name: | SEBASTIAN MUNI |
| City: | SEBASTIAN |
| State: | FL |
| Scale: | 1:100,000 |
| Proc ID: | DP RWY 8 |

FM 15A

| No | SEGMENT | OBSTRUCTION | ELEV |
|---|---|---|---|
| 1 | ICA: CG/CTA/CEIL/VIS | TOWER (12-004576) | 198 |

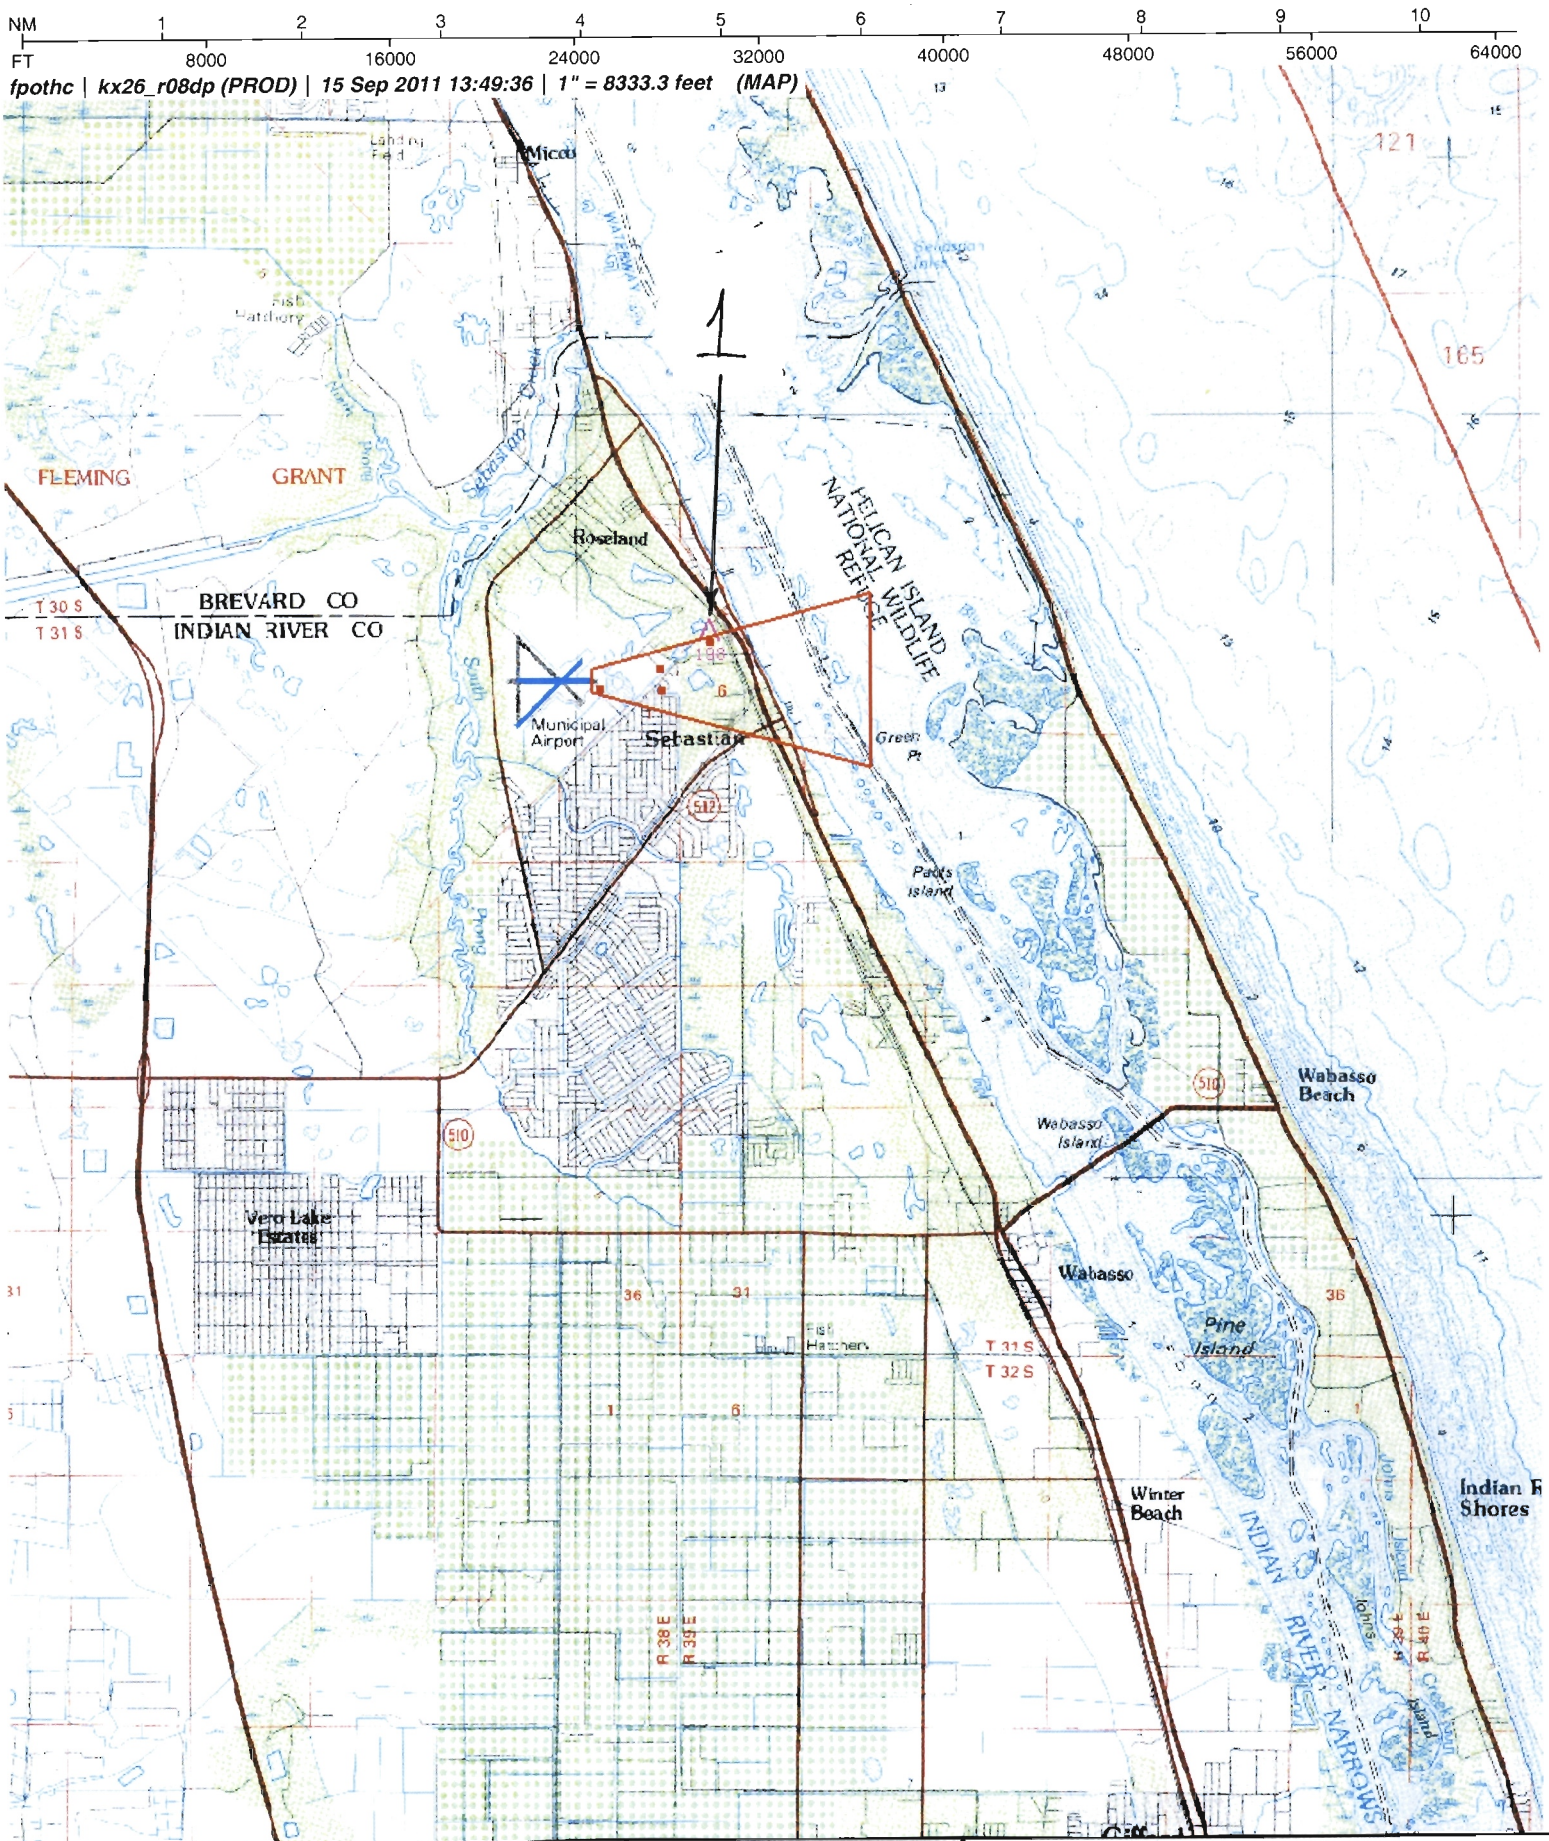


| | |
|---|---|
| Airport ID: | KX26 |
| Apt Name: | SEBASTIAN MUNI |
| City: | SEBASTIAN |
| State: | FL |
| Scale: | 1:100,000 |
| Proc ID: | DP RWY 4 |

FM 15A

| No | SEGMENT | OBSTRUCTION | ELEV |
|---|---|---|---|
| 1 | ICA | TREE | 125 |
| | | | |
| | | | |
| | | | |

U.S. DEPARTMENT OF TRANSPORTATION – FEDERAL AVIATION ADMINISTRATION
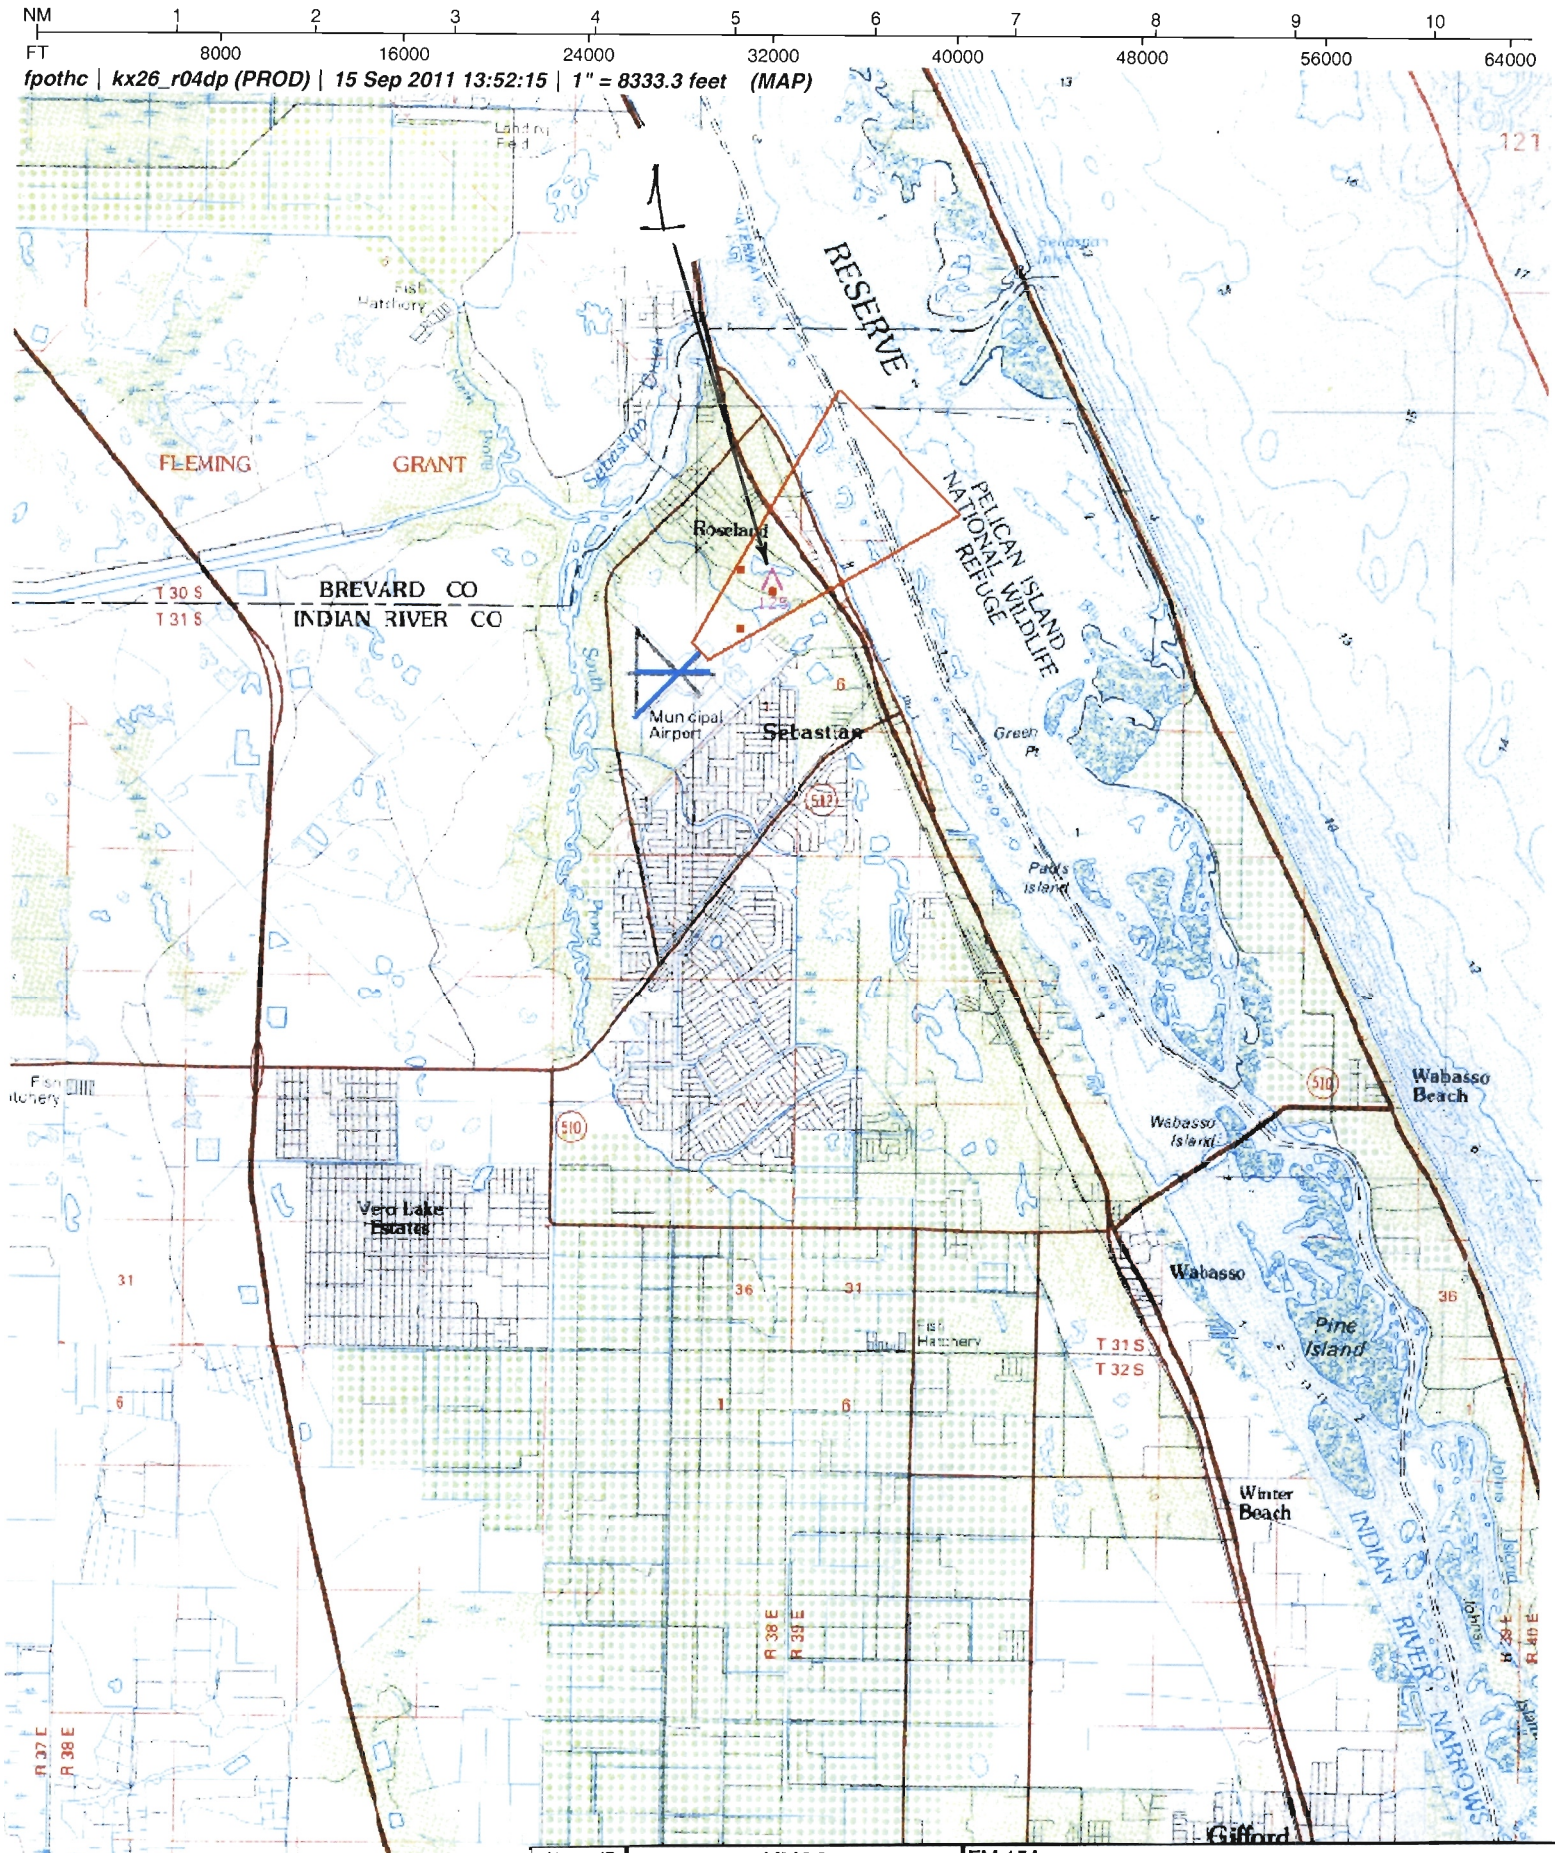
# TAKEOFF MINIMUMS AND OBSTACLE DEPARTURE PROCEDURES (ODP)

Bearings, headings, courses, tracks and radials are magnetic. Elevation and altitudes are in feet MSL. Altitudes are minimum altitudes unless otherwise indicated. Ceilings are in feet above airport elevation. Distances are in nautical miles. Visibilities are in statute miles or feet RVR unless otherwise indicated.

| City, State | Airport | Effective Date | Amdt. No. |
|---|---|---|---|
| SEBASTIAN, FL | SEBASTIAN MUNI | | ORIG |

## TAKEOFF MINIMUMS:

**RWY 4, 22, 26** – STANDARD.

**RWY 8** – 300-1 OR STANDARD WITH MINIMUM CLIMB OF 270 FT PER NM TO 300.

## TEXTUAL DEPARTURE PROCEDURES:

## TAKEOFF OBSTACLE NOTES:

**NOTE: RWY 4,** TREES BEGINNING 1902 FT FROM DER, 543 FT RIGHT OF CENTERLINE, UP TO 100 FT AGL/124 FT MSL. TREES BEGINNING 4060 FT FROM DER, 391 FT RIGHT OF CENTERLINE, UP TO 100 FT AGL/125 FT MSL. TREES BEGINNING 3702 FT FROM DER, 1281 FT LEFT OF CENTERLINE, UP TO 100 FT AGL/125 FT MSL.

**NOTE: RWY 8,** VEHICLES ON ROADWAY 388 FT FROM DER, ACROSS CENTERLINE, UP TO 15 FT AGL/40 FT MSL. TREES BEGINNING 2970 FT FROM DER, 534 FT LEFT OF CENTERLINE, UP TO 100 FT AGL/125 FT MSL. TREES BEGINNING 3047 FT FROM DER, 405 FT RIGHT OF CENTERLINE, UP TO 100 FT AGL/125 FT MSL. TOWER 5190 FT FROM DER, 1671 FT LEFT OF CENTERLINE, 173 FT AGL/198 FT MSL.

**NOTE: RWY 23,** TREES BEGINNING 570 FT FROM DER, 225 FT RIGHT OF CENTERLINE, UP TO 100 FT AGL/119 FT MSL. TREES BEGINNING 647 FT FROM DER, 354 FT LEFT OF CENTERLINE, UP TO 100 FT AGL/124 FT MSL.

**NOTE: RWY 27,** TREES BEGINNING 1035 FT FROM DER, 391 FT LEFT OF CENTERLINE, UP TO 100 FT AGL/125 FT MSL. TREES BEGINNING 1057 FT FROM DER, 515 FT RIGHT OF CENTERLINE, UP TO 100 FT AGL/119 FT MSL

## CONTROLLING OBSTACLES:

**RWY 9:** 198 FT MSL TOWER 274907.00N/0802827.00W.

QUALITY 2 CHECKED

# TAKEOFF MINIMUMS AND OBSTACLE DEPARTURE PROCEDURES (ODP)

Bearings, headings, courses, tracks and radials are magnetic. Elevation and altitudes are in feet MSL. Altitudes are minimum altitudes unless otherwise indicated.
Ceilings are in feet above airport elevation. Distances are in nautical miles. Visibilities are in statute miles or feet RVR unless otherwise indicated.

| City, State | Airport | Effective Date | Amdt. No. |
|---|---|---|---|
| SEBASTIAN, FL | SEBASTIAN MUNI | | ORIG |

**REMARKS:**

**FLIGHT INSPECTED BY:**

**REQUIRED EFFECTIVE DATE:**

ROUTINE

**DEVELOPED BY:**

DONALD SMITH (THERON CYRUS) AJV-352 09/12/2011

**APPROVED BY:**

DARRYEL ADAMS AJV-352

**COORDINATED WITH:**

AOPA, NBAA, MIA APP CON, MCO APP CON, ZMA, VRB ATCT, AMGR

**CHANGES:**

**REASONS:**

QUALITY 2 CHECKED
